

RESPONSE AND DEVELOPMENT WORK PLAN

AREA B: SUB-PARCEL B2-2
LOGISTICS CENTER X
TRADEPOINT ATLANTIC
SPARROWS POINT, MARYLAND

Prepared For:



ENVIROANALYTICS GROUP
1515 Des Peres Road, Suite 300
Saint Louis, Missouri 63131

Prepared By:



ARM GROUP LLC
9175 Guilford Road
Suite 310
Columbia, Maryland 21046

ARM Project No. 160443M-16

Respectfully Submitted,

A handwritten signature in black ink, appearing to read "Taylor R. Smith".

Taylor R. Smith, P.E.
Project Engineer

A handwritten signature in black ink, appearing to read "Neil Peters".

T. Neil Peters, P.E.
Senior Vice President

Revision 3 – March 18, 2020

TABLE OF CONTENTS

1.0	Introduction.....	1
2.0	Site Description and History.....	4
2.1.	Site Description.....	4
2.2.	Site History.....	4
3.0	Environmental Site Assessment Results.....	6
3.1.	Phase I Environmental Site Assessment Results.....	6
3.2.	Phase II Investigation Results.....	7
3.2.1.	Soil Investigation Findings.....	8
3.2.2.	Groundwater Investigation Findings.....	9
3.2.3.	NAPL Investigation Findings.....	10
3.3.	Human Health Screening Level Risk Assessment.....	11
3.3.1.	Analysis Process.....	11
3.3.2.	Sub-Parcel B2-2 SLRA Results and Risk Characterization.....	14
3.3.3.	Evaluation of Comprehensive Environmental Response, Compensation, and Liability Act (CERCLA) Criteria.....	17
4.0	Proposed Site Development Plan.....	21
4.1.	Response Phase – Well Abandonment.....	22
4.2.	Development Phase.....	22
4.2.1.	Erosion and Sediment Control Installation.....	22
4.2.2.	Grading and Site Preparation.....	23
4.2.3.	Installation of Structures and Underground Utilities.....	23
4.2.4.	Floor Slabs and Paving.....	24
4.2.5.	Landscaping.....	24
4.2.6.	Stormwater Management.....	24
5.0	Development Implementation Protocols.....	25
5.1.	Development Phase.....	25
5.1.1.	Erosion/Sediment Control.....	26
5.1.2.	Soil Excavation and Utility Trenching.....	26
5.1.3.	Soil Sampling and Disposal.....	28
5.1.4.	Fill.....	28
5.1.5.	Dust Control.....	29

TABLE OF CONTENTS (CONT.)

5.2.	Water Management	30
5.2.1.	Groundwater PAL Exceedances	30
5.2.2.	Dewatering	31
5.3.	Health and Safety	32
5.4.	Institutional Controls (Future Land Use Controls)	32
5.5.	Post Remediation Requirements	33
5.6.	Construction Oversight	33
6.0	Permits, Notifications and Contingencies.....	35
7.0	Implementation Schedule.....	36

FIGURES

Figure 1	Area A & B Parcels.....	Following Text
Figure 2	Sub-Parcel B2-2 (Logistics Center X) Development Area.....	Following Text
Figure 3	Soil Boring Locations	Following Text
Figure S1	SVOC Soil PAL Exceedances	Following Text
Figure S2	NAPL – TPH/Oil & Grease Soil PAL Exceedances	Following Text
Figure S3	Inorganic Soil PAL Exceedances	Following Text
Figure 4	Groundwater Sample Locations.....	Following Text
Figure GW1	VOC Groundwater PAL Exceedances	Following Text
Figure GW2	SVOC Groundwater PAL Exceedances	Following Text
Figure GW3	TPH/Oil & Grease Groundwater PAL Exceedances	Following Text
Figure GW4	Inorganic Groundwater PAL Exceedances	Following Text
Figure 5	Risk Assessment Exposure Units.....	Following Text
Figure 6	Groundwater Network Abandonment.....	Following Text

TABLES

Table 1	Summary of Organics Detected in Soil	Following Text
Table 2	Summary of Inorganics Detected in Soil	Following Text
Table 3	Summary of Organics Detected in Groundwater.....	Following Text
Table 4	Summary of Inorganics Detected in Groundwater	Following Text
Table 5	COPC Screening Analysis	Following Text
Table 6	Assessment of Lead	Following Text
Table 7	Soil Exposure Point Concentrations	Following Text
Table 8	Risk Ratios – Composite Worker Surface Soil.....	Following Text
Table 9	Risk Ratios – Composite Worker Sub-Surface Soil	Following Text
Table 10	Risk Ratios – Composite Worker Pooled Soil.....	Following Text

TABLE OF CONTENTS (CONT.)

Table 11	Risk Ratios – Construction Worker Surface Soil	Following Text
Table 12	Risk Ratios – Construction Worker Sub-Surface Soil.....	Following Text
Table 13	Risk Ratios – Construction Worker Pooled Soil.....	Following Text

APPENDICES

Appendix A	Request Letter from Tradepoint Atlantic	Following Text
Appendix B	Summary of Organics and Inorganics Detected in Soil (NAPL Screening Locations).....	Following Text
Appendix C	Select Soil Boring and Piezometer Logs	Following Text
Appendix D	Construction Worker SSLs – Calculation Spreadsheet	Following Text
Appendix E	Personal Protective Equipment Standard Operational Procedure.....	Following Text
Appendix F	Development Plan Drawings	Following Text
Appendix G	Capping Section Details.....	Following Text
Appendix H	Utility Trench Section Detail	Following Text
Appendix I	Utility Excavation NAPL Contingency Plan	Following Text
Appendix J	Health and Safety Plan.....	Following Text

ELECTRONIC ATTACHMENTS

Soil Laboratory Certificates of Analysis.....	Electronic Attachment
Soil Data Validation Reports	Electronic Attachment
Groundwater Laboratory Certificates of Analysis.....	Electronic Attachment
Groundwater Data Validation Reports.....	Electronic Attachment
ProUCL Input Tables (formatted soil analytical data).....	Electronic Attachment
ProUCL Output Tables	Electronic Attachment
Lead Evaluation Spreadsheet.....	Electronic Attachment

1.0 INTRODUCTION

ARM Group LLC (ARM), on behalf of EnviroAnalytics Group, LLC (EAG), has prepared this Response and Development Work Plan (RADWP) for a portion of the Tradepoint Atlantic property that has been designated as Area B: Sub-Parcel B2-2 (the Site). Tradepoint Atlantic submitted a letter (**Appendix A**) requesting an expedited remedial plan review to achieve construction deadlines for the proposed development on this Site. The proposed development of Sub-Parcel B2-2 will include permanent improvements on approximately 98.0 acres of land intended for occupancy in the central portion of Parcel B2 and northern portion of Parcel B5 (**Figure 1**). Outside of the main development area designated as Sub-Parcel B2-2, several easements with a total area of approximately 7.6 acres within the construction Limit of Disturbance (LOD) will be utilized to install stormwater and service utilities for the project. The utility installations within the easements are not covered by this RADWP because this work is not intended to be the basis for the issuance of a No Further Action Letter or a Certificate of Completion for the Sub-Parcel. The work to be completed outside of the Site boundary but within the easements is detailed under separate cover in a Limited Scope Project Plan (LSPP) as directed by the agencies.

The conduct of any environmental assessment and cleanup activities on the Tradepoint Atlantic property, as well as any associated development, is subject to the requirements outlined in the following agreements:

- Administrative Consent Order (ACO) between Tradepoint Atlantic (formerly Sparrows Point Terminal, LLC) and the Maryland Department of the Environment (MDE), effective September 12, 2014; and
- Settlement Agreement and Covenant Not to Sue (SA) between Tradepoint Atlantic (formerly Sparrows Point Terminal, LLC) and the United States Environmental Protection Agency (USEPA), effective November 25, 2014.

Sub-Parcel B2-2 is part of the acreage that was removed (Carveout Area) from inclusion in the Multimedia Consent Decree between Bethlehem Steel Corporation, the USEPA, and the MDE (effective October 8, 1997) as documented in correspondence received from USEPA on September 12, 2014. Based on this agreement, USEPA determined that no further investigation or corrective measures will be required under the terms of the Consent Decree for the Carveout Area. However, the SA reflects that the property within the Carveout Area will remain subject to the USEPA's Resource Conservation and Recovery Act (RCRA) Corrective Action authorities.

An application to enter the full Tradepoint Atlantic property (3,100 acres) into the Maryland Department of the Environment Voluntary Cleanup Program (MDE-VCP) was submitted to the MDE and delivered on June 27, 2014. The property's current and anticipated future use is Tier 3

(Industrial), and plans for the property include demolition and redevelopment over the next several years.

In consultation with the MDE, Tradepoint Atlantic affirms that it desires to accelerate the assessment, remediation and redevelopment of certain sub-parcels within the larger site due to current market conditions. To that end, the MDE and Tradepoint Atlantic agree that the Controlled Hazardous Substance (CHS) Act (Section 7-222 of the Environment Article) and the CHS Response Plan (Code of Maryland Regulations (COMAR) 26.14.02) shall serve as the governing statutory and regulatory authority for completing the development activities on the Sub-Parcel B2-2 and complement the statutory requirements of the Voluntary Cleanup Program (Section 7-501 of the Environment Article). Upon submission of a Site RADWP and completion of any remedial activities for the sub-parcel, the MDE shall issue a No Further Action Letter (NFA) upon a recordation of an environmental covenant describing any necessary land use controls for the specific sub-parcel. At such time that all the sub-parcels within the larger parcel have completed remedial activities, Tradepoint Atlantic shall submit to the MDE a request for issuing a Certificate of Completion (COC) as well as all pertinent information concerning completion of remedial activities conducted on the parcel. Once the VCP has completed its review of the submitted information it shall issue a COC for the entire parcel described in Tradepoint Atlantic's VCP application.

Alternatively, Tradepoint Atlantic or other entity may elect to submit an application for a specific sub-parcel and submit it to the VCP for review and acceptance. If the application is received after the cleanup and redevelopment activities described in this RADWP are implemented and a NFA is issued by the MDE pursuant to the CHS Act, the VCP shall prepare a No Further Requirements Determination for the sub-parcel.

If Tradepoint Atlantic or other entity has not carried out cleanup and redevelopment activities described in the RADWP, the cleanup and redevelopment activities may be conducted under the oversight authority of either the VCP or the CHS Act, so long as those activities comport with this RADWP.

The Sub-Parcel B2-2 Development Area (the Site) consists of approximately 98.0 acres of land slated for development and occupancy. The proposed development will include the construction of a warehouse building designated as Logistics Center X, along with exterior support areas (parking, access drives, etc.) and a paved extension to Tradepoint Avenue near the northeast corner of the warehouse. The proposed layout of the development area is shown on **Figure 2**. Outside of the main development area, several easements (with a total area of approximately 7.6 acres within the LOD) will be utilized to install subgrade utilities for the project. The temporary utility work is not intended to be the basis for the issuance of a NFA or a COC; therefore, the scope of utility work within the easements is not covered by this RADWP. The work to be completed within the easements is detailed under separate cover in a LSPP.

This RADWP provides a Site description and history; summary of environmental conditions identified by the Phase I Environmental Site Assessment (ESA); summary of relevant findings and environmental conditions identified by the Parcel B2 Phase II Investigation, Parcel B5 Phase II Investigation, and Area B Groundwater Investigation; a human health Screening Level Risk Assessment (SLRA) conducted for the identified conditions; and any necessary engineering and/or institutional controls to facilitate the planned development and address the impacts and potential human health exposures. These controls include work practices and applicable protocols that are submitted for approval to support the development and use of the Site. Engineering/institutional controls approved and installed for this RADWP shall be described in closure certification documentation submitted to the MDE demonstrating that exposure pathways on the Site are addressed in a manner that protects public health and the environment.

The remaining acreage of Parcel B2 and Parcel B5 will be addressed in future work associated with completion of the obligations of the ACO and associated VCP requirements. This work will include assessments of risk and, if necessary, RADWPs to address risks associated with future land use. Although easements extend into several additional parcels to facilitate the installation of stormwater and service utilities, the temporary utility work is not intended to be the basis for the issuance of a NFA or a COC, and the work within the easements will be implemented under a separate LSPP. These areas will also be covered by subsequent RADWPs, as necessary.

2.0 SITE DESCRIPTION AND HISTORY

2.1. SITE DESCRIPTION

Parcel B2 includes an area of 122.7 acres and Parcel B5 includes an area of 305 acres as shown on **Figure 1**. The Sub-Parcel B2-2 Development Area consists of approximately 98.0 acres intended for occupancy in the central portion of Parcel B2 and northern portion of Parcel B5 which will include a warehouse designated as Logistics Center X, along with exterior support areas (parking, access drives, etc.) and a paved extension to Tradepoint Avenue (**Figure 2**). Outside of the main development area designated as Sub-Parcel B2-2, several easements with a total area of approximately 7.6 acres within the construction LOD will be utilized to install stormwater and service utilities for the project. The temporary utility work is not intended to be the basis for the issuance of a NFA or a COC; therefore, the scope of utility work within the easements is not covered by this RADWP. The work to be completed within the easements is detailed under separate cover in a LSPP. The Site is currently zoned Manufacturing Heavy-Industrial Major (MH-IM), and is not occupied. All historical buildings have been demolished, and the Site has been cleared of all significant vegetation. There is no groundwater use on-site or within the surrounding Tradepoint Atlantic property.

Sub-Parcel B2-2 is at an average elevation of approximately 10 to 12 feet above mean sea level (amsl) over the majority of the Site. Elevations in the sub-parcel are fairly uniform, with no clear discharge direction for surface water drainage. According to Figure B-2 of the Stormwater Pollution Prevention Plan (SWPPP) Revision 6 dated February 22, 2018, stormwater from the northern portion of the Site is discharged through the permitted National Pollution Discharge Elimination System (NPDES) Outfalls 016 and 017 to the adjoining surface waters of Jones Creek and Old Road Bay. Stormwater from the southern portion of the Site is discharged through the Pennwood Canal and NPDES Outfall 001.

2.2. SITE HISTORY

From the late 1800s until 2012, the production and manufacturing of steel was conducted at Sparrows Point. Iron and steel production operations and processes at Sparrows Point included raw material handling, coke production, sinter production, iron production, steel production, and semi-finished and finished product preparation. In 1970, Sparrows Point was the largest steel facility in the United States, producing hot and cold rolled sheets, coated materials, pipes, plates, and rod and wire. The steel making operations at the facility ceased in fall 2012.

The proposed Sub-Parcel B2-2 Development Area occupies the central portion of Parcel B2 and northern portion of Parcel B5. These areas of the Tradepoint Atlantic property were formerly occupied by portions of the main steel making area and various support facilities. Parcel B2 contained the Steelside Electronics building and several small storage areas and shops. A large

portion of the western and central areas of Parcel B2 were occupied by railways installed in the former Sparrows Point Scrap Processing area, and the majority of the eastern-central areas of the parcel were occupied by a network of roadways and the former residential town that was occupied by mill workers. The portion of Parcel B5 covered by this RADWP was formerly occupied by the Blast Furnace Area, which included several iron and steel work processes. The blast furnaces were used for extracting iron from ore and other iron-rich recyclable materials. The furnaces received ore, sinter, coke, and limestone and/or dolomite, heated air, and fuel injectants (coal, oil, or natural gas) and produced a molten iron product and slag as a by-product. A small portion of the former residential town was also present within the northern portion of Parcel B5. More information regarding historical activities at the Site can be found in the agency-approved Phase II Investigation Work Plans for Parcel B2 (Revision 1 dated May 17, 2017) and Parcel B5 (Revision 1 dated December 3, 2015).

3.0 ENVIRONMENTAL SITE ASSESSMENT RESULTS

3.1. PHASE I ENVIRONMENTAL SITE ASSESSMENT RESULTS

A Phase I ESA was completed by Weaver Boos Consultants for the entire Sparrows Point property on May 19, 2014. Weaver Boos completed site visits of Sparrows Point from February 19 through 21, 2014, for the purpose of characterizing current conditions at the former steel plant. The Phase I ESA identified particular features across the Tradepoint Atlantic property which presented potential risks to the environment. These Recognized Environmental Conditions (RECs) included buildings and process areas where releases of hazardous substances and/or petroleum products potentially may have occurred. The Phase I ESA also relied upon findings identified during a previous visual site inspection (VSI) conducted as part of the RCRA Facility Assessment (RFA) prepared by A.T. Kearney, Inc. dated August 1993, for the purpose of identifying Solid Waste Management Units (SWMUs) and Areas of Concern (AOCs) on the property. This 1991 VSI is regularly cited in the Description of Current Conditions (DCC) Report prepared by Rust Environment and Infrastructure, dated January 1998 (included with Weaver Boos' Phase I ESA).

Weaver Boos' distinction of a REC or Non-REC was based upon the findings of the DCC Report (which was prepared when the features remained on-site in 1998) or on observations of the general area during their site visit. Weaver Boos made the determination to identify a feature as a REC based on historical information, observations during the site visit, and prior knowledge and experience with similar facilities. The following RECs were identified within, or in close proximity to, the Sub-Parcel B2-2 boundary:

Scrap Processing Facility and Bulk Petroleum Storage (REC 9C, Finding 239):

According to Freedom of Information Act (FOIA) documents provided by Baltimore County, a bulk petroleum storage area was located northwest of the former residential town in the rolling mills area. The types of petroleum products, storage area conditions, and conditions of the storage containers remain unknown. Therefore, the Phase I ESA concluded that there was the potential for a release to the environment in this area.

Residential Town Tanks (REC 21, Finding 271):

According to the Weaver Boos review of fire insurance maps, at least three buildings located in the Sparrows Point residential town were identified to have boiler rooms. Weaver Boos noted that boiler rooms are often supplied fuel oil from tanks located within or along the exterior of the building. There is no further information on these tanks currently available regarding their locations (UST or AST), contents, use, removal, or spill/leak history.

Relevant SWMUs and AOCs were also identified as located in Figure 3-1 from the DCC Report. This figure generally shows the SWMUs, AOCs, and main facility areas within the property

boundaries. The following SWMUs and AOCs were identified within, or in close proximity to, the Sub-Parcel B2-2 boundary:

L Furnace Slag Piles (SWMU 165):

The DCC Report identifies slag piles which collected slag generated as a by-product of the iron making process. After cooling, the slag was crushed and evaluated for reuse. These piles were designated as units managing non-hazardous waste.

Former Diesel Fuel UST Area (HREC, Finding 236, AOC Q):

The Phase I ESA included information regarding a steel 1,000-gallon No. 2 fuel oil tank that was removed on December 6, 1989 from near the eastern end of Slab Haul Road. During removal, corrosion pitting was observed on the outer tank surface, but soil BTEX concentrations were at or below minimum detectable levels. Contaminated soil was removed and the remediation was approved by the MDE.

3.2. PHASE II INVESTIGATION RESULTS

Phase II Investigations specific to soil and groundwater conditions were performed for the areas covering Sub-Parcel B2-2 in accordance with the requirements outlined in the ACO as further described in the following agency-approved Phase II Investigation Work Plans:

- Area B: Parcel B2 (Revision 1) dated May 17, 2017; and subsequent comment response letter dated June 14, 2017.
- Area B: Parcel B5 (Revision 1) dated December 3, 2015.
- Area B Groundwater Investigation (Revision 3) dated October 6, 2015.

All soil and groundwater samples were collected and analyzed in accordance with agency-approved protocols during these Phase II Investigations, the specific details of which can be reviewed in each agency-approved Work Plan. Each Phase II Investigation was developed to target specific features which represented a potential release of hazardous substances and/or petroleum products to the environment, including RECs, SWMUs, and AOCs as well as numerous other targets defined from former operations that would have the potential for environmental contamination. Samples were also collected at site-wide locations to ensure full coverage of each investigation area. The full analytical results and conclusions of each investigation have been presented to the agencies in the following Phase II Investigation Reports:

- Area B: Parcel B2 (Revision 2) dated October 12, 2018.
- Area B: Parcel B5 (Revision 3) dated July 8, 2019.
- Area B Groundwater Investigation (Revision 0) dated September 30, 2016.

This RADWP summarizes the relevant soil and groundwater findings from these Phase II Investigations with respect to the proposed development of Sub-Parcel B2-2.

3.2.1. Soil Investigation Findings

Based on the scope of development for Sub-Parcel B2-2 (98.0 acres), 79 soil samples collected from 40 boring locations during the various Phase II Investigations listed in the preceding section were selected for this evaluation of Sub-Parcel B2-2. The 40 boring locations are shown on **Figure 3**, and the samples obtained from these borings provided analytical data for discussion of on-site conditions. The identified borings are located within the proposed development area such that the data from these borings should be considered representative of potential exposures during construction within Sub-Parcel B2-2.

Soil samples collected during the various Phase II Investigations were analyzed for the USEPA Target Compound List (TCL) semi-volatile organic compounds (SVOCs), TCL volatile organic compounds (VOCs), total petroleum hydrocarbon (TPH) diesel range organics (DRO) and gasoline range organics (GRO), Oil & Grease, USEPA Target Analyte List (TAL) metals, hexavalent chromium, and/or cyanide based on the parcel-specific sampling plans for Parcels B2 and B5. Shallow soil samples (0 to 1 foot bgs) were also analyzed for polychlorinated biphenyls (PCBs). The specific requirements for parameter analyses have varied over time, and can be reviewed in each agency-approved Work Plan. The laboratory Certificates of Analysis (including Chains of Custody) and relevant Data Validation Reports (50+% validated soil data) are included as electronic attachments. The Data Validation Reports contain qualifier keys for the flags assigned to individual results in the attached summary tables.

Soil sample results relevant for the Sub-Parcel B2-2 Development Area were screened against the Project Action Limits (PALs) established in the property-wide Quality Assurance Project Plan (QAPP) dated April 5, 2016, or based on other direct agency guidance (e.g., TPH/Oil & Grease). **Table 1** and **Table 2** provide a summary of the detected organic compounds and inorganics in the soil samples collected from the 40 soil borings that are most relevant for evaluating soil conditions at the Site. **Figure S1** through **Figure S3** present summaries of the soil sample results that exceeded the PALs among these 40 soil borings. The PALs for relevant polynuclear aromatic hydrocarbons (PAHs) have been adjusted upward based on revised toxicity data published in the USEPA Regional Screening Level (RSL) Composite Worker Soil Table. PAL exceedances in the soil samples relevant for the proposed development project were limited to five inorganics (arsenic, manganese, lead, thallium, and hexavalent chromium), two SVOCs (benzo[a]pyrene and naphthalene), and Oil & Grease.

An additional 20 soil borings outside the development area were included as secondary locations to evaluate the potential presence of non-aqueous phase liquid (NAPL) in close proximity to the Site. These 20 soil borings are highlighted on **Figure 3**. The purpose of these additional soil borings was to provide a conservative screening for the potential presence of NAPL at the Site,

which could be indicated through the presence of free product, sheen, or elevated concentrations of TPH-DRO/GRO and/or Oil & Grease. These 20 soil borings have been included solely for NAPL screening purposes, and the analytical data obtained from these borings is not included in the main detection summary tables (**Table 1** and **Table 2**) because a sufficient soil dataset is already available within the Site boundary and along the easements. **Appendix B** provides summary tables for the organic compounds and inorganics detected in the 20 soil borings that were completed within the conservative NAPL screening buffer. These analytical detections are provided for reference.

Sample B2-024-SB-1 was the only sample evaluated in this RADWP that exceeded the PAL for TPH/Oil & Grease (6,200 mg/kg). Potential evidence of NAPL was also observed at several soil boring locations. These findings are further discussed in Section 3.2.3, and contingency measures to address the potential presence of NAPL which could be encountered during construction are addressed in subsequent sections of this RADWP.

3.2.2. Groundwater Investigation Findings

Groundwater conditions were investigated in accordance with the separate Area B Groundwater Investigation Work Plan. During this groundwater investigation, nine shallow permanent wells were sampled within a reasonable proximity to Sub-Parcel B2-2. In addition, one supplemental sample was obtained from temporary groundwater point B2-051-PZ, as discussed in the Parcel B2 Phase II Investigation Report. The 10 shallow groundwater points which provided relevant analytical data for the proposed development project are shown on **Figure 4**. Groundwater conditions below the Site are not a significant concern because there is no use of groundwater on the Tradepoint Atlantic property; however, groundwater may be encountered in the sub-parcel during some construction tasks.

The shallow groundwater samples were analyzed for TCL-SVOCs, TLC-VOCs, TAL-dissolved/total metals, TPH-DRO/GRO, Oil & Grease, hexavalent chromium, and/or total cyanide based on the project-specific sampling methods. The laboratory Certificates of Analysis (including Chains of Custody) and relevant Data Validation Reports (50+% validated groundwater data) are included as electronic attachments. The Data Validation Reports contain qualifier keys for the flags assigned to individual results in the attached summary tables.

The groundwater results relevant for the Sub-Parcel B2-2 Development Area were screened against the PALs established in the property-wide QAPP dated April 5, 2016, or based on other direct agency guidance (e.g., TPH/Oil & Grease). **Table 3** and **Table 4** provide a summary of the detected organic compounds and inorganics in the groundwater samples submitted for laboratory analysis, and **Figure GW1** through **Figure GW4** present summaries of the groundwater results that exceeded the PALs. The tables and figures include all locations and analytical data relevant for the proposed development project. Similar to the evaluation of soil data, the PALs for relevant PAHs have been adjusted upward based on revised toxicity data

published in the USEPA RSL Resident Tapwater Table. Groundwater PAL exceedances in the vicinity of the proposed development project consisted of three VOCs (benzene, chloroform, and methyl tert-butyl ether), three SVOCs (benz[a]anthracene, naphthalene, and pentachlorophenol), DRO, and five total/dissolved metals (beryllium, cobalt, iron, manganese, and vanadium). For simplicity, the inorganic PAL exceedances shown on **Figure GW4** do not include duplicate exceedances of total/dissolved metals. If both total and dissolved concentrations exceeded the PAL, the values for the total metals is displayed.

While concentrations of these constituents did exceed the aqueous PALs specified in the QAPP, none of the detected levels were significantly elevated and there were no concerns related to potential vapor intrusion (VI) risks. Total cyanide had previously been identified as a potential VI risk in the Area B Groundwater Phase II Investigation Report, but the screening level for cyanide has since been adjusted upward by the USEPA, eliminating this concern. Each groundwater collection point was also inspected for evidence of NAPL using an oil-water interface probe prior to sampling. None of the piezometers or permanent wells relevant for the proposed development project showed evidence of NAPL during these checks. If groundwater is encountered during development, it will be managed to prevent exposures in accordance with the dewatering requirements outlined in Section 5.2.

3.2.3. NAPL Investigation Findings

Soil borings that had visual observations of NAPL (free product or sheen), strong non-visual evidence of NAPL, and/or elevated concentrations of TPH/Oil & Grease have been identified on **Figure S2** and are evaluated herein. A temporary NAPL screening piezometer was installed at each identified soil boring to investigate the potential presence and mobility of NAPL in groundwater at these locations. The soil boring logs and piezometer construction logs have been included as **Appendix C**. Each location is further discussed in its respective Phase II Investigation Report, but the specific findings at each location can be summarized as follows:

- Soil boring B2-024-SB (located within the development boundary under the future building footprint) exhibited an elevated concentration of 12,400 mg/kg of Oil & Grease in the shallow soil sample (0 to 1 foot interval) collected at this location. No physical evidence of NAPL was observed within the soil core at this location. Due to the elevated analytical detection, and a lack of underlying soil data, a temporary piezometer was installed at this location. Based on 0-hour, 48-hour, and 30-day gauging measurements, NAPL was not detected at this location.
- Soil boring B2-051-SB (located within the development boundary outside of the future building footprint) had observations of trace to light NAPL in the soil core. Based on these observations, a temporary piezometer was installed at this location. Due to its presence in an area subject to high traffic volumes, Tradepoint Atlantic requested the early abandonment of B2-051-PZ; however, NAPL was not detected during the 0-hour or

48-hour checks, and no visible product was noted in or on the PVC casing when the piezometer was withdrawn from the ground. A groundwater sample was collected from this location prior to abandonment to further evaluate the potential presence of dissolved-phase contamination, with the results included herein.

- Soil borings B2-053-SB and B2-055-SB in the former Mason’s Garage Area (located outside of the development boundary but in close proximity) exhibited strong non-visual observations of potential product, including strong fuel-type odors and elevated PID readings. Due to these observations, and based on the historical use of the area, a temporary piezometer was installed at each location. Based on 0-hour, 48-hour, and 30-day gauging measurements of both screening piezometers, NAPL was not detected at these locations.
- Soil boring B5-097-SB (located outside of the development boundary but in close proximity) had visual observations of NAPL in the soil core. Due to these observations, a temporary piezometer was installed at this location. Based on 0-hour, 48-hour, and 30-day gauging measurements, NAPL was not detected at this location.

3.3. HUMAN HEALTH SCREENING LEVEL RISK ASSESSMENT

3.3.1. Analysis Process

A human health Screening Level Risk Assessment (SLRA) has been completed based on the analytical data obtained from the characterization of surface and subsurface soils in Sub-Parcel B2-2. The site-specific Composite Worker and Construction Worker SLRA includes only data obtained within the Site boundary (intended for future occupancy).

Although the Composite Worker SLRA based on the existing baseline conditions does not indicate unacceptable risks at the Site, Sub-Parcel B2-2 will be subject to surface engineering controls (environmental capping), along with institutional controls, due to the proposed use of processed slag aggregate as structural fill. The SLRA included the following evaluation process:

Identification of Exposure Units (EUs): The Composite Worker and Construction Worker SLRA evaluated two Exposure Units (EU1 and EU2) with areas of 34.5 acres and 63.5 acres, respectively. EU1 and EU2 correspond to the area inside of the footprint of the proposed future warehouse, and the area outside of the warehouse, respectively. The SLRA EUs are shown in relation to the 40 applicable soil borings on **Figure 5**. Three additional soil borings which did not provide analytical data for the SLRA (B2-053-SB, B2-055-SB, and B5-097-SB) are shown for NAPL screening purposes only, as described in Section 3.2.1.

Identification of Constituents of Potential Concern (COPCs): For the project-specific SLRA, compounds that were present at concentrations at or above the USEPA RSLs set at a target cancer risk of $1E-6$ or target non-cancer Hazard Quotient (HQ) of 0.1 were identified as COPCs to be included in the SLRA. A COPC screening analysis is provided in **Table 5** to identify compounds above the relevant screening levels.

The results for thallium were eliminated from the risk assessment because this compound was very infrequently detected in the dataset for Sub-Parcel B2-2. Thallium was only detected in 3.0% of the samples analyzed for this compound (2 samples out of 67). If the detection frequency of a COPC is less than 5% in a dataset with a minimum of 20 samples, the COPC can be eliminated from the risk analysis assuming the detections are not extremely high (based on agency discretion). A single detection that is extremely high could require delineation rather than elimination. In this case it is reasonable to remove thallium from the risk assessment based on the relatively low concentrations detected. All remaining COPCs identified in **Table 5** have been retained for the risk assessment.

Exposure Point Concentrations (EPCs): The COPC soil datasets for each EU were divided into surface (0 to 1 foot), subsurface (>1 foot), and pooled depths for estimation of potential EPCs. Thus, there are three soil datasets associated with each EU. A statistical analysis was performed for each COPC dataset using the ProUCL software (version 5.0) developed by the USEPA to determine representative reasonable maximum exposure (RME) values for the EPC for each constituent. The RME value is typically the 95% Upper Confidence Limit (UCL) of the mean. For lead, the arithmetic mean for each depth was calculated for comparison to the Adult Lead Model (ALM)-based values, and any individual results exceeding 10,000 mg/kg would be delineated for possible excavation and removal (if applicable). For PCBs, all results equaling or exceeding 50 mg/kg would be delineated for excavation and removal (if applicable).

Risk Ratios: The surface soil EPCs, subsurface soil EPCs, and pooled soil EPCs were compared to the USEPA RSLs for the Composite Worker and to site-specific Soil Screening Levels (SSLs) for the Construction Worker based on equations derived in the USEPA Supplemental Guidance for Developing Soil Screening Levels for Superfund Sites (OSWER 9355.4-24, December 2002). Risk ratios were calculated with a cancer risk of $1E-6$ and a non-cancer HQ of 1. The risk ratios for the carcinogens were summed to develop a screening level estimate of the baseline cumulative cancer risk. The risk ratios for the non-carcinogens were segregated and summed by target organ to develop a screening level estimate of the baseline cumulative non-cancer hazard.

For the Construction Worker, site-specific risk-based evaluations were completed for a range of potential exposure frequencies to determine the maximum exposure frequency

for each EU that would result in risk ratios equivalent to a cumulative cancer risk of $1E-5$ or Hazard Index (HI) of 1 for the individual target organs. This analysis indicated that the allowable exposure frequencies before additional worker protections or more detailed job safety evaluations might be needed are 95 days and 55 days for EU1 and EU2, respectively.

There is no potential for human exposure to groundwater for a Composite Worker since groundwater is not used on the Tradepoint Atlantic property (and is not proposed to be utilized). In the event that construction/excavation leads to a potential Construction Worker exposure to groundwater during development, health and safety plans and management procedures shall be followed to limit exposure risk.

Assessment of Lead: For lead, the arithmetic mean concentrations for surface soils, subsurface soils, and pooled soils for each EU were compared to the applicable RSL (800 mg/kg) as an initial screening. If the mean concentrations for the EU were below the applicable RSL, the EU was identified as requiring no further action for lead. If a mean concentration exceeded the RSL, the mean values were compared to calculated ALM values (ALM Version dated 6/21/2009 updated with the 5/17/2017 OLEM Directive) with inputs of 1.8 for the geometric standard deviation and a blood baseline lead level of 0.6 ug/dL. The ALM calculation generates a soil lead concentration of 2,518 mg/kg, which is the most conservative (i.e., lowest) concentration which would yield a probability of 5% of a blood lead concentration of 10 ug/dL. If the arithmetic mean concentrations for the EU were below 2,518 mg/kg, the EU was identified as requiring no further action for lead. The lead averages and ALM screening levels are presented for surface, subsurface, and pooled soils in **Table 6**. For lead, any results equaling or exceeding 10,000 mg/kg would warrant additional delineation for possible excavation and removal (if applicable).

Assessment of TPH-DRO/GRO and Oil & Grease: EPCs were not calculated for TPH-DRO/GRO or Oil & Grease. Instead, the individual results were compared to the PAL set to a HQ of 1 (6,200 mg/kg). One soil sample exceeded the PAL for Oil & Grease: B2-024-SB-1 with a concentration of 12,400 mg/kg. Potential evidence of NAPL was also observed at several soil boring locations. These findings are further discussed in Section 3.2.3. The borings with physical evidence of NAPL or elevated Oil & Grease concentrations are plotted with respect to the proposed development plan on **Figure 5**. Contingency measures to address the potential presence of NAPL which could be encountered during construction are addressed in subsequent sections of this RADWP.

Risk Characterization Approach: Generally, if the baseline risk ratio for each non-carcinogenic COPC or cumulative target organ does not exceed 1 (with the exception of lead), and the sum of the risk ratios for the carcinogenic COPCs does not exceed a

cumulative cancer risk of $1E-5$, then a no further action determination will be recommended. If the baseline estimate of cumulative cancer risk exceeds $1E-5$ but is less than or equal to $1E-4$, then capping of the EU will be considered to be an acceptable remedy for the Composite Worker. For the Construction Worker, cumulative cancer risks exceeding $1E-5$, but less than or equal to $1E-4$, will be mitigated via site-specific health and safety requirements. The efficacy of capping for elevated non-cancer hazard will be evaluated in terms of the magnitude of exceedance and other factors such as bioavailability of the COPC.

Due to the major grading activities, including cut and fill, planned at the Site (covered by the Logistics Centers Grading Plan for Area B: Sub-Parcel B2-2 dated July 3, 2018; which was developed for preparatory grading work associated with the project), the SLRA was evaluated to determine baseline Composite and Construction Worker exposures to surface, subsurface, and pooled data. It should be noted that processed slag aggregate sourced from the Tradepoint Atlantic property will be used as the primary fill material for this project; therefore, regardless of the findings of the Composite Worker baseline assessment, Sub-Parcel B2-2 will be subject to surface engineering controls (i.e., capping) unless separate approvals are received from the MDE following appropriate laboratory testing of the slag aggregate material. The goal of the SLRA is therefore to determine whether additional response actions beyond capping may be needed due to current conditions at the Site.

The USEPA's acceptable risk range is between $1E-6$ and $1E-4$. If the sum of the risk ratios for carcinogens exceeds a cumulative cancer risk of $1E-4$, further analysis of site conditions will be required including the consideration of toxicity reduction in any proposal for a remedy. The magnitude of any non-carcinogen HI exceedances and bioavailability of the COPC will also dictate further analysis of site conditions including consideration of toxicity reduction in any proposal for a remedy. For lead, if the ALM results indicate that the mean concentrations would present a 5% to 10% probability of a blood concentration of 10 ug/dL for the EU, then capping of the EU would be an acceptable presumptive remedy. The mean soil lead concentrations corresponding to ALM probabilities of 5% and 10% are 2,518 mg/kg, and 3,216 mg/kg, respectively. If the ALM indicates that the mean concentrations would present a >10% probability of a blood concentration of 10 ug/dL for the EU, further analysis of site conditions including toxicity reduction will be completed such that the probability would be reduced to less than 10% after toxicity reduction, but before capping.

3.3.2. Sub-Parcel B2-2 SLRA Results and Risk Characterization

Soil data were divided into three datasets (surface, subsurface, and pooled) for Sub-Parcel B2-2 to evaluate potential exposure scenarios. Due to the major grading activities, including cut and

fill, planned at the Site (covered by the Logistics Centers Grading Plan dated July 3, 2018), each of these potential exposure scenarios is relevant for both the Composite and Construction Worker.

EPCs were calculated for each soil exposure dataset (i.e., surface, subsurface, and pooled surface/subsurface) in each EU. ProUCL output tables (with computed UCLs) derived from the data for each COPC in soils are provided as electronic attachments, with computations presented and EPCs calculated for COPCs within each of the three datasets. The ProUCL input tables are also included as electronic attachments. The results were evaluated to identify any samples that may require additional assessment or special management based on the risk characterization approach. The calculated EPCs for the surface, subsurface, and pooled exposure scenarios are provided in **Table 7**. These EPCs were used for both the Composite Worker and Construction Worker risk assessments.

As indicated above, the EPCs for lead are the average (i.e., arithmetic mean) values for each dataset. A lead evaluation spreadsheet, providing the computations used to determine lead averages for each dataset in each EU is also included as an electronic attachment. The average lead concentrations are presented for each dataset in **Table 6**, which indicates that neither surface, subsurface, nor pooled soils exceeded an average lead value of 800 mg/kg in any EU. The screening criterion for lead was set at an EU arithmetic mean of 800 mg/kg based on the RSL, with a secondary limit of 2,518 mg/kg based on the May 2017 updated ALM developed by the USEPA (corresponding to a 5% probability of a blood lead level of 10 ug/dL). There were no locations where concentrations of lead exceeded 10,000 mg/kg.

None of the detections of PCBs included in the project-specific SLRA evaluation exceeded the mandatory excavation criterion of 50 mg/kg.

Composite Worker Assessment:

Risk ratios for the estimates of potential EPCs for the site-specific Composite Worker baseline scenario prior to the placement of slag aggregate at the Site are shown in **Table 8** (surface), **Table 9** (subsurface), and **Table 10** (pooled soils). The results are summarized as follows:

Worker Scenario	Exposure Unit	Medium	Hazard Index (>1)	Total Cancer Risk
Composite Worker	EU1 Inside	Surface Soil	none	3E-6
		Subsurface Soil	none	4E-6
		Surface & Subsurface Soil	none	4E-6
	EU2 Outside	Surface Soil	none	4E-6
		Subsurface Soil	none	4E-6
		Surface & Subsurface Soil	none	4E-6

Based on the risk ratios for Sub-Parcel B2-2, the proposed environmental capping (100% of the Site) is an acceptable remedy to be protective of future Composite Workers for the surface, subsurface, and pooled exposure scenarios. None of the carcinogenic risk estimates for the Composite Worker scenario were greater than 1E-4 and none of the non-carcinogenic HI values exceeded 1. Capping and institutional controls (to maintain the integrity of the cap) are suitable measures for the protection of the future Composite Worker for both cancer risks and non-cancer hazards. The capping remedy will be protective of slag aggregate which will be used as the primary fill material at the Site.

Construction Worker Assessment:

According to the work schedule provided by Tradepoint Atlantic, intrusive activities which could result in potential Construction Worker exposure risks are expected to be limited to three primary utility installation tasks:

- Domestic Water/Fire Loop: 120 exposure days estimated
- Sanitary: 120 exposure days estimated
- Stormwater: 96 exposure days estimated

Although the anticipated work period may be subject to change (see Schedule provided in Section 7.0), the duration of these activities is not expected to increase. Each of these primary intrusive work tasks will be performed by a separate work crew. Construction Worker risks were evaluated for several exposure scenarios to determine the exposure frequency for each EU that would result in risk ratios equivalent to a cumulative cancer risk above 1E-5 or HI of 1 for any individual target organ. Risk ratios for the estimates of potential EPCs for the Construction Worker scenario using the selected exposure durations (95 and 55 work days for EU1 and EU2, respectively) are shown in **Table 11** (surface), **Table 12** (subsurface), and **Table 13** (pooled surface and subsurface soils). The variables entered for calculation of site-specific Construction Worker SSLs (EU area, input assumptions, and exposure frequency) are indicated as notes on the tables. The spreadsheet used for computation of the site-specific Construction Worker SSLs is included in **Appendix D**. The results are summarized as follows:

Worker Scenario	Medium	Hazard Index (>1)	Total Cancer Risk
Construction Worker EU1 (95 exposure days)	Surface Soil	none	2E-7
	Subsurface Soil	none	3E-7
	Surface & Subsurface Soil	none	3E-7
Construction Worker EU2 (55 exposure days)	Surface Soil	none	6E-7
	Subsurface Soil	none	2E-7
	Surface & Subsurface Soil	none	3E-7

Using the 95-day exposure duration for EU1 and the 55-day exposure duration for EU2, the carcinogenic risks were all less than $1E-5$, and none of the non-carcinogens caused a cumulative HI to exceed 1 for any target organ system. These findings are below the acceptable limits for no further action established by the agencies. This evaluation indicates that site-specific health and safety protocols or further action would be required only if 95 exposure days or 55 exposure days were exceeded for an individual worker in EU1 and EU2, respectively.

Certain activities at the Site (utility installations for specific crews as noted above) are anticipated to exceed these allowable durations, and Construction Worker risks must be mitigated to facilitate the proposed construction work. Additional site-specific health and safety requirements are warranted to be protective of workers. Upgraded Personal Protective Equipment (PPE) beyond standard Level D protection will be used for the entire scope of intrusive work covered by this RADWP as a protective measure to ensure that there are no unacceptable exposures for Construction Workers during project implementation. The modified Level D PPE requirements which will be applied during this project, including specific PPE details, planning, tracking/supervision, enforcement, and documentation, are outlined in the PPE Standard Operational Procedure (SOP) provided as **Appendix E**.

Institutional controls will be required to be established for the protection of future Construction Workers in the event of any future long-term development which could include intrusive activities. The anticipated institutional controls, including notification requirements, health and safety requirements, and materials management requirements, are specified in Section 5.4.

3.3.3. Evaluation of Comprehensive Environmental Response, Compensation, and Liability Act (CERCLA) Criteria

Based on the data obtained from the characterization of surface and subsurface soils, results from the SLRA indicate that no further action is required within the proposed development area to mitigate potential Composite Worker risks. However, Tradepoint Atlantic will be using processed slag aggregate as construction fill material throughout the Site. The placement of materials other than approved clean fill, including processed slag aggregate, will necessitate that Sub-Parcel B2-2 will be subject to surface engineering controls (i.e., capping) based on prior MDE guidance. The entirety of the Site (98.0 acres) will therefore require a remedy of capping with institutional controls to mitigate potential current and future Composite Worker risks.

Site-specific health and safety controls will be required to mitigate Construction Worker risks within the sub-parcel. This includes using modified Level D PPE. The modified Level D PPE requirements will be implemented throughout the project duration in accordance with the PPE SOP provided as **Appendix E**. Institutional controls will be required to be established for the protection of future Construction Workers in the event of any future long-term development which could include intrusive activities.

The proposed VCP capping remedy (with institutional controls) for Sub-Parcel B2-2 was evaluated for consistency with the CERCLA Threshold Criteria and the Balancing Criteria. The Threshold Criteria assess the overall protection of human health and the environment, as well as achievement of media cleanup objectives and control of sources of releases at the Site. The Balancing Criteria assess long-term effectiveness and permanence; reduction of toxicity, mobility or volume; short-term effectiveness; implementability; cost effectiveness; and community and State acceptance.

Threshold Criteria:

Protect Human Health and the Environment: The assessment against this criterion evaluates how the remedy, as a whole, protects and maintains protection of human health and the environment. This criterion is satisfied when response actions are complete. The purpose of this remedy is to provide a protective barrier between human site users and potentially impacted slag aggregate, and to protect the environment by preventing surface water from contacting potentially impacted materials in place. The capping and institutional control remedy would eliminate risk to current and future Composite Workers by preventing exposure to areas of the Site where processed slag aggregate has been placed. Groundwater does not present a human health hazard since there is no groundwater use. Implementation of the proposed use restrictions will address the residual risk and will also protect hypothetical future Construction Workers by eliminating or controlling potential exposure pathways, thus, reducing potential intake and contact of soil/groundwater COPCs by human receptors.

Achieve Media Cleanup Objective: The assessment against this criterion describes how the remedy meets the cleanup objective, which is risk reduction, appropriate for the expected current and reasonably anticipated future land use. The objective is to protect current/future Composite Workers and Construction Workers from potential exposures to constituents present in slag aggregate at levels that may result in risks of adverse health effects. Given the controlled access and use restrictions, the proposed remedy will attain soil and groundwater objectives. The activity use restrictions will eliminate current and future unacceptable exposures to both soil and groundwater.

Control the Source of Releases: In its RCRA Corrective Action proposed remedies, USEPA seeks to eliminate or reduce further releases of hazardous wastes or hazardous constituents that may pose a threat to human health and the environment. Controlling the sources of contamination relates to the ability of the proposed remedy to reduce or eliminate, to the maximum extent practicable, further releases. Sampling results did not indicate localized, discernible source areas associated with the soil conditions observed at the Site, with the possible exception of NAPL at select soil boring locations (as described in Section 3.2.3). The proposed capping remedy will prevent contact with COPCs potentially present in the soil or slag aggregate, reducing potential risks for future

industrial workers. The control measures included in the proposed remedy, such as Materials Management Plan requirements and groundwater use restrictions, provide a mechanism to control and reduce potential further releases of COPCs. This is achieved by eliminating the potential for groundwater use and requiring proper planning associated with intrusive activities.

Balancing Criteria:

Long-Term Reliability and Effectiveness: The assessment against this criterion evaluates the long-term effectiveness of the remedy in maintaining protection of human health and the environment after the response objectives have been met. The primary focus of this criterion is the extent and effectiveness of the controls that may be required to manage the risk posed by slag aggregate, treatment residuals and/or untreated wastes. The capping remedy for the Composite Worker area will permanently contain the slag aggregate and other potentially contaminated media in place. In order for the cap to effectively act as a barrier, regular inspections will be required to determine if erosion or cracks have formed that could expose workers to contaminated materials.

Institutional controls will be implemented to protect future Composite and Construction Workers against inadvertent contact with potentially impacted media. The anticipated institutional controls are specified in Section 5.4. The Tenant will be required to sign onto the Environmental Covenant with restriction in the NFA. The proposed remedy will maintain protection of human health and the environment over time by controlling exposures to the hazardous constituents potentially remaining in slag aggregate or existing on-site media. The long-term effectiveness is high, as use restrictions are readily implementable and easily maintained. Given the historical, heavily industrial uses of the Site and the surrounding area, including the presence of landfills, land and groundwater use restrictions are expected to continue in the long term.

Reduction of Toxicity, Mobility, or Volume of Waste: The assessment against this criterion evaluates the anticipated performance of specific technologies that a remedial action alternative may employ. The capping remedy for the Composite Worker area will prevent the spread of contaminants in wind-blown dust or stormwater and will prevent infiltration through the unsaturated zone from carrying contaminants to the groundwater. Thus, the mobility of contaminants will be reduced by the capping remedy.

Short-term Effectiveness: The assessment against this criterion examines how well the proposed remedy protects human health and the environment during the construction and implementation until response objectives have been met. This criterion also includes an estimate of the time required to achieve protection for either the entire site or individual elements associated with specific site areas or threats. The risks to the Construction Worker during remedy implementation are mitigated by implementing site-specific

health and safety requirements including upgraded PPE. The short-term risk to site workers following appropriate health and safety measures during implementation of the remedy will be low, leading to a high level of short-term effectiveness for protection of future site users and the environment. Short-term effectiveness in protecting on-site workers and the environment will be achieved through establishing appropriate management, construction, health and safety, and security procedures. Proper water management protocols will be implemented to prevent discharges offsite. Security and fences will be used to maintain controlled access during construction.

Implementability: The assessment against this criterion evaluates the technical and administrative feasibility, including the availability of trained and experienced personnel, materials, and equipment. Technical feasibility includes the ability to construct and operate the technology, the reliability of the technology, and the ability to effectively monitor the technology. Administrative feasibility includes the capability of obtaining permits, meeting permit requirements, and coordinating activities of governmental agencies. The proposed capping remedy for the Composite Worker area uses readily available capping techniques.

Cost Effectiveness: The assessment against this criterion evaluates the capital costs, annual Operating and Maintenance (O&M) costs, and the net present value (NPV) of this remedy relative to other alternatives. The capping remedy for the Composite Worker area remedial costs would be incurred as part of the proposed site development, regardless of the placement of slag aggregate.

State Support / Agency Acceptance: MDE has been involved throughout the Site investigation process. The proposed use restrictions included in the proposed remedy are generally recognized as commonly employed measures for long-term stewardship. Ultimately State/MDE support will be evaluated based on comments received during the public comment period.

A capping remedy with institutional controls would satisfy the CERCLA Threshold Criteria and the Balancing Criteria and would do so in a manner that ensures reliable implementation and effectiveness. The remedy is cost-effective and consistent with the proposed development plan.

4.0 PROPOSED SITE DEVELOPMENT PLAN

Tradepoint Atlantic is proposing to construct a warehouse building designated as Logistics Center X on Sub-Parcel B2-2, along with exterior support areas (parking, etc.) and a paved extension to Tradepoint Avenue near the northeast corner of the warehouse. The proposed development of the warehouse facility and roadway will include permanent improvements on approximately 98.0 acres of land intended for occupancy in the central portion of Parcel B2 and northern portion of Parcel B5. The proposed future use of Sub-Parcel B2-2 is Tier 3 – Industrial. The remainder(s) of Parcel B2 and Parcel B5 will be addressed in separate development plans in accordance with the requirements of the ACO that will include RADWPs, if necessary. Outside of the main development area designated as Sub-Parcel B2-2, several easements (with a total area of approximately 7.6 acres within the LOD) will be utilized to install stormwater and service utilities for the project. The temporary utility work is not intended to be the basis for the issuance of a NFA or a COC; therefore, the utility work within the easements is not covered by this RADWP.

Certain compounds are present in the soils located near the surface and in the subsurface at concentrations in excess of the PALs. Therefore, soil is considered a potential media of concern. The SLRA has indicated no unacceptable potential risks/hazards to future adult Composite Workers associated with impacts to surface or subsurface soil exceeding the PALs. Based on the SLRA findings, surface engineering controls are not required at the Site to be protective of future adult Composite Workers who could potentially contact surface soil (or relocated subsurface soil) at the Site. However, Tradepoint Atlantic has proposed the use of processed slag aggregate as fill material at the Site. The placement of materials other than approved clean fill, including processed slag aggregate, will necessitate that Sub-Parcel B2-2 will be subject to surface engineering controls (i.e., capping) based on prior MDE guidance.

Future Construction Workers may contact impacted surface and/or subsurface soil during earth movement activities associated with construction. The findings of the SLRA indicated that the screening level estimates of Construction Worker cancer risk for the site-specific 95-day and 55-day exposure frequencies were less than 1E-5 (the acceptable level for no further action) for EU1 and EU2, respectively. Furthermore, no non-cancer hazards above the HI of 1 were identified for any target organ in the development area using these respective exposure frequencies. This evaluation indicates that site-specific health and safety protocols or further action would be required only if these durations were exceeded in EU1 and EU2, respectively.

Certain activities at the Site are anticipated to exceed these allowable durations, and Construction Worker risks must be mitigated to facilitate the proposed construction work. Additional site-specific health and safety requirements are warranted to be protective of workers. Upgraded PPE beyond standard Level D protection will be used in conjunction with the property-wide Health and Safety Plan (HASP) for the entire scope of intrusive work covered by this RADWP

as a protective measure to ensure that there are no unacceptable exposures for Construction Workers during project implementation. The modified Level D PPE requirements which will be applied during this project, including specific PPE details, planning, tracking/supervision, enforcement, and documentation, are outlined in the PPE SOP provided as **Appendix E**.

A restriction prohibiting the use of groundwater for any purpose at the Site will be included as an institutional control in the NFA and COC issued by the MDE, and a deed restriction prohibiting the use of groundwater will be filed. These groundwater use restrictions will protect future Composite Workers from potential exposures. Proper water management is required to prevent unacceptable discharges or risks to Construction Workers during development. Work practices and health and safety plans governing groundwater encountered during excavation activities will provide protection for Construction Workers involved with future development at the Site.

The development plan for the Site is indicated in **Figure 2**, and the detailed development drawings (provided by Bohler Engineering) are included as **Appendix F**. The process of constructing the proposed Logistics Center X will involve the tasks listed below. As-built and regulatory documentation for the outlined tasks and procedures will be provided in a Sub-Parcel B2-2 Development Completion Report:

4.1. RESPONSE PHASE – WELL ABANDONMENT

Permanent groundwater monitoring wells SW-057-MWS, SW-070-MWS, SW09-PZM004, SW09-PZM028, and SW09-PZM068 are located inside the development boundary as shown on **Figure 6**. Each of the listed monitoring wells was previously sampled during the Area B Groundwater Investigation, with the results presented and discussed in the Phase II Investigation Report. These monitoring wells have been properly abandoned in accordance with COMAR 26.04.04.34 through 36. These abandonments were covered by the Logistics Centers Grading Plan for Area B: Sub-Parcel B2-2 (which was developed for preparatory grading work associated with the development of Logistics Center X as well as the adjacent Logistics Center IX).

The abandonment of any permitted monitoring wells on the property must be reported to the Water Management Administration as per COMAR 26.04.04, and records of all monitoring well and piezometer abandonments (including abandonment forms, if available) will be included in the Development Completion Report.

4.2. DEVELOPMENT PHASE

4.2.1. Erosion and Sediment Control Installation

Installation of erosion and sediment controls will be completed in accordance with the requirements of the 2011 Maryland Standards and Specifications for Soil Erosion and Sediment Control prior to any construction at the Site. Any soils which are disturbed during the installation of erosion and sediment controls will be replaced on-site below the cap.

4.2.2. Grading and Site Preparation

As indicated on the development plans in **Appendix F**, site grading will occur within the Sub-Parcel B2-2 boundary. The Site will be raised with net fill, which will require importing material to the Site. The major grading activities were covered by the Logistics Centers Grading Plan for Area B: Sub-Parcel B2-2 (which was developed for preparatory grading work associated with the development of Logistics Center X as well as the adjacent Logistics Center IX); however, some additional grading work will be required to facilitate final construction.

Any material that is not suitable for compaction will be excavated and replaced with subbase material, although it is not anticipated that poor soils will be encountered. Borrow materials will be obtained from MDE-approved sources, and will be documented prior to transport to the Site. Processed slag aggregate sourced from the Tradepoint Atlantic property or other materials approved by the MDE for industrial use may be used as fill, but the placement of materials other than approved clean fill will necessitate that the Site will be subject to surface engineering controls (i.e., capping). Fill sources shall be free of organic material, frozen material, or other deleterious material. In the case that there is excess material (not anticipated), the spoils will be stockpiled at a suitable location in accordance with the Materials Management Plan (MMP) for the Sparrows Point Facility (Papadopulos & Associates, et al., June 17, 2015). This work will be coordinated with MDE accordingly. No excess material will leave the 3,100-acre property without prior approval from MDE.

4.2.3. Installation of Structures and Underground Utilities

The warehouse, parking areas, and other infrastructure associated with the Logistics Center X will be installed at the grades and lines shown on the development plans in **Appendix F**. Soils relocated or removed during construction may be replaced on-site below the cap, but soil removed from utility trenches cannot be used as fill within the utility trenches unless such materials are approved for this use by the VCP. Additional protocols for the installation of utilities at the Site are provided in Section 5.1.2.

Any water removed will be collected to be sampled as described in Section 5.2 and, if acceptable, sent to the on-site Humphrey Creek Waste Water Treatment Plant (HCWWTP). If analytical results indicate the presence of levels of contaminants exceeding levels that are acceptable for treatment at the HCWWTP (as defined in Section 5.2), the water will either be pre-treated through an on-site treatment system and retested prior to sending to the HCWWTP or will be disposed of at an appropriate off-site facility. Any water that must be removed and sent to the HCWWTP will be pumped to the nearest catch basin that discharges to the Tin Mill Canal (TMC). Any water discharged to a catch basin will be pumped through a filter bag or equivalent to remove suspended solids prior to discharge. Documentation of the catch basin(s) used shall be provided in the Development Completion Report.

4.2.4. Floor Slabs and Paving

Much of the Site will be covered with floor slabs or paving as indicated in the development plans provided in **Appendix F**. The paved areas will receive a layer of subbase material which will consist of compacted aggregate base, which may include processed slag aggregate sourced from the Tradepoint Atlantic property. The placement of processed slag aggregate or materials other than MDE-approved clean fill will necessitate that the Site will be subject to surface engineering controls (i.e., capping).

The required minimum thicknesses of all site-wide pavement sections which will serve as surface engineering controls are indicated in the general cap sections provided in **Appendix G**. According to the development plans, all paved areas at the Site will be installed with a minimum of 4 inches of compacted aggregate base and a minimum of 4 inches of overlying pavement (asphalt or concrete) surface, which meet these required minimum thicknesses.

4.2.5. Landscaping

Small areas of the Site will be landscaped and may overlie areas which have been graded using processed slag aggregate as fill material. The required minimum thicknesses of all site-wide landscaping sections which will serve as surface engineering controls are indicated in the general cap sections provided in **Appendix G**. According to the development plans, all landscape areas at the Site will be installed with a minimum of 6 inches of clean topsoil overlying 18 inches of clean fill, with an underlying geotextile marker fabric between the clean fill and the underlying materials. The proposed landscape sections meet the minimum capping requirements.

4.2.6. Stormwater Management

The stormwater management plan for the Site is provided on the overall utility plan provided within **Appendix F**. Stormwater infrastructure will be installed throughout the Site, and will discharge to the north into the TMC and to the south into an existing subgrade stormwater utility. The northern and southern alignments of the stormwater system will be installed through easements outside of Sub-Parcel B2-2, which are covered by a separate LSPP. Tradepoint Atlantic will work with the MDE Industrial & General Permits Division to renew the property-wide NPDES permit. A meeting has already been conducted for this purpose. The stormwater management systems for each parcel are reviewed and approved by Baltimore County for each individual development project. A full plan for the property will be designed once more parcels have been completed and there is a greater understanding of how the overall property will be developed. The agencies will be copied when the management plan is submitted.

5.0 DEVELOPMENT IMPLEMENTATION PROTOCOLS

5.1. DEVELOPMENT PHASE

This plan presents protocols for the handling of soils and fill materials in association with the development of Sub-Parcel B2-2. In particular, this plan highlights the minimum standards for construction practices and managing potentially contaminated materials to reduce potential risks to workers and the environment.

Several exceedances of the PALs were identified in soil samples across the Site. The PALs are set based on USEPA's RSLs for industrial soils, or other direct guidance from the MDE. Because PAL exceedances can present potential risks to human health and the environment at certain concentrations, this plan presents material management and other protocols to be followed during the work to adequately mitigate such potential risks for material remaining on-site during the development phase. No soils contaminated with total PCBs in excess of 50 mg/kg have been identified in Sub-Parcel B2-2. There were no samples where detections of lead were identified in excess of 10,000 mg/kg. There were several locations within, or adjacent to, the proposed development LOD with soil exceedances of the TPH/Oil & Grease PAL (6,200 mg/kg) and/or potential indications of NAPL in the soil core (B2-024-SB, B2-051-SB, B2-053-SB, B2-055-SB, B5-097-SB). These borings are pictured with respect to the development layout on **Figure S2** and should be considered with respect to utility alignments and inverts prior to trenching in these areas. The soil boring observation logs from these locations are provided for reference in **Appendix C**.

Following completion of the SLRA, the screening level estimates of Construction Worker cancer risk for the site-specific 95-day and 55-day exposure frequencies were less than $1E-5$ (the acceptable level for no further action) for EU1 and EU2, respectively. Furthermore, none of the potential non-cancer hazards were elevated above the HI of 1 for any exposure scenario when the schedule for intrusive construction activities was limited to these respective exposure durations. Certain activities at the Site are anticipated to exceed these durations, and Construction Worker risks must be mitigated to facilitate the proposed construction work. Additional site-specific health and safety requirements are warranted to be protective of workers. Upgraded PPE beyond standard Level D protection will be used for the entire scope of intrusive work covered by this RADWP as a protective measure to ensure that there are no unacceptable exposures for Construction Workers during project implementation. The modified Level D PPE requirements which will be applied during this project, including specific PPE details, planning, tracking/supervision, enforcement, and documentation, are outlined in the PPE SOP provided as **Appendix E**.

Based on the characterization of surface and subsurface soils and the associated SLRA findings, surface engineering controls are not required at the Site to be protective of future adult

Composite Workers who could potentially contact surface soil (or relocated subsurface soil) at the Site. However, Tradepoint Atlantic has proposed the use of processed slag aggregate as fill material at the Site. The placement of materials other than approved clean fill, including processed slag aggregate, will necessitate that the Site will be subject to surface engineering controls (i.e., capping) based on prior MDE guidance. The proposed capping sections will meet the required minimum thicknesses for surface engineering controls, which are provided in **Appendix G**.

5.1.1. Erosion/Sediment Control

Erosion and sediment controls will be installed prior to commencing work in accordance with 2011 Maryland Standards and Specifications for Soil Erosion and Sediment Control. The erosion and sediment controls will be approved by the MDE. In addition, the following measures will be taken to prevent contaminated soil from exiting the Site:

- Stabilized construction entrance will be placed at site entrance.
- A dry street sweeper will be used as necessary on adjacent roads, and the swept dust will be collected and properly managed.
- Accumulated sediment removed from silt fence, and sediment traps if applicable, shall be periodically removed and returned to the Site.

5.1.2. Soil Excavation and Utility Trenching

A pre-excavation meeting shall be held to address proper operating procedures for working on-site and monitoring excavations and utility trenching in potentially contaminated material. This meeting shall include the construction manager and the Environmental Professional (EP) providing oversight on the project. During the meeting, the construction manager and the EP shall review the proposed excavation and trenching locations and any associated utility inverts. The construction manager will be responsible for conveying all relevant information regarding excavation/grading and/or utility work to the site workers who will be involved with these activities. There were several soil borings with potential evidence of NAPL identified during the preceding Phase II Investigations within a reasonable proximity to the development LOD (see **Figure S2** and **Appendix C**). However, based on the soil core observations and lack of NAPL accumulation within temporary screening piezometers installed at these locations, no special considerations are required prior to work other than review of the NAPL Contingency Plan discussed below. The HASP for the project shall also be reviewed and discussed.

The EP will provide oversight of soil excavation/trenching activities as described in Section 5.6. Soil excavation/trenching will occur during various phases of construction. In general, and based on the existing sampling information, all excavated materials are expected to be suitable

for replacement on the Site. However, the EP will monitor the soil excavation activities for signs of significantly contaminated material which may not be suitable for reuse (as described below).

To the extent practical, all excavation activities should be conducted in a manner to minimize double or extra handling of materials. Any stockpiles shall be kept within the Site footprint, and in a location that is not subjected to concentrated stormwater runoff. Stockpiles shall be managed as necessary to prevent the erosion and off-site migration of stockpiled materials, and in accordance with the applicable provisions of the 2011 Maryland Standards and Specifications for Soil Erosion and Sediment Control. Soil designated for replacement on-site which does not otherwise exhibit evidence of contamination (as determined by the EP) may be managed in large stockpiles (no size restriction) as long as they remain within the erosion and sediment controls.

All utility trenches will be backfilled with bedding and backfill materials approved by the MDE for industrial use. A general utility cross section is provided as **Appendix H**. Additional preventative measures will be required if evidence of petroleum contamination is encountered, to prevent the discharge to, or migration of, petroleum product along a utility conduit. Contingency measures have been developed to ensure that utilities will be constructed in a manner that will prevent the migration of any encountered NAPL, and that excavated material will be properly managed. The Utility Excavation NAPL Contingency Plan (**Appendix I**) provides protocols to be followed if NAPL is encountered during the construction activities. Preventative measures to inhibit the spread of petroleum product will be conducted in accordance with this plan.

The EP will monitor all soil excavation and utility trenching activities for signs of potential contamination. In particular, soils will be monitored with a hand-held PID for potential VOCs, and will also be visually inspected for the presence of staining, petroleum waste materials, or other indications of significant contamination. If screening of excavated materials by the EP indicates the presence of conditions of potential concern (i.e., sustained PID readings greater than 10 ppm, visual staining, unsuitable waste materials, etc.), such materials shall be segregated for additional sampling and special management.

Excavated material exhibiting evidence of significant contamination shall be placed in stockpiles (not to exceed 500 cubic yards) on polyethylene sheeting and covered with polyethylene sheeting to minimize potential exposures and erosion when not in use. Materials stockpiled due to evidence of contamination will be sampled in accordance with waste disposal requirements, and transported to an appropriate permitted disposal facility. Plans for analysis of segregated soils for any use other than disposal must be submitted to the MDE for approval.

Excavated material that is visibly impacted by NAPL will be segregated and managed in accordance with the requirements specified in the Utility Excavation NAPL Contingency Plan. Excavated material with indications of possible NAPL contamination will also be containerized or placed in a stockpile (not to exceed 500 cubic yards) on polyethylene sheeting and covered with polyethylene sheeting until the material can be analyzed for TPH/Oil & Grease and PCBs

(total) to characterize the material for appropriate disposal. The MDE will be notified if such materials are encountered during excavation or utility trenching activities.

5.1.3. Soil Sampling and Disposal

Excavated materials that are determined by the EP to warrant sampling and analysis because of elevated PID readings or other indications of potential contamination shall be sampled and analyzed to determine how the materials should be managed. If excavated and stockpiled, such materials should be covered with a polyethylene tarp to minimize potential exposures and erosion. All stockpiled soil may be considered for use as fill at this Site or on other areas of the property depending on the analytical results. A sampling Work Plan including a description of the material, estimated volume, and sampling parameters will be submitted to the MDE for approval. The resulting analytical data will be submitted to the MDE to determine the suitability of the material for reuse. If the MDE determines that the materials are unsuitable for reuse, the materials will be sampled to determine if they are classified as hazardous waste.

Soil material that is determined to be a hazardous waste shall be shipped off-site in accordance with applicable regulations to an appropriate and permitted RCRA disposal facility. Soil material may be taken to an appropriate off-site non-hazardous landfill for proper disposal if the concentrations of excavated sampled materials indicate that the materials are not hazardous, but still are not suitable for reuse. The quantities of all materials that require disposal off-site, if any, will be recorded and identified in the Development Completion Report.

5.1.4. Fill

Processed slag aggregate sourced from the Tradepoint Atlantic property will be used as the primary fill material for this project. The placement of processed slag aggregate or materials other than approved clean fill will necessitate that the Site will be subject to surface engineering controls (i.e., capping). Soil excavated on the sub-parcel has been determined to be suitable for re-use at the Site below the surface engineering controls, unless such materials are determined by the EP/MDE to be unsuitable for use as outlined in Section 5.1.2 and Section 5.1.3.

All over-excavated utility trenches will be backfilled with bedding and backfill approved by the MDE for industrial use. As with structural fill, processed slag aggregate and other materials approved for industrial use can be used as backfill in utility trenches if the area will be covered by a VCP cap. Any utility backfill which will extend into the cap (i.e., top 2 feet of backfill in landscaped areas) must meet the VCP clean fill requirements, and a geotextile marker fabric will be placed between the VCP clean fill and any underlying material. Soil removed from utility trenches cannot be used as fill within the utility trenches unless such materials are approved for this use by the VCP. A general utility detail drawing is provided as **Appendix H**. Material imported to the Site will be screened according to MDE guidance for suitability.

5.1.5. Dust Control

General construction operations, including soil excavation and transport, and trenching for utilities will be performed at the Site. These activities are anticipated to be performed in areas of soil impacted with COPCs. Best management practices should be undertaken at the Sparrows Point property as a whole to prevent the generation of dust which could impact other areas of the property outside of the immediate work zone. To limit worker exposure to contaminants borne on dust and windblown particulates, dust monitoring will be performed in the immediate work zone and at the upwind and downwind perimeter of the Site, and dust control measures will be implemented if warranted based on the monitoring results. The action level proposed for the purpose of determining the need for dust suppression techniques (e.g. watering and/or misting) during the development activities at the Site will be 3.0 mg/m³. The lowest of the site-specific dust action levels, OSHA PELs, and ACGIH TLV was selected as the proposed action level.

The EP will be responsible for the dust monitoring program. Air monitoring will be performed using Met One Instruments, Inc. E-Sampler dust monitors or equivalent real-time air monitoring devices. The EP will set-up dust monitoring equipment at the outset of ground intrusive work or other dust-generating activities, and continuous dust monitoring will be performed during this work. In addition to work area monitoring, a dust monitor will be placed at selected perimeter locations that will correspond to the upwind and downwind boundaries based on the prevailing wind direction predicted for that day. The prevailing wind direction will be assessed during the day, and the positions of the perimeter monitors will be adjusted if there is a substantial shift in the prevailing wind direction.

Once all dust-generating activities are complete (which may occur at a later stage of the project once ground intrusive work has been completed or after the Site has been capped), the dust monitoring program may be discontinued. If additional dust-generating activities commence, additional dust monitoring activities will be performed.

If sustained dust concentrations exceed the action level (3.0 mg/m³) at any of the monitoring locations as a result of conditions occurring at the Site, operations will be stopped temporarily until dust suppression can be implemented. Operations may be resumed once monitoring indicates that dust concentrations are below the action level. The background dust concentration will be utilized to evaluate whether Site activities are the source of the action level exceedance. The background dust concentration will be based on measurements over a minimum of a 1-hour period at the upwind Site boundary. The upwind data will be used to calculate a time weighted average background dust concentration. As noted above, the locations of the perimeter dust monitors may be adjusted periodically if there is a substantial shift in the prevailing wind direction.

As applicable, air monitoring will be conducted during development implementation activities to assess levels of exposure to Site workers, establish that the work zone designations are valid, and

verify that respiratory protection being worn by personnel, if needed, is adequate. Concurrent with the work zone air monitoring, perimeter air monitoring will also be performed at the upwind and downwind Site boundaries to ensure contaminants are not migrating off-site. The concentration measured at the downwind perimeter shall not exceed the action level of 3.0 mg/m³, unless caused by background dust from upwind of the Site. If exceedances of the action level are identified downwind for more than five minutes, the background dust concentration shall be evaluated to determine whether the action level exceedances are attributable to Site conditions. If on-site activities are the source of the exceedances, dust control measures and additional monitoring will be implemented. The dust suppression measures may include wetting or misting using a hose connected to a water supply or a water truck stationed at the Site.

Dust control measures will be implemented as described above to address dust generated as a result of construction activities conducted at the Site. However, based on the nature of the area and/or on-going activities surrounding the Site, it is possible that windblown particulates may come from surrounding areas. As discussed above, the dust concentration in the upwind portion of the Site will be considered when monitoring dust levels in the work area. A pre-construction meeting will be held to discuss the potential of windblown particulates from other activities impacting the air monitoring required for this RADWP. Site contact information will be provided to address the possibility of upwind dust impacts. If sustained dust is observed above the action level (3.0 mg/m³) and it is believed to originate from off-site (i.e., upwind) sources, this will immediately be reported to the MDE-VCP project team, as well as the MDE Air and Radiation Administration (ARA).

5.2. WATER MANAGEMENT

This plan presents the protocols for handling any groundwater or surface water that needs to be removed to facilitate construction of the proposed Logistics Center X. While it is not anticipated that a significant volume of groundwater will be encountered during the proposed development, the following measures are provided as contingencies.

5.2.1. Groundwater PAL Exceedances

A total of 10 shallow groundwater samples (as shown on **Figure 4**) were collected from a temporary groundwater sample collection point and permanent monitoring wells within and surrounding the Site. Aqueous PAL exceedances in shallow groundwater in the vicinity of the development LOD included both inorganic and organic compounds, although none of the detections were significantly elevated. The complete analytical findings of the Area B Groundwater Investigation and Parcel B2 Phase II Investigation, including the results obtained from shallow groundwater points in the vicinity of the development LOD, were presented to the agencies within the respective Phase II Investigation Reports. The aqueous PAL exceedances that are relevant for this RADWP are summarized on **Figure GW1** through **Figure GW4**. While the concentrations of PAL exceedances are not deemed to be a significant human health

hazard since there is no on-site groundwater use, proper water management is required to prevent unacceptable discharges or risks to on-site workers.

5.2.2. Dewatering

Dewatering may be necessary during the installation of underground utilities (within trenches/excavations). If dewatering is required, it shall be done in accordance with all local, state, and federal regulations. Water that collects in excavations/trenches due to intrusion of groundwater, stormwater, and/or dust control waters will be transported to the HCWWTP. The water will be treated and discharged in accordance with NPDES Permit No. 90-DP-0064A; I. Special Conditions; A.4; Effluent Limitations and Monitoring Requirements.

Any water that must be removed and sent to the HCWWTP will be pumped to the nearest catch basin that discharges to the TMC. Water in the TMC feeds into the HCWWTP where it is treated prior to release into Bear Creek. Any water discharged to a catch basin will be pumped through a filter bag or equivalent to remove suspended solids prior to discharge. A figure is not being provided at this time as the specific discharge location for dewatering fluids may change during development as conditions dictate. Documentation of the catch basin(s) used shall be provided in the Development Completion Report.

The EP will inspect any water that collects in the excavations/trenches. If the water exhibits indications of significant contamination (sheen, odor, discoloration, presence of product), or if the excavation/trench is within a known area of significant groundwater contamination (if groundwater is the source of the intrusive water) or a significant Phase II Investigation target, the water may be sampled and analyzed for some or all of the analyses listed below. The analyses run will be dependent on the suspected source of contamination and local site conditions.

The results of the analyses will be reviewed by the HCWWTP operator to determine if any wastewater treatment system adjustments are necessary. If the results of the analyses are above the threshold levels listed below, the water will be further evaluated to confirm acceptable treatment at the HCWWTP, or will be evaluated to design an appropriate pre-treatment option. Alternatively, the water may be disposed of at an appropriate off-site facility.

<u>Analysis</u>	<u>Threshold Levels</u>
• <u>Total metals by USEPA Method 6020A</u>	<u>1,000 ppm</u>
• <u>PCBs by USEPA Method 8082</u>	<u>>Non-Detect</u>
• <u>SVOCs by USEPA Method 8270C</u>	<u>1 ppm</u>
• <u>VOCs by USEPA Method 8260B</u>	<u>1 ppm</u>
• <u>Oil & Grease by USEPA Method 1664</u>	<u>200 ppm</u>

Documentation of any water testing, as well as the selected disposal option, will be reported to the MDE in the Development Completion Report. Any permits or permit modifications related to dewatering will be provided to the agencies as addenda to this RADWP.

5.3. HEALTH AND SAFETY

A property-wide Health and Safety Plan (HASP provided as **Appendix J**) has been developed and is attached to this plan to present the minimum requirements for worker health and safety protection for all development projects. All contractors working on the Site must prepare their own HASP that provides a level of protection at least as much as that provided by the attached HASP. Alternately, on-site contractors may elect to adopt the HASP provided.

General health and safety controls (level D protection) would be adequate to mitigate the potential risk to Construction Workers during development for a duration of up to 95 exposure days in EU1 and 55 exposure days in EU2. However, certain activities at the Site (utility installations for specific crews) are anticipated to exceed these allowable durations. Modified Level D PPE will be used for the entire scope of intrusive work covered by this RADWP as an additional protective measure to ensure that there are no unacceptable exposures for Construction Workers during project implementation. Health and safety controls outlined in the property-wide HASP and PPE SOP will mitigate any potential risk to Construction Workers from contacting impacted soil and groundwater during development. The modified Level D PPE requirements proposed for this development project, including specific PPE details, planning, tracking/supervision, enforcement, and documentation, are outlined in the PPE SOP provided as **Appendix E**.

Prior to commencing work, the contractor must conduct an on-site safety meeting for all personnel. All personnel must be made aware of the HASP and the PPE SOP. Detailed safety information shall be provided to personnel who may be exposed to COPCs. Workers will be responsible for following established safety procedures to prevent contact with potentially contaminated material.

5.4. INSTITUTIONAL CONTROLS (FUTURE LAND USE CONTROLS)

Long-term conditions related to future use of the Site will be placed on the RADWP approval, NFA, and COC. These conditions are anticipated to include the following:

- A restriction prohibiting the use of groundwater for any purpose at the Site and a requirement to characterize, containerize, and properly dispose of groundwater in the event of deep excavations encountering groundwater. The entire Tradepoint Atlantic property will be subject to the groundwater use restriction.
- Notice to the MDE at least 30 days prior to any future soil disturbances that are expected to breach the approved capping remedy (i.e., through the pavement cap or marker fabric in landscaped areas).
- Notice to the USEPA at least 30 days prior to any future soil disturbances that are expected to breach the approved capping remedy, only if the proposed duration of

intrusive activity would exceed the allowable exposure duration determined in the SLRA and the contractor will not use the modified Level D PPE specified in the approved SOP.

- Requirement for a HASP in the event of any future excavations at the Site.
- Complete appropriate characterization and disposal of any future material excavated at the Site in accordance with applicable local, state and federal requirements.
- Implementation of inspection procedures and maintenance of the containment remedies.

The responsible party will file the above deed restrictions as defined by the MDE-VCP in the NFA and COC. The Tenant will be required to sign onto the Environmental Covenant with restriction in the NFA. Tradepoint Atlantic will notify the Tenant of this requirement and will provide MDE with contact information for the Tenant prior to issuance of the NFA.

5.5. POST REMEDIATION REQUIREMENTS

Post remediation requirements will include compliance with the conditions specified in the NFA, COC, and the deed restrictions recorded for the Site. Deed restrictions will be recorded within 30 days after receipt of the final NFA. In addition, the MDE and USEPA will be provided with a written notice of any future excavations (as applicable) in accordance with the requirements given in Section 5.4. Written notice of planned excavation activities will include the proposed date(s) for the excavation, location of the excavation, health and safety protocols (as required), clean fill source (as required), and proposed characterization and disposal requirements.

Additional requirements will include inspection procedures and maintenance of the containment remedies to minimize degradation which could lead to future exposures. An Operations and Maintenance Plan (O&M Plan) will be submitted in the future for MDE approval, and will include long-term inspection and maintenance requirements for the capping remedies installed at the Site. The responsible party will perform cap inspections, perform maintenance of the cap, and retain cap inspection records, as required by the O&M Plan.

5.6. CONSTRUCTION OVERSIGHT

Construction Oversight by an EP will ensure and document that the project is built as designed and appropriate environmental and safety protocols are followed. Upon completion, the EP will certify that the project is constructed in accordance with this RADWP.

The EP will monitor all soil excavation/trenching activities for signs of potential contamination that may not have been previously identified. In particular, soils will be monitored with a hand-held PID for potential VOCs, and will also be visually inspected for staining, petroleum waste materials, or other indications of significant contamination. If screening of excavated materials by the EP indicates the presence of conditions of potential concern (i.e., sustained PID readings greater than 10 ppm, visual staining, unsuitable waste materials, etc.), such materials shall be

segregated for additional sampling and special management (as described in Section 5.1.2; Soil Excavation and Utility Trenching). The EP will also perform routine periodic breathing zone monitoring and PPE spot checks during ground intrusive activities. The EP will also inspect any water that collects in the excavations/trenches on an as-needed basis to coordinate appropriate sampling prior to disposal (as described in Section 5.2.2; Dewatering).

Daily inspections, as necessary, will be performed during general site grading and cap construction activities to verify that appropriate fill materials are being used (as described in Section 5.1.4; Fill), dust monitoring and control measures are being implemented as appropriate (as described in Section 5.1.5; Dust Control), the requirements of the HASP and the PPE SOP are being enforced as applicable (as described in Section 5.3; Health and Safety), and surface engineering controls are being installed with the appropriate minimum thicknesses (as shown on the RADWP attachments). Oversight by an EP will not be required during construction activities which do not have a significant environmental component, such as above-grade building construction.

Records shall be provided by the EP to document:

- Compliance with soil screening requirements
- Proper water management, including documentation of any testing and water disposal
- Observations of construction activities during site grading and cap construction
- Proper cap thickness and construction

6.0 PERMITS, NOTIFICATIONS AND CONTINGENCIES

The participant and their contractors will comply with all local, state, and federal laws and regulations by obtaining any necessary approvals and permits to conduct the activities contained herein. Any permits or permit modifications from State or local authorities will be provided as addenda to this RADWP.

A grading permit is required if the proposed grading disturbs over 5,000 square feet of surface area or over 100 cubic yards of earth. A grading permit is required for any grading activities in any watercourse, floodplain, wetland area, buffers (stream and within 100 feet of tidal water), habitat protection areas or forest buffer areas (includes forest conservation areas). Erosion and Sediment Control Plans will be submitted to, and approved by, the MDE prior to initiation of land disturbance for development.

There are no wetlands identified within the project area and no work will be performed beyond the shoreline so no permits are required from the MDE Water Resources Administration.

Contingency measures will include the following:

1. The MDE will be notified immediately of any previously undiscovered contamination, previously undiscovered storage tanks and other oil-related issues, and citations from regulatory entities related to health and safety practices.
2. Any significant change to the implementation schedule will be noted in the progress reports to MDE.
3. General health and safety controls (level D protection) would be adequate to mitigate the potential risk to Construction Workers during development for a duration of up to 95 exposure days in EU1 and 55 exposure days in EU2. However, certain activities at the Site are anticipated to exceed these allowable durations. Therefore, additional site-specific health and safety requirements are warranted to be protective of workers. Upgraded PPE beyond standard Level D protection will be used for the entire scope of intrusive work covered by this RADWP as a protective measure to ensure that there are no unacceptable exposures for Construction Workers during project implementation. The modified Level D PPE requirements which will be applied during this project, including specific PPE details, planning, tracking/supervision, enforcement, and documentation, are outlined in the PPE SOP provided as **Appendix E**. If it is not possible to implement the PPE SOP as provided, the agencies will be notified and a RADWP Addendum will be submitted which details procedures to be undertaken to mitigate the potential risk to Construction Workers.

7.0 IMPLEMENTATION SCHEDULE

Progress reports will be submitted to the MDE on a quarterly basis. Each quarterly progress report will include, at a minimum, a discussion of the following information regarding tasks completed during the specified quarter:

- Development Progress
- Dust Monitoring
- Water Management
- Soil Management (imported materials, screening, stockpiling)
- Soil Sampling and Disposal
- Notable Occurrences (if applicable)
- Additional Associated Work (if applicable)

The proposed implementation schedule is shown below:

<u>Task</u>	<u>Proposed Completion Date</u>
Anticipated RADWP Approval(s)	February 6, 2019 (approved to proceed with work)
	March 27, 2020 (final RADWP approval)


<u>Task</u>	<u>Proposed Completion Date</u>
Well Abandonment	November 2018


<u>Task</u>	<u>Proposed Completion Date</u>
Erosion and Sediment Control Installation	February 2019
Utility Installations:	
Domestic Water/Fire Loop	March 2019 (start)
Sanitary	March 2019 (start)
Stormwater	March 2019 (start)
Building Pad Construction	March 2019
Parking Area Grading Completion	October 2019
Shell Completion	Fall 2019

Submittal of Development Completion Report/ Notice of Completion of Remedial Actions*	June 2020
Request for a NFA from the MDE	July 2020
Recordation of institutional controls in the land records office of Baltimore County	Within 30 days of receiving the approval of NFA from the MDE
Submit proof of recordation with Baltimore County	Upon receipt from Baltimore County

*Notice of Completion of Remedial Actions shall be prepared by Professional Engineer registered in Maryland and submitted with the Development Completion Report to certify that the work is consistent with the requirements of this RADWP and the Site is suitable for occupancy and use.

FIGURES

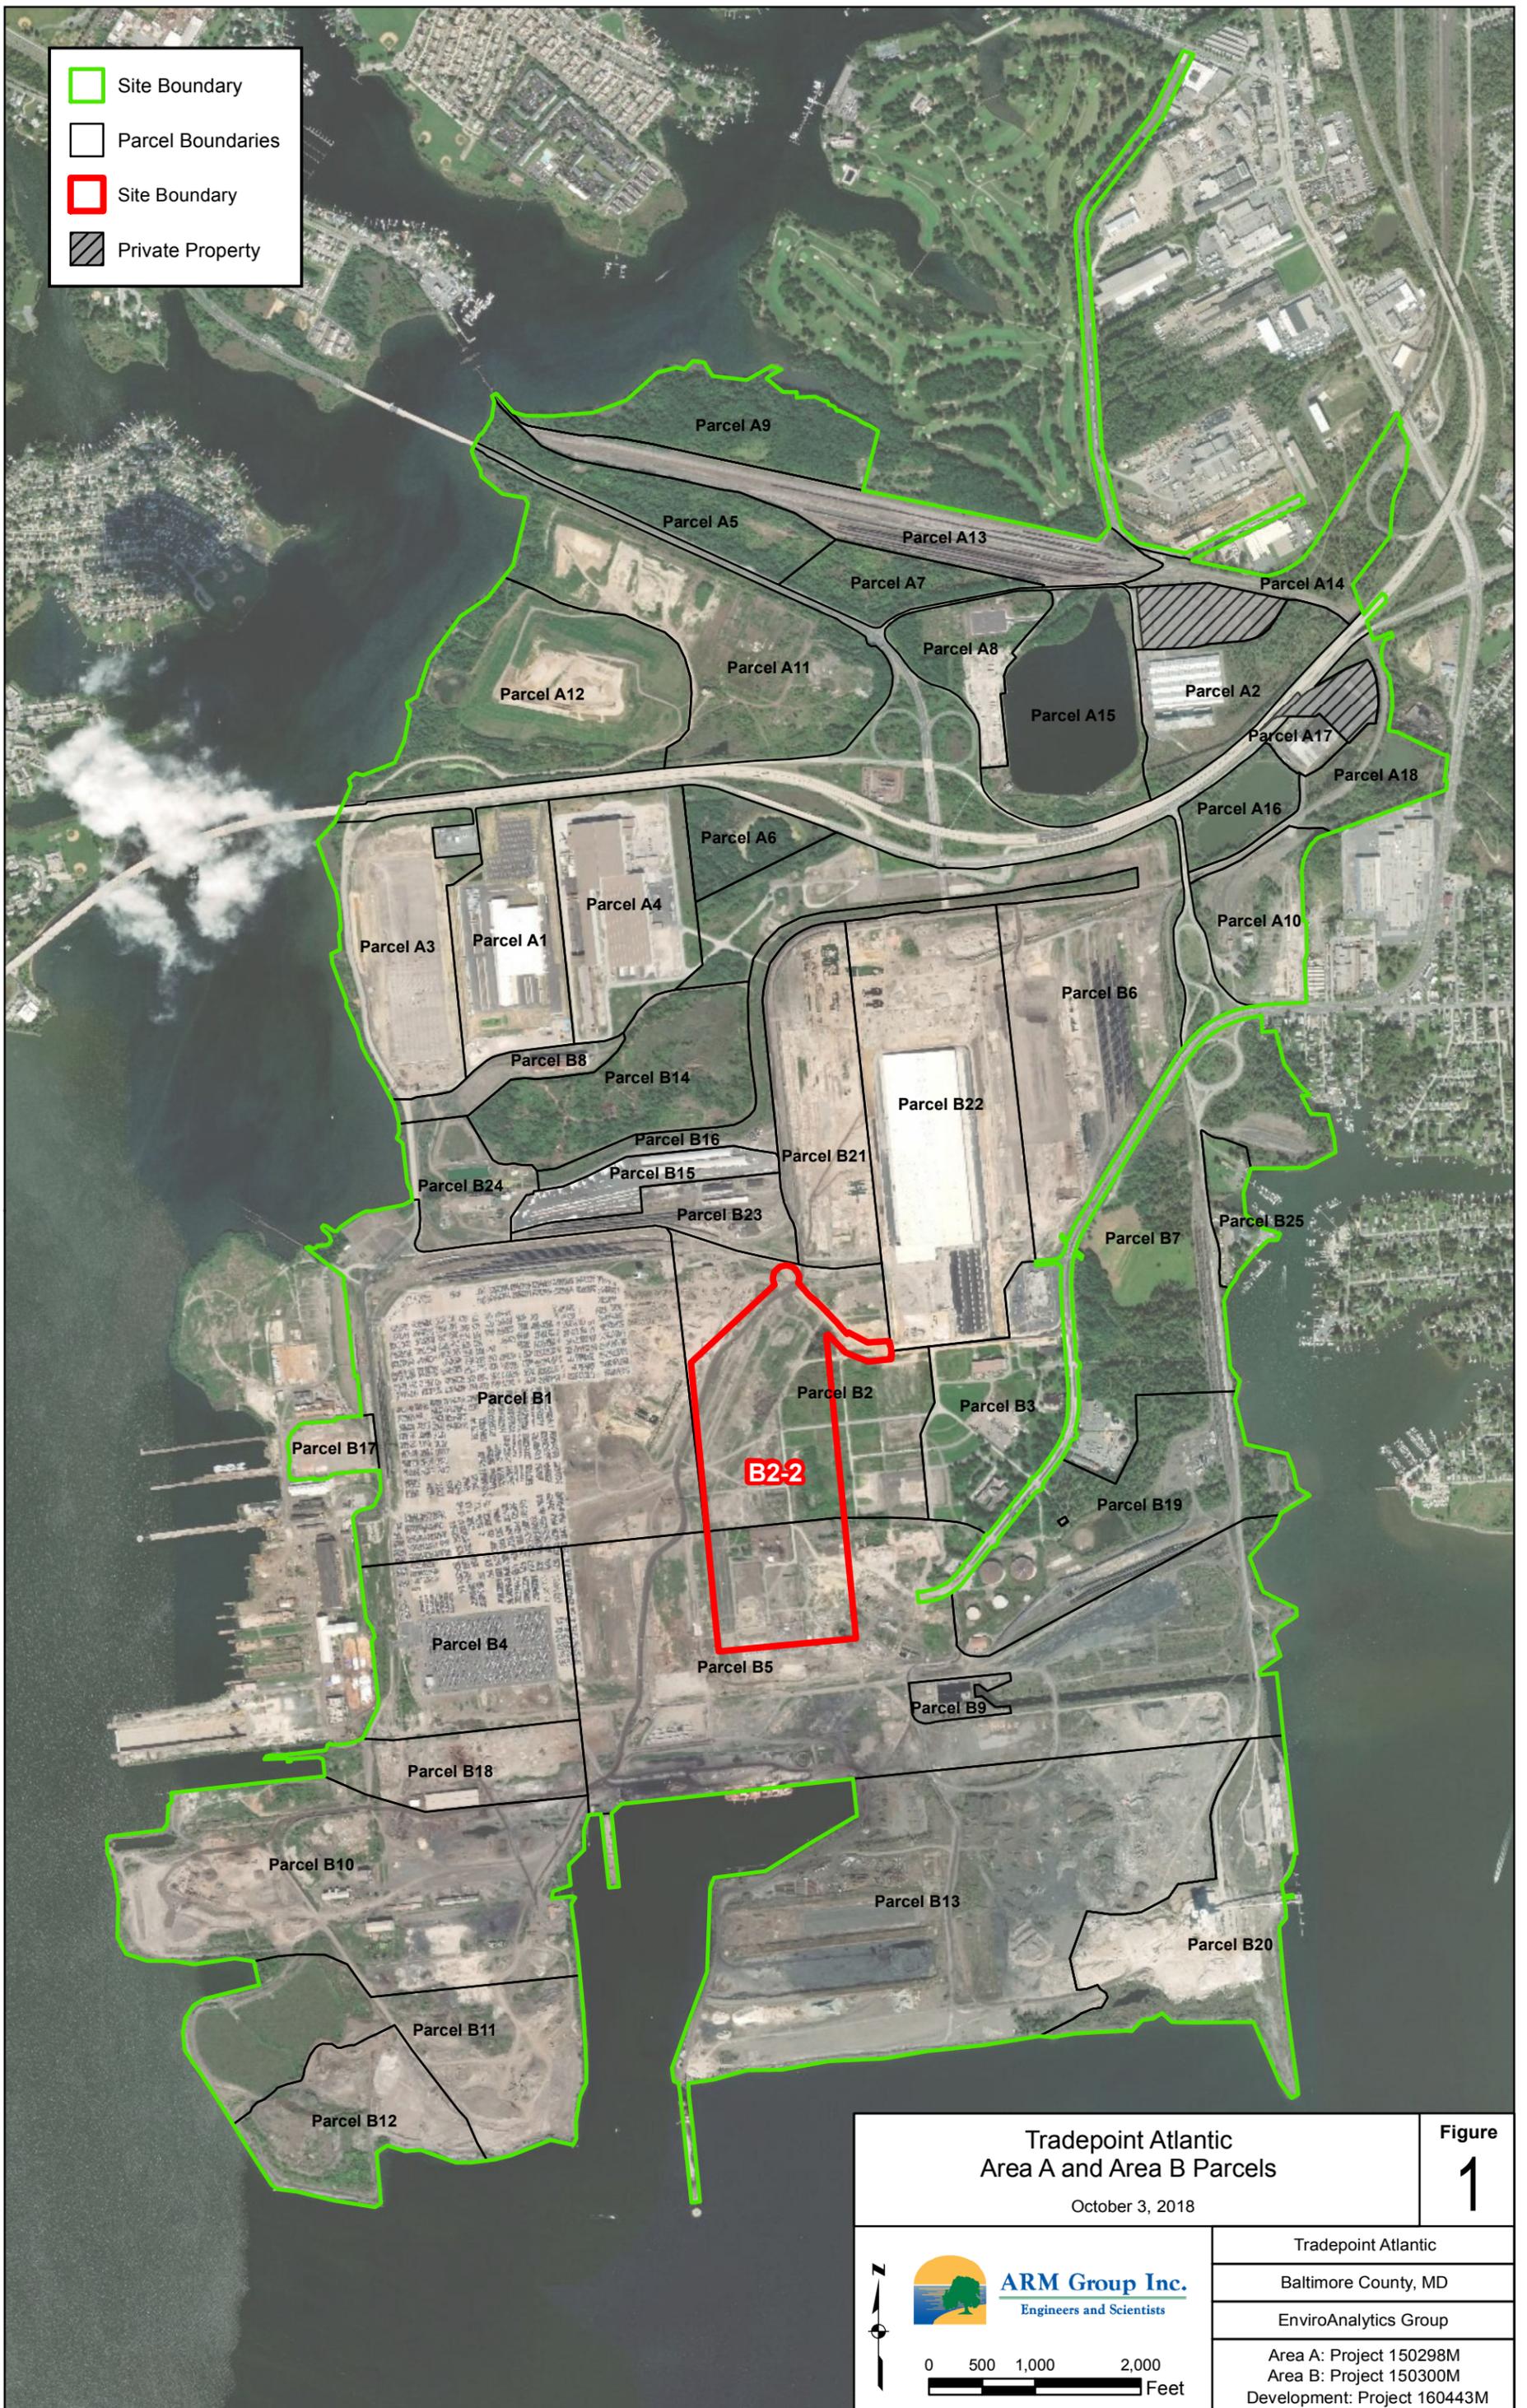

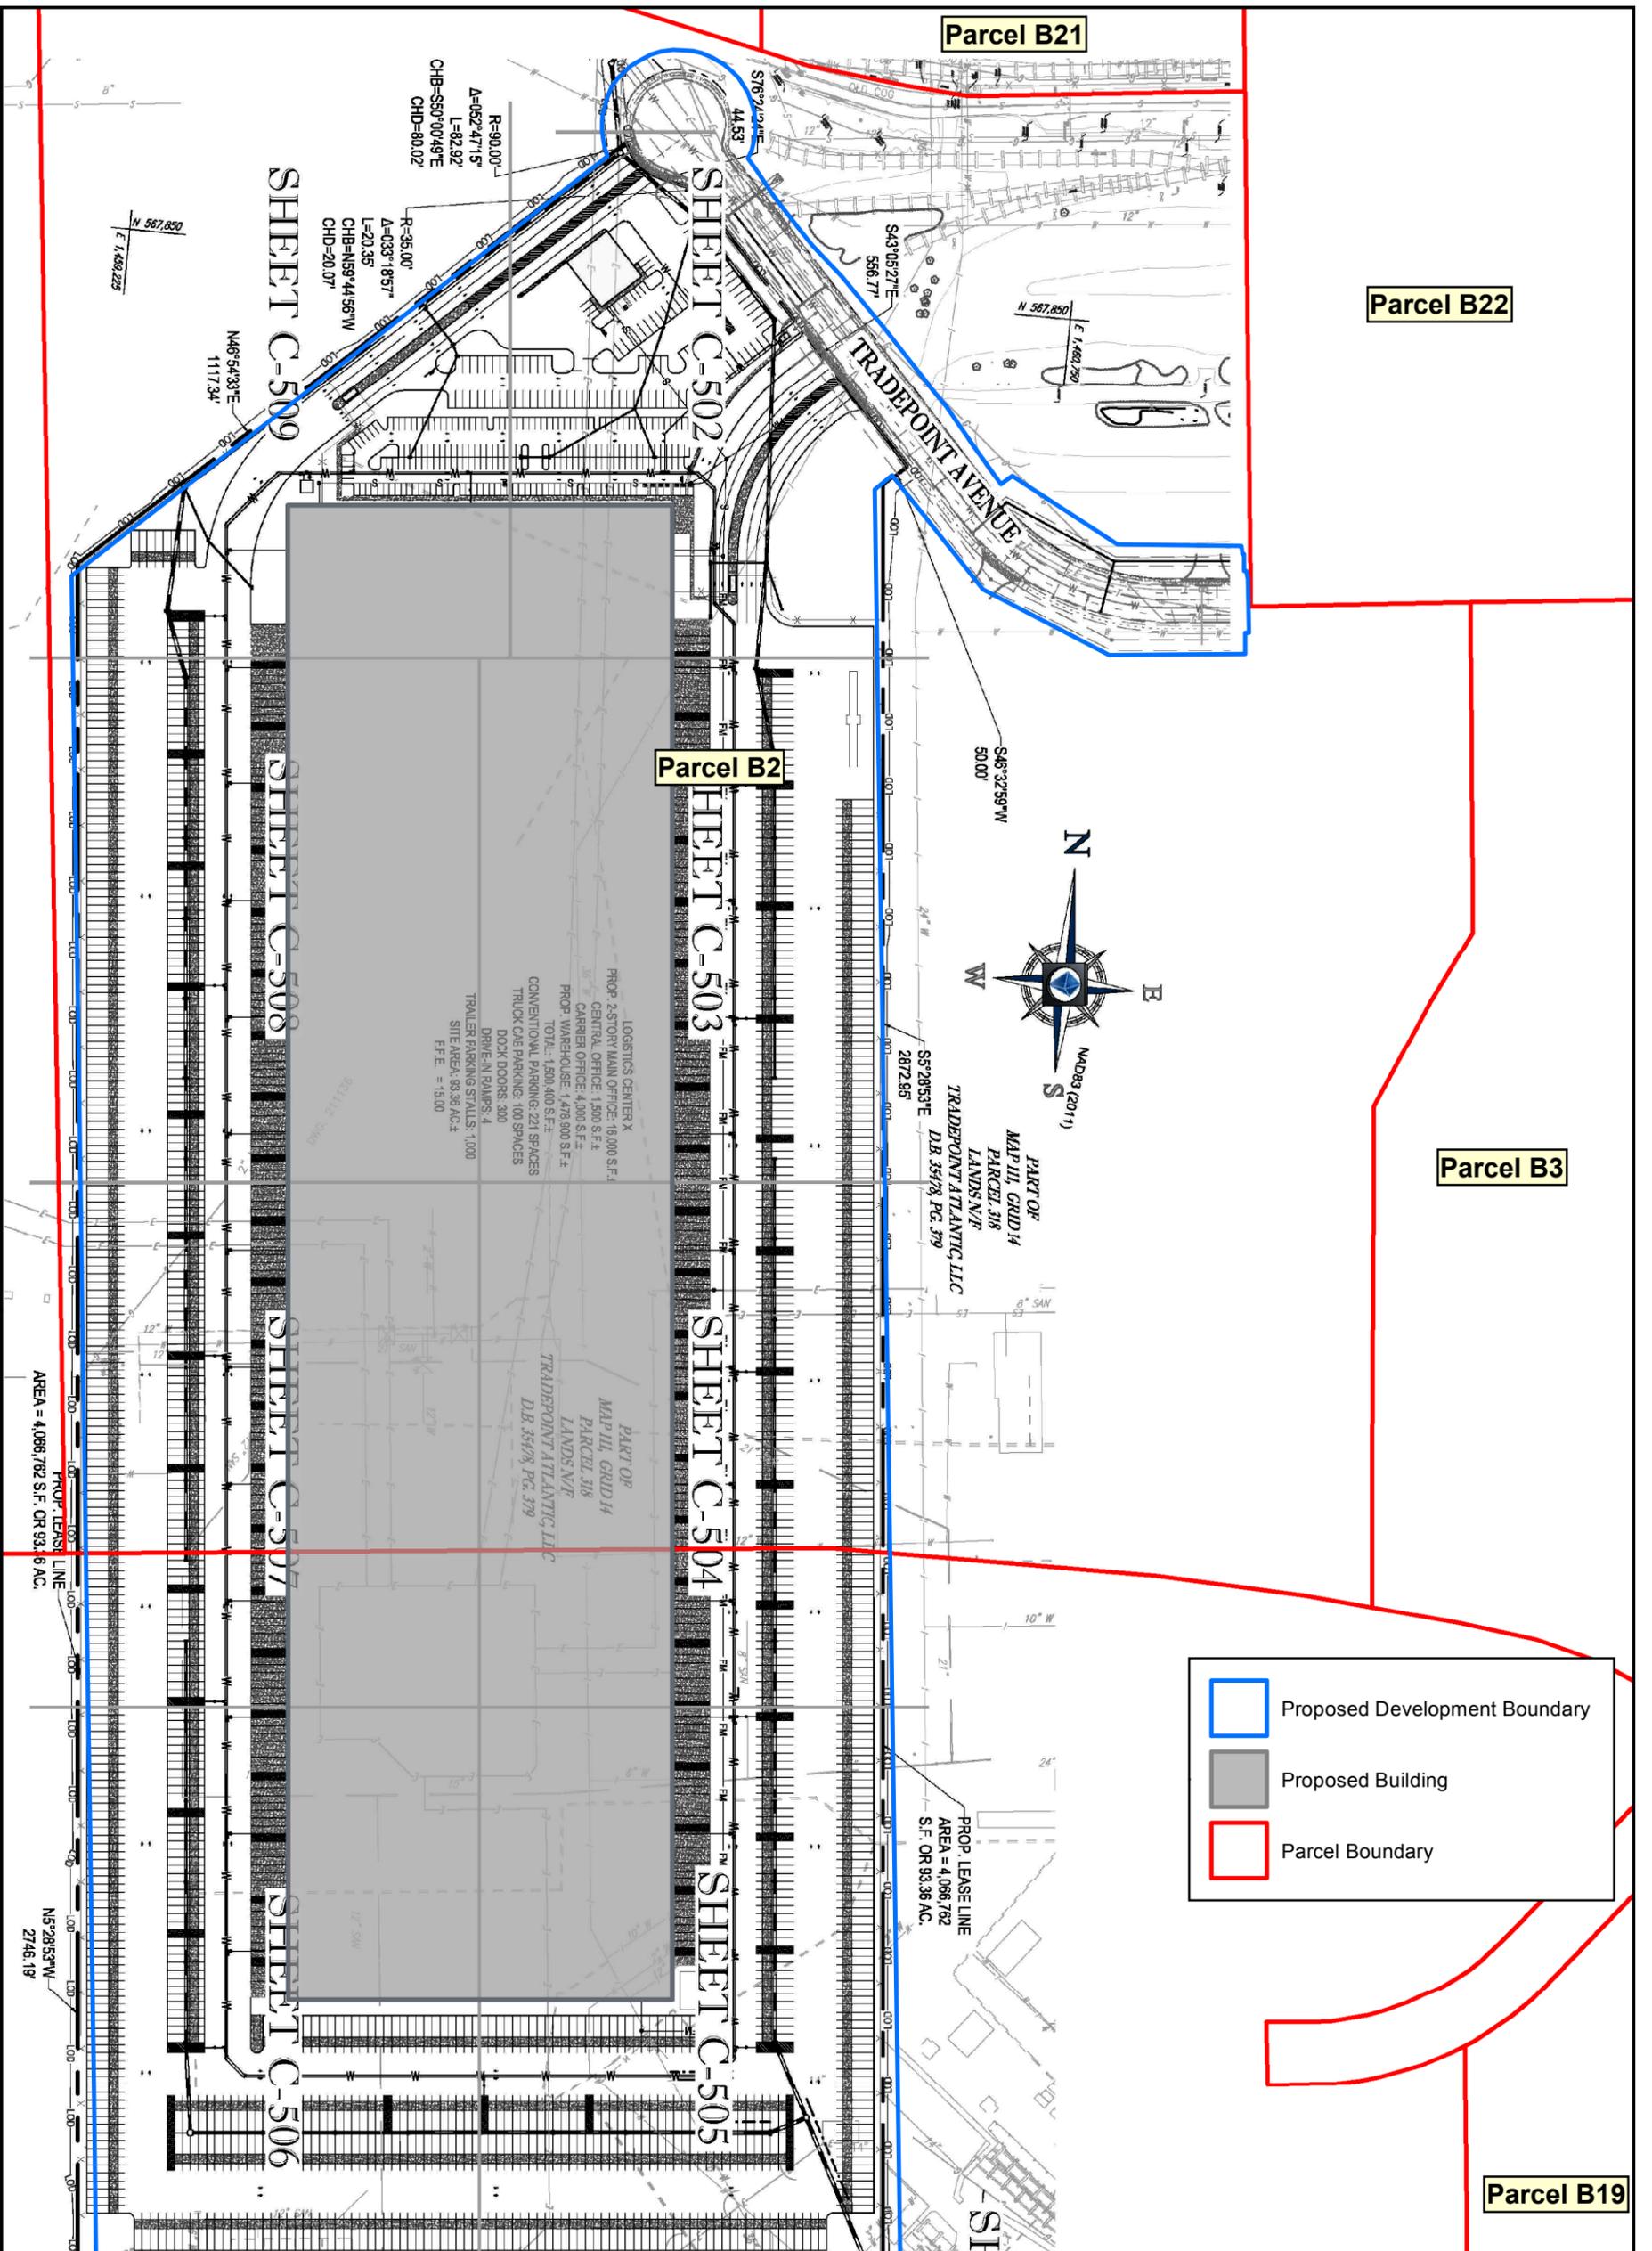

Sub-Parcel B2-2 - Logistics Center X
Development Area


July 1, 2019

Figure
2

ARM Group Inc.
Engineers and Scientists

0 100 200 400
Feet

Tradepoint Atlantic
Baltimore County, MD
EnviroAnalytics Group
ARM Project 160443M-16

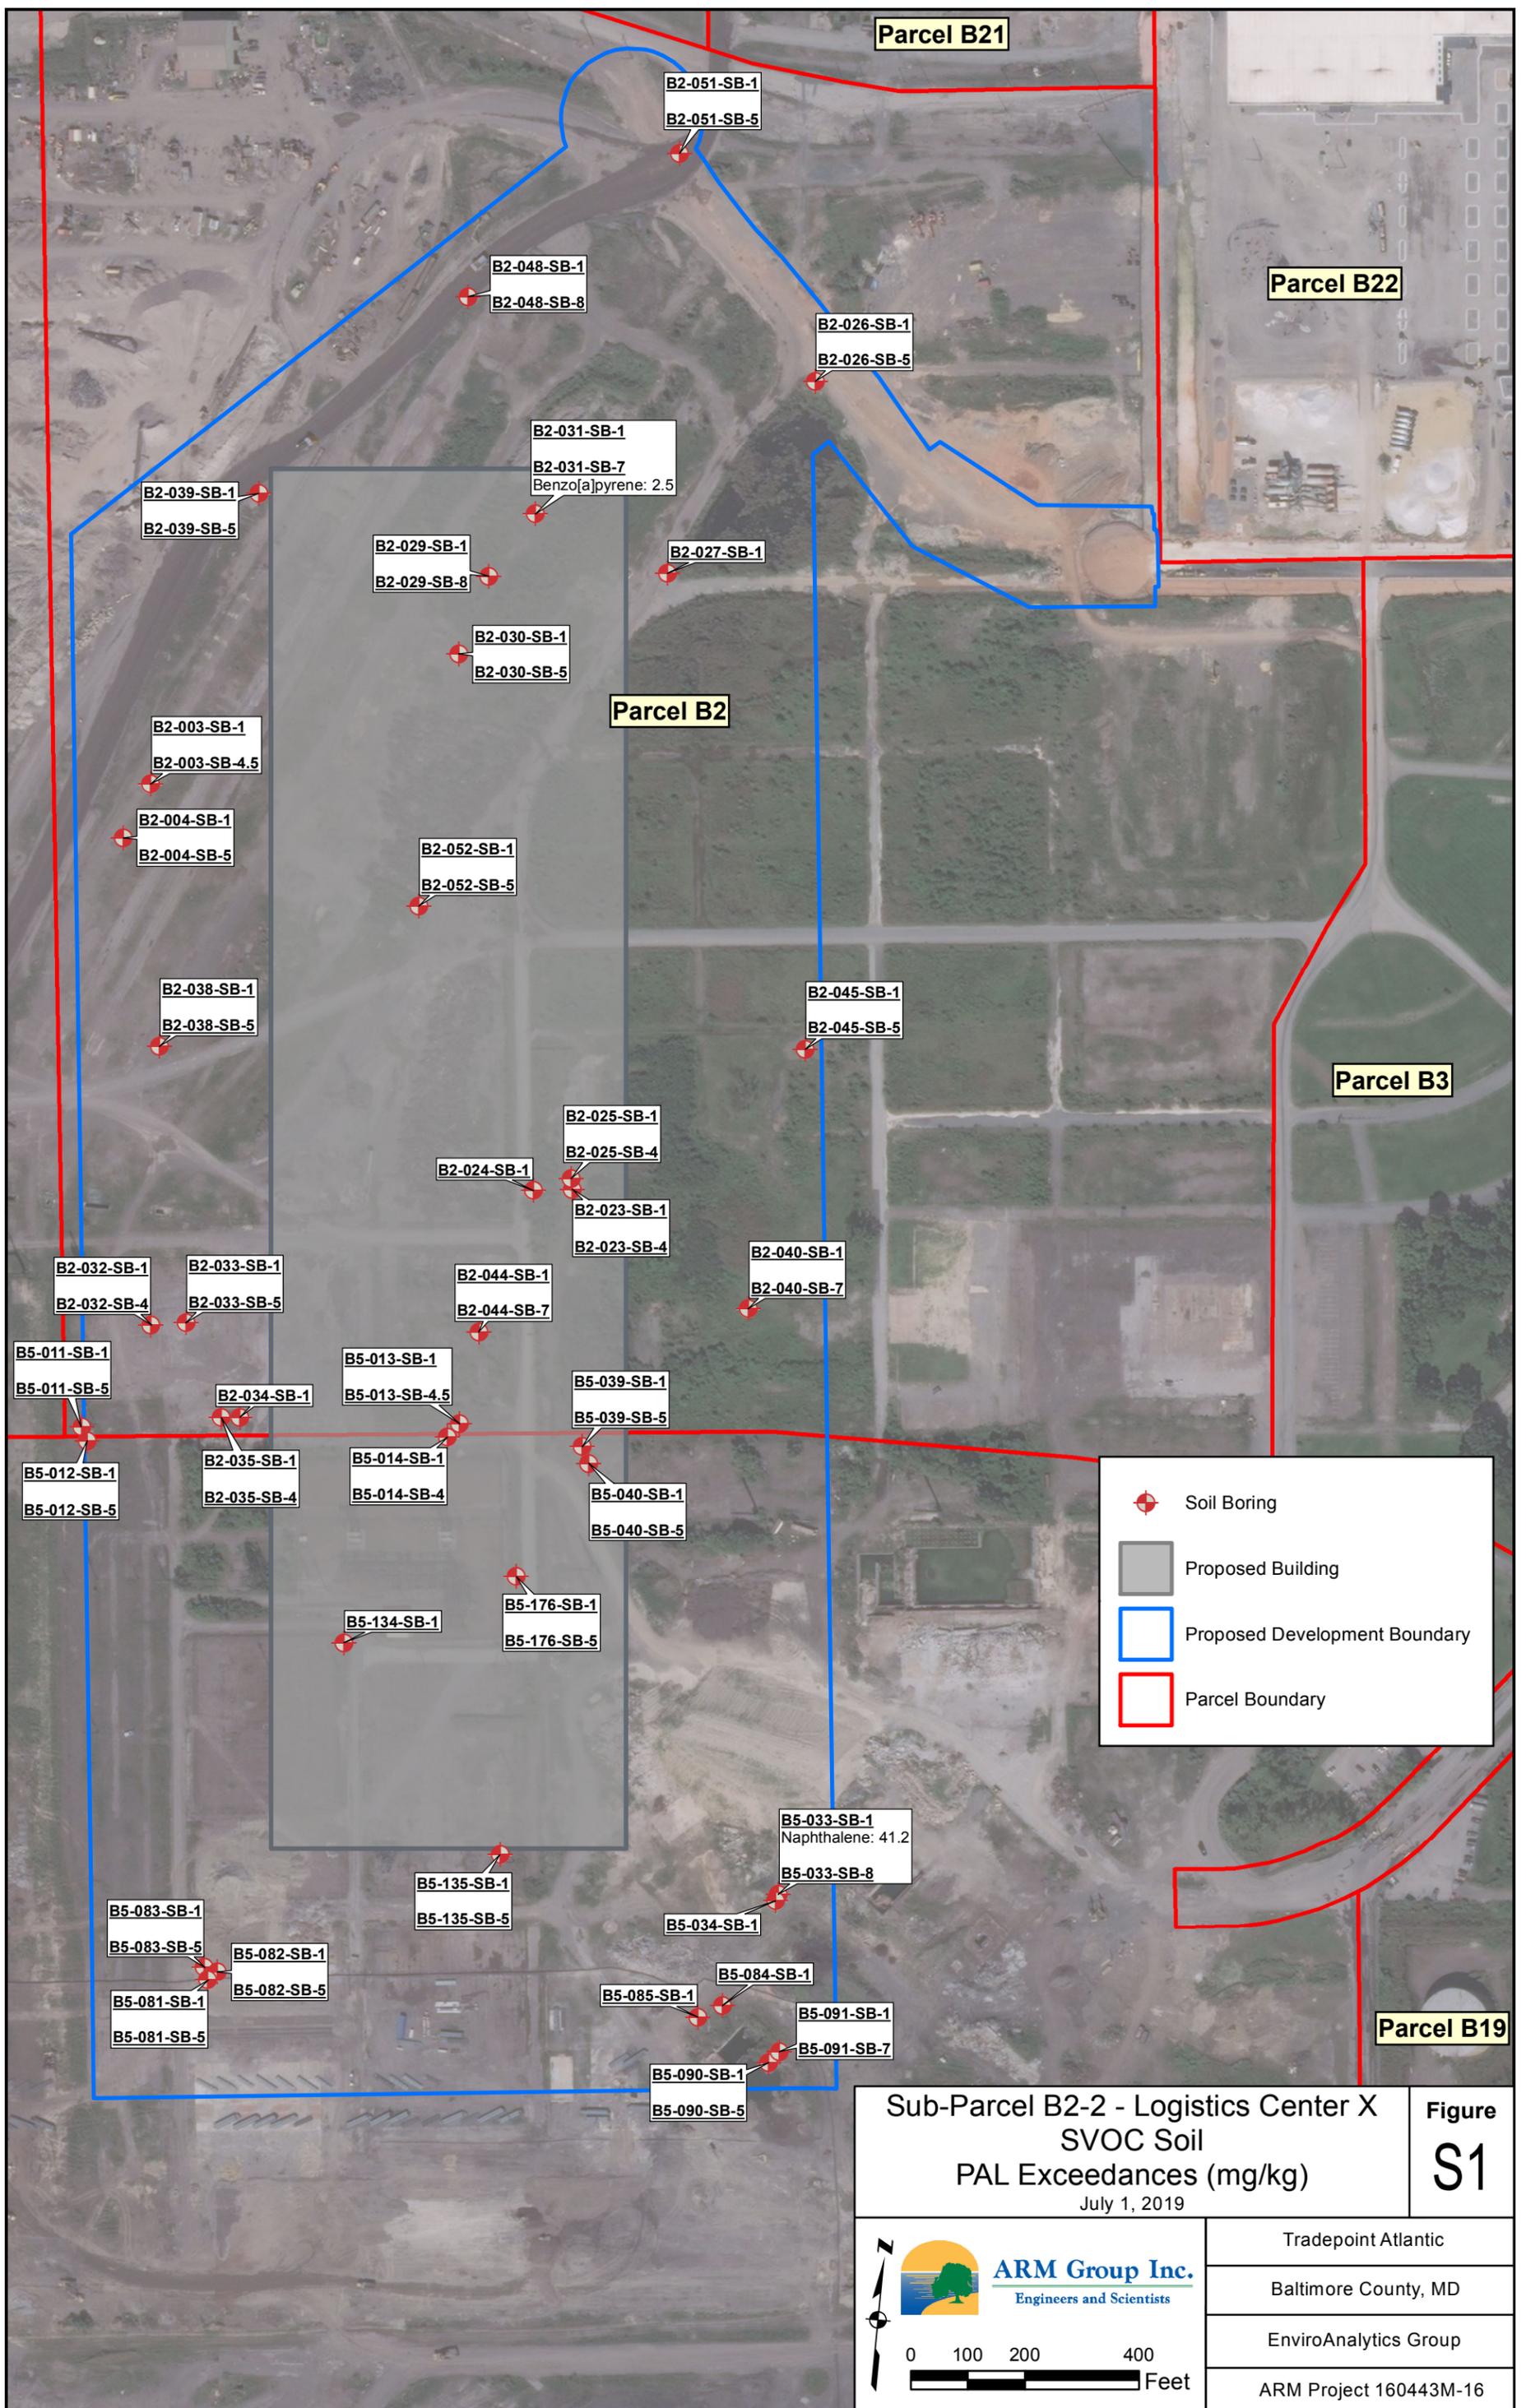

Sub-Parcel B2-2 - Logistics Center X
 SVOC Soil
 PAL Exceedances (mg/kg)
 July 1, 2019


Figure
S1



ARM Group Inc.
 Engineers and Scientists

0 100 200 400
 Feet

Tradepoint Atlantic
Baltimore County, MD
EnviroAnalytics Group
ARM Project 160443M-16

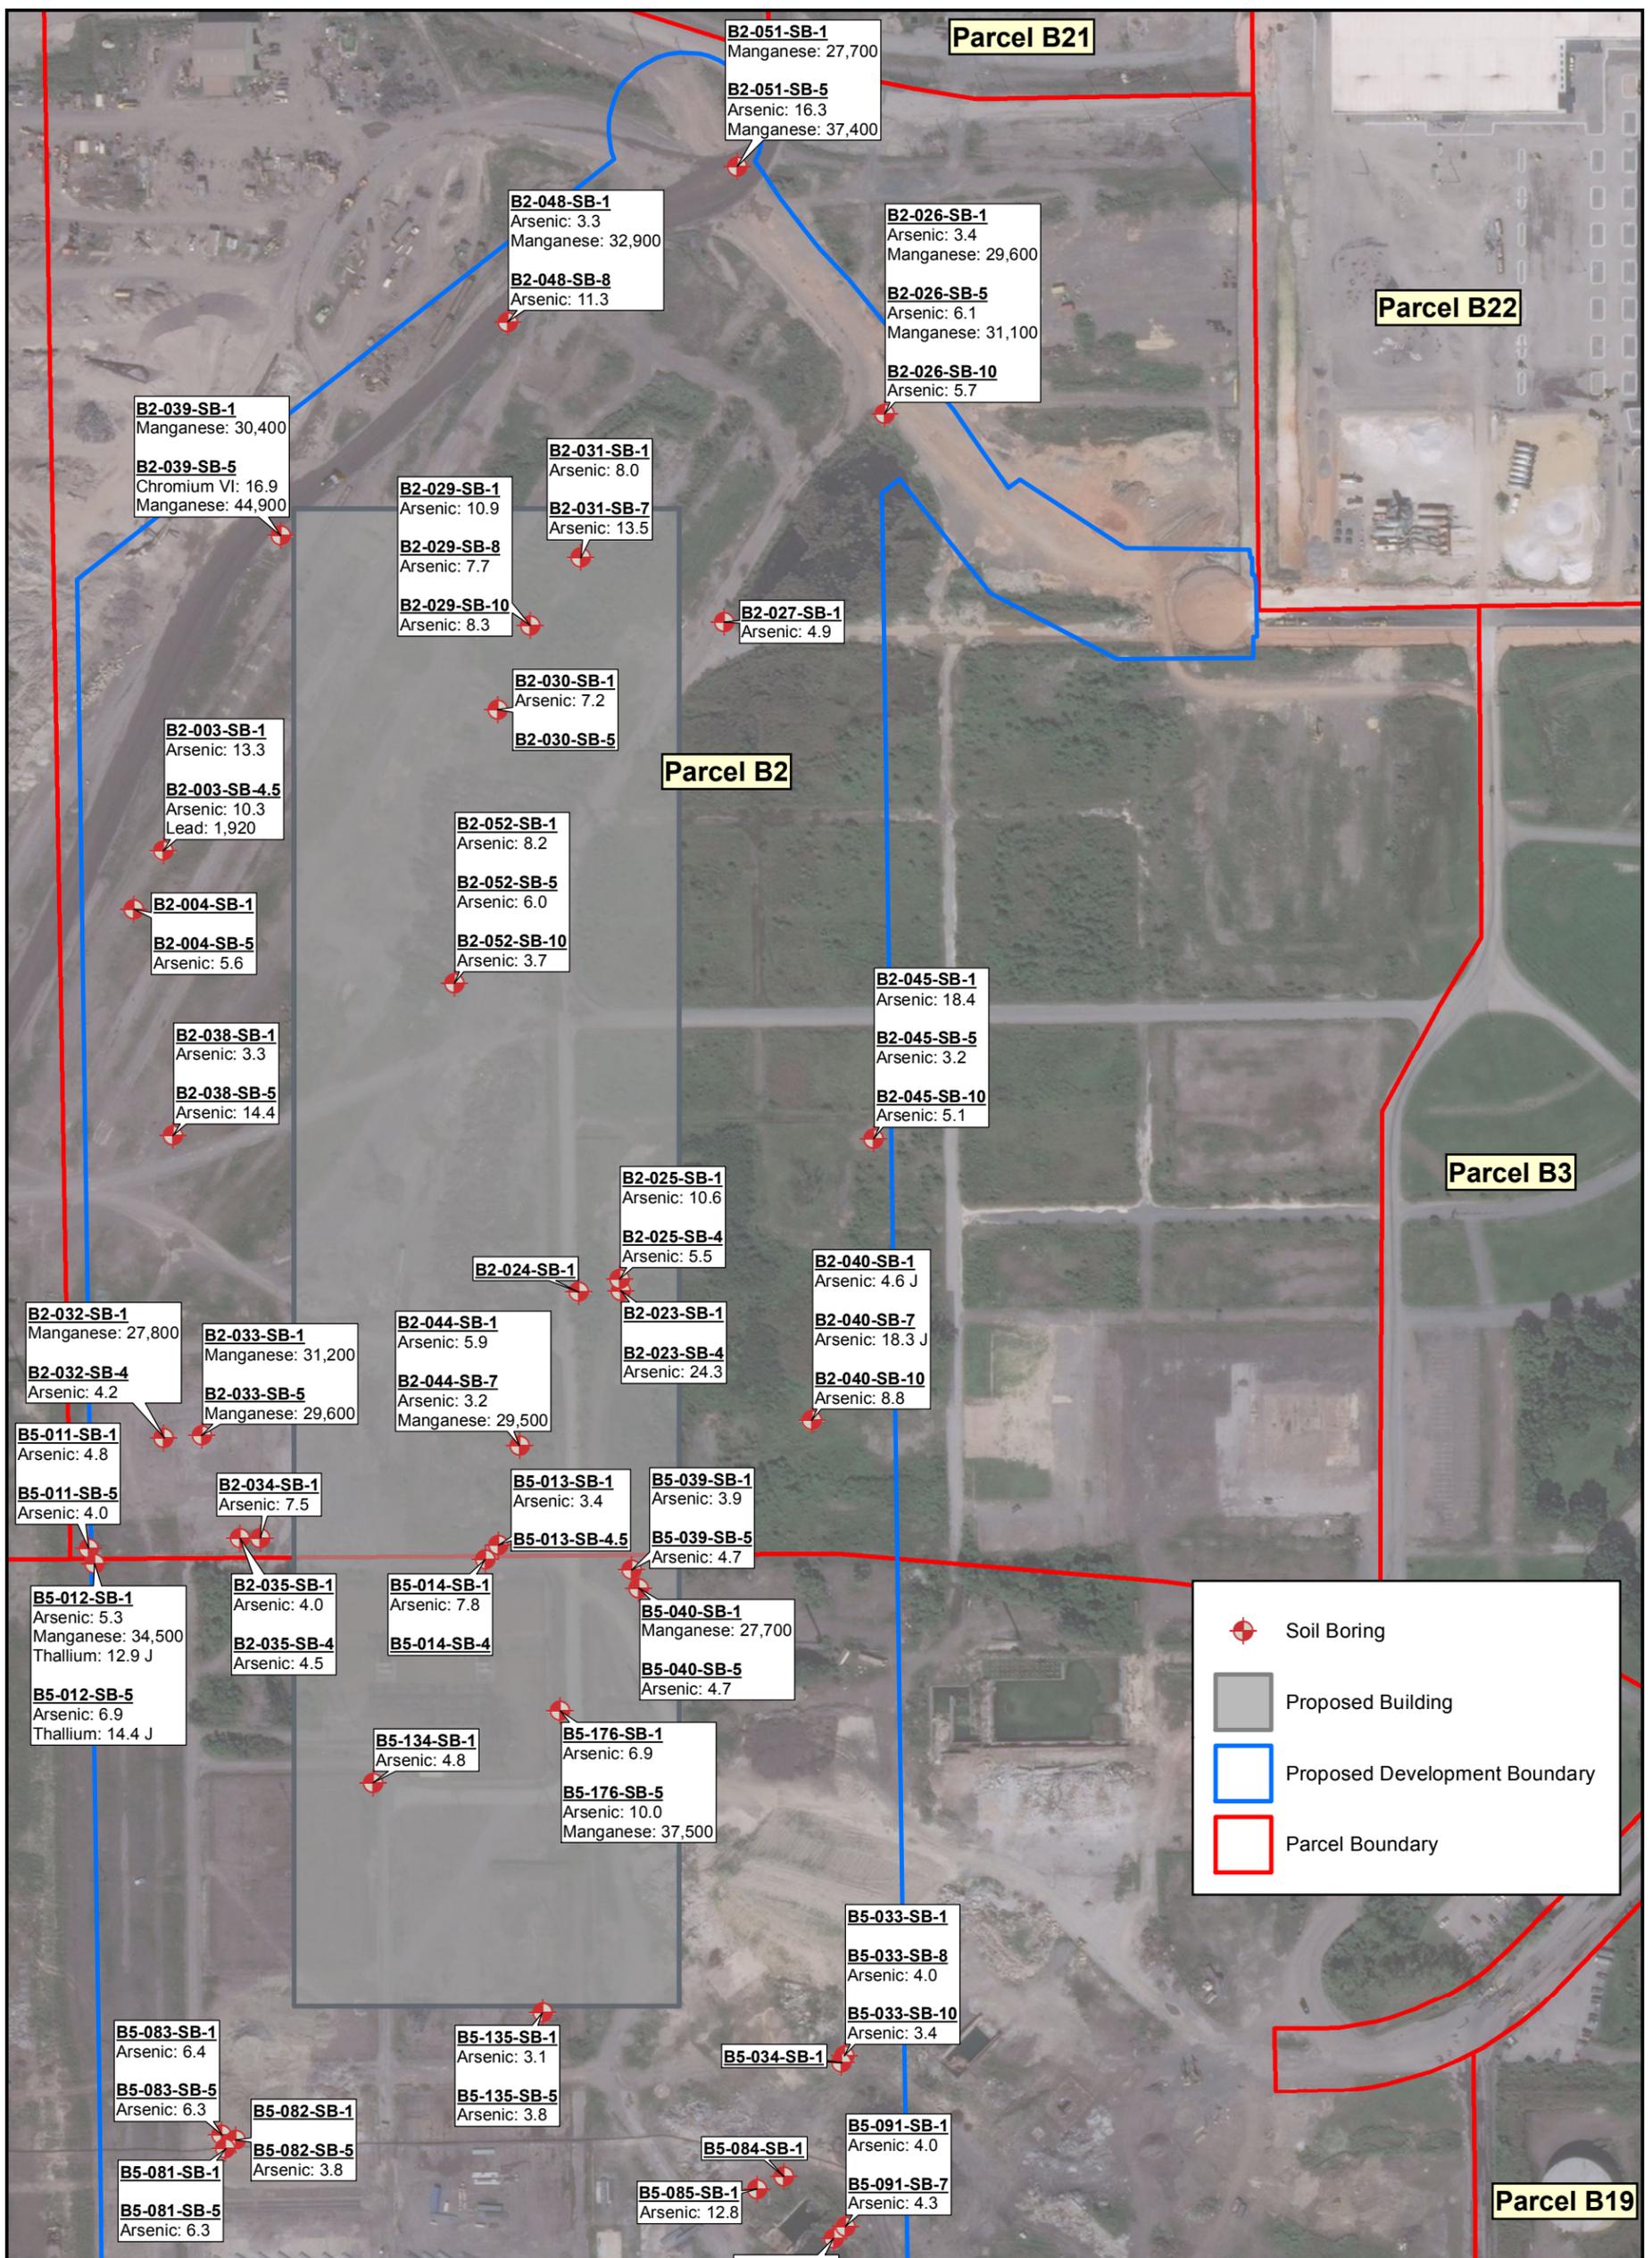


Sub-Parcel B2-2 - Logistics Center X
Inorganic Soil
PAL Exceedances (mg/kg)
 July 1, 2019


Figure SH


Tradepoint Atlantic
 Baltimore County, MD
 EnviroAnalytics Group
 ARM Project 160443M-16

ARM Group Inc.
 Engineers and Scientists

0 100 200 400 Feet

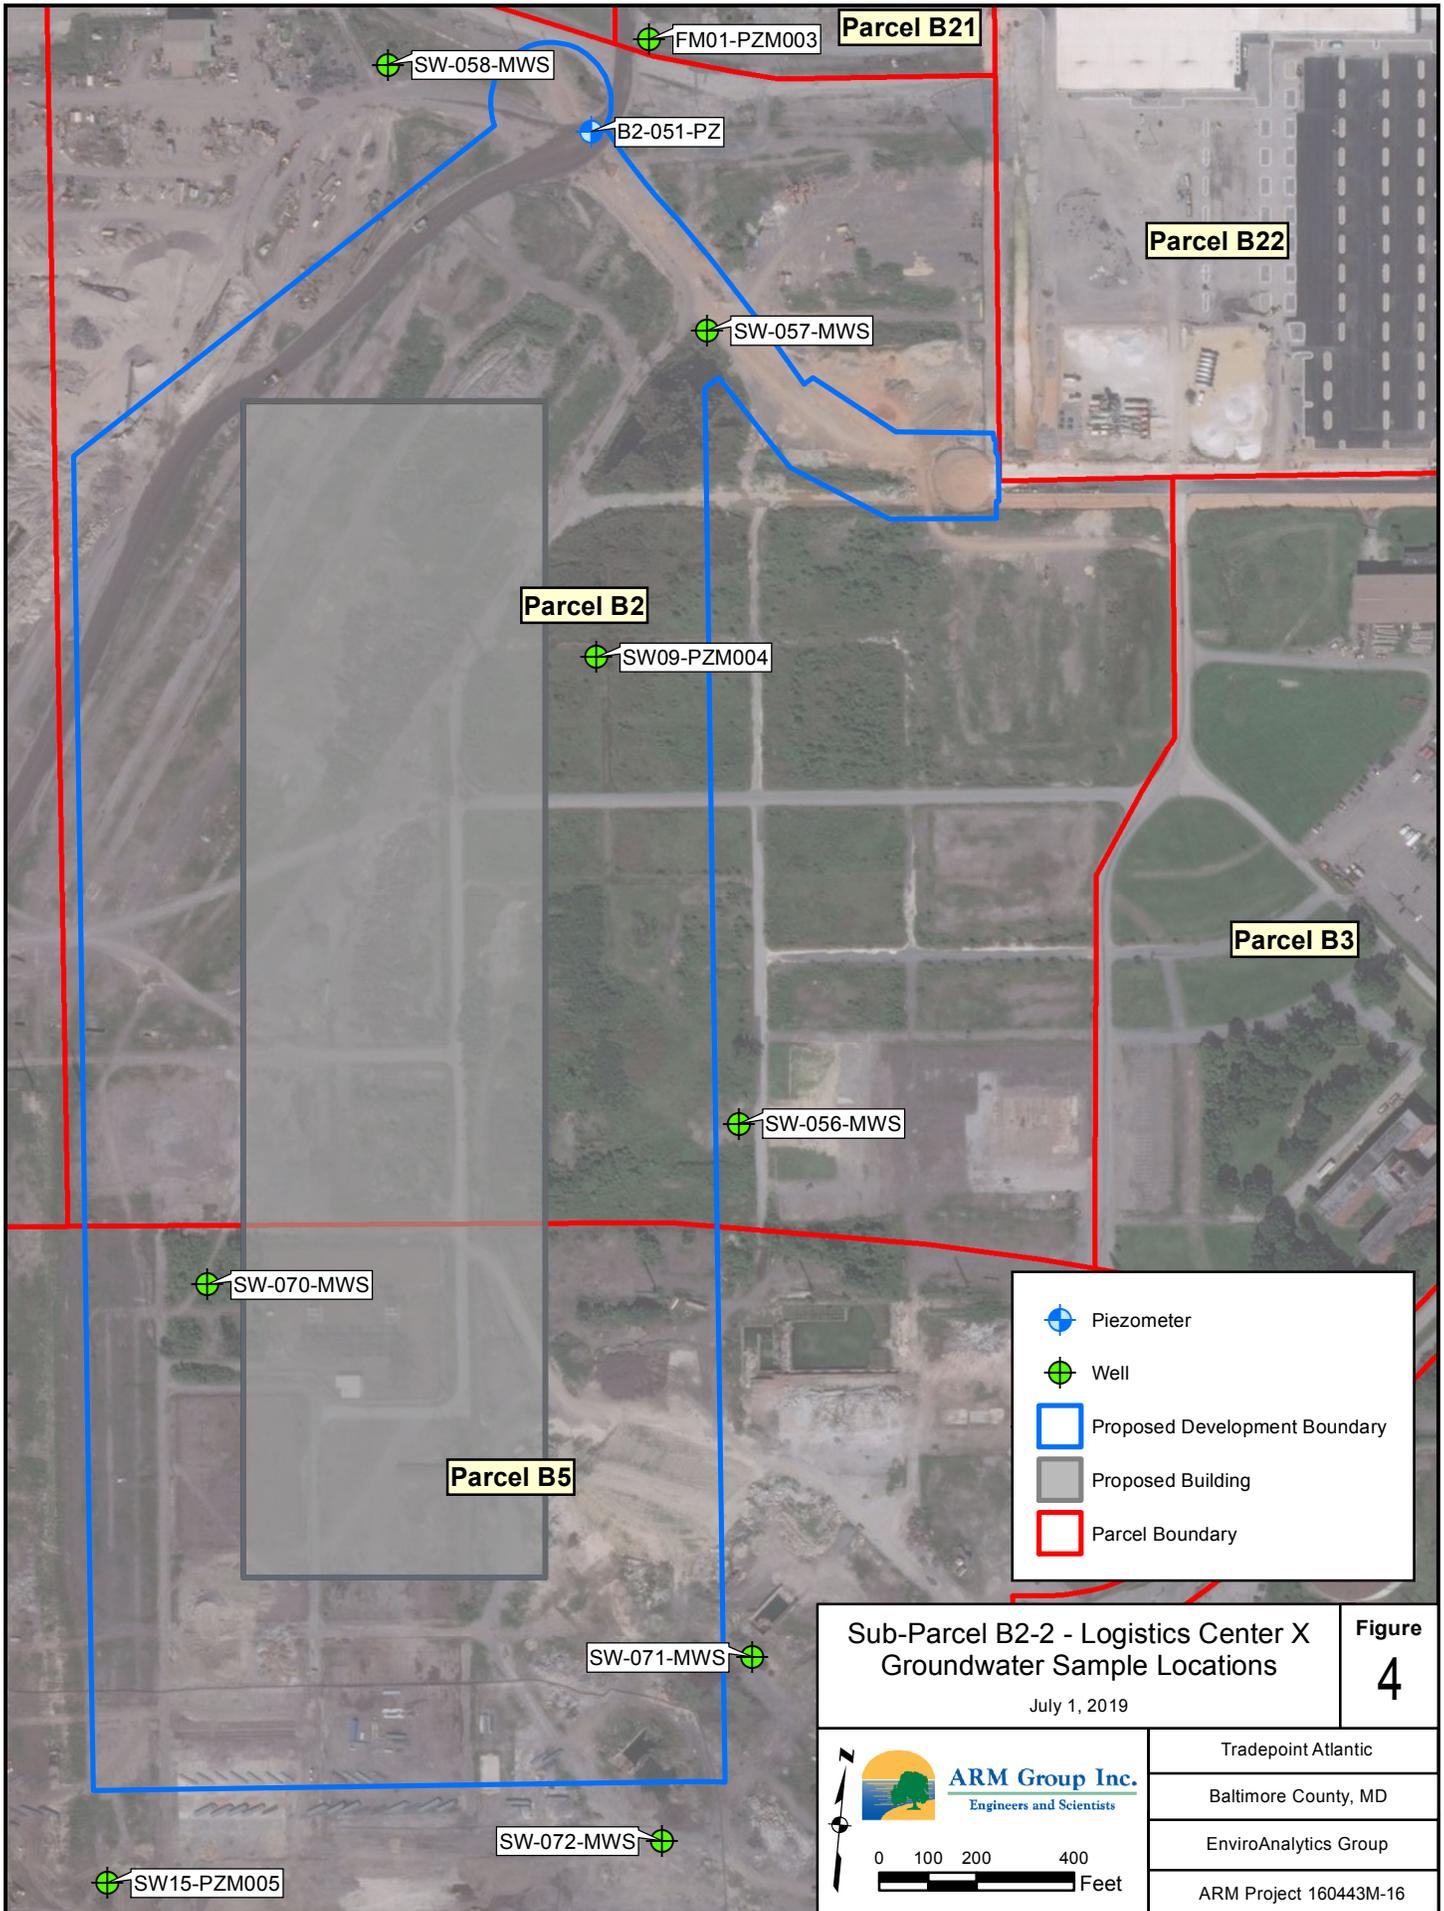

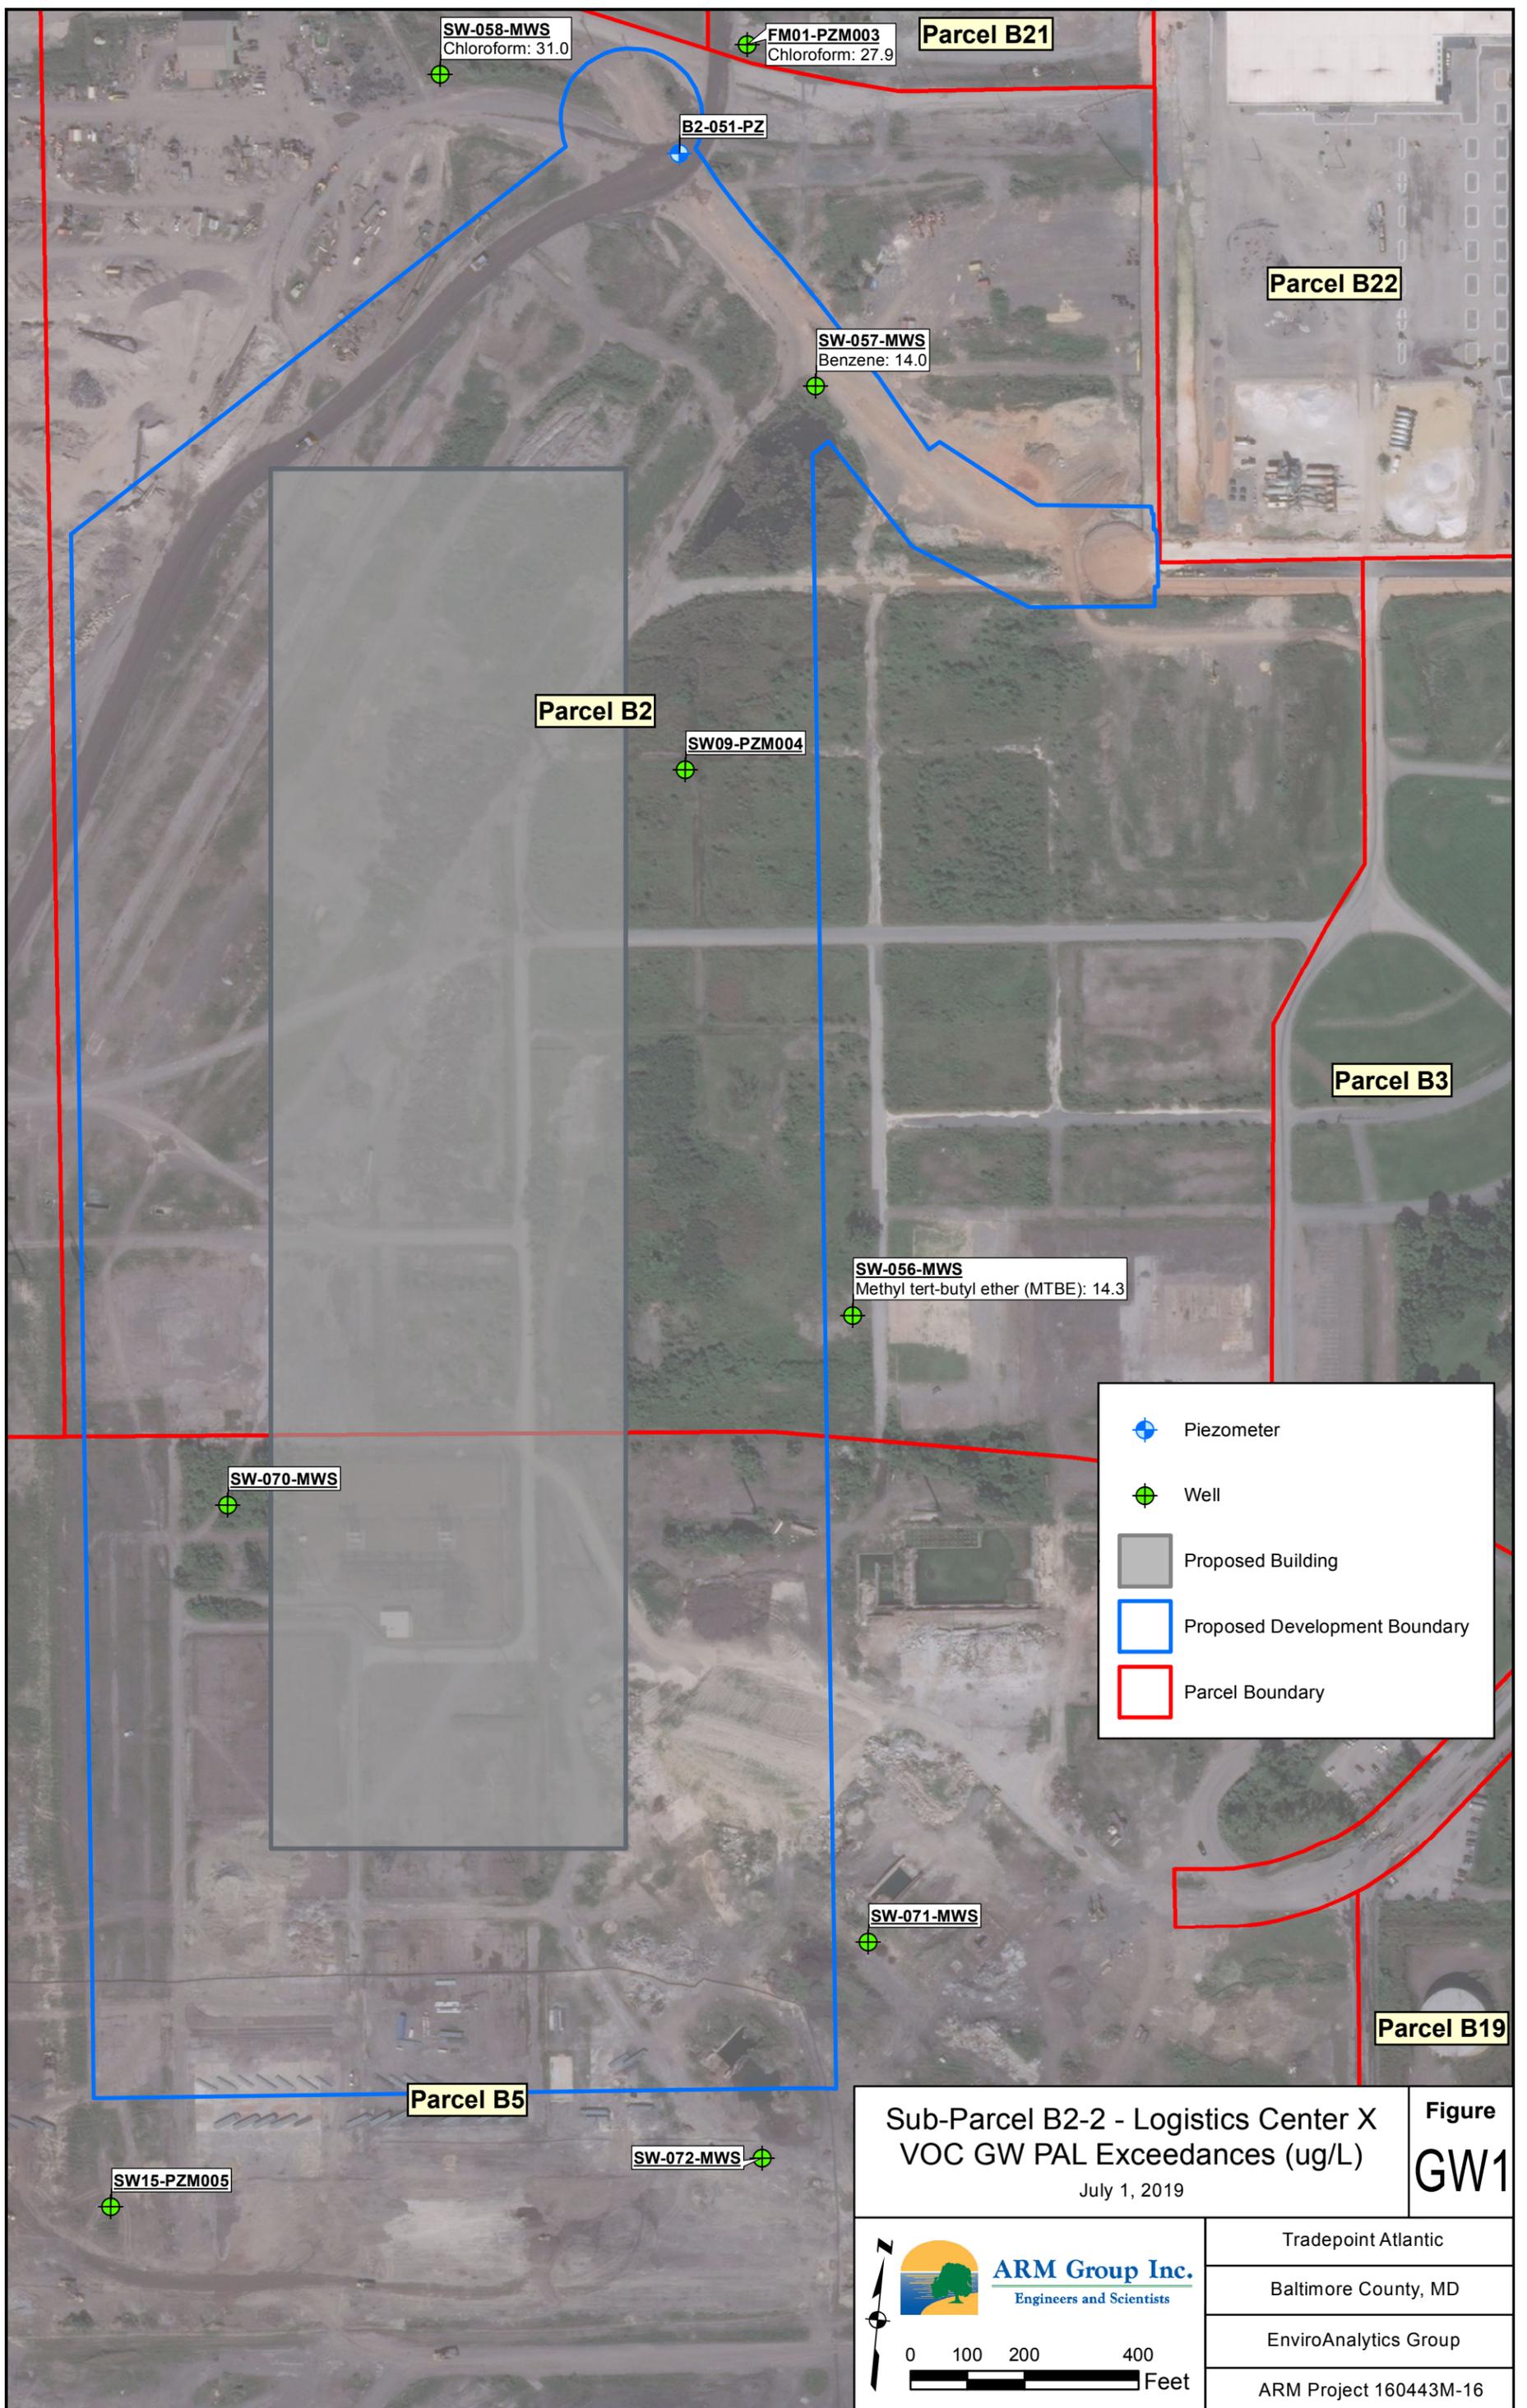

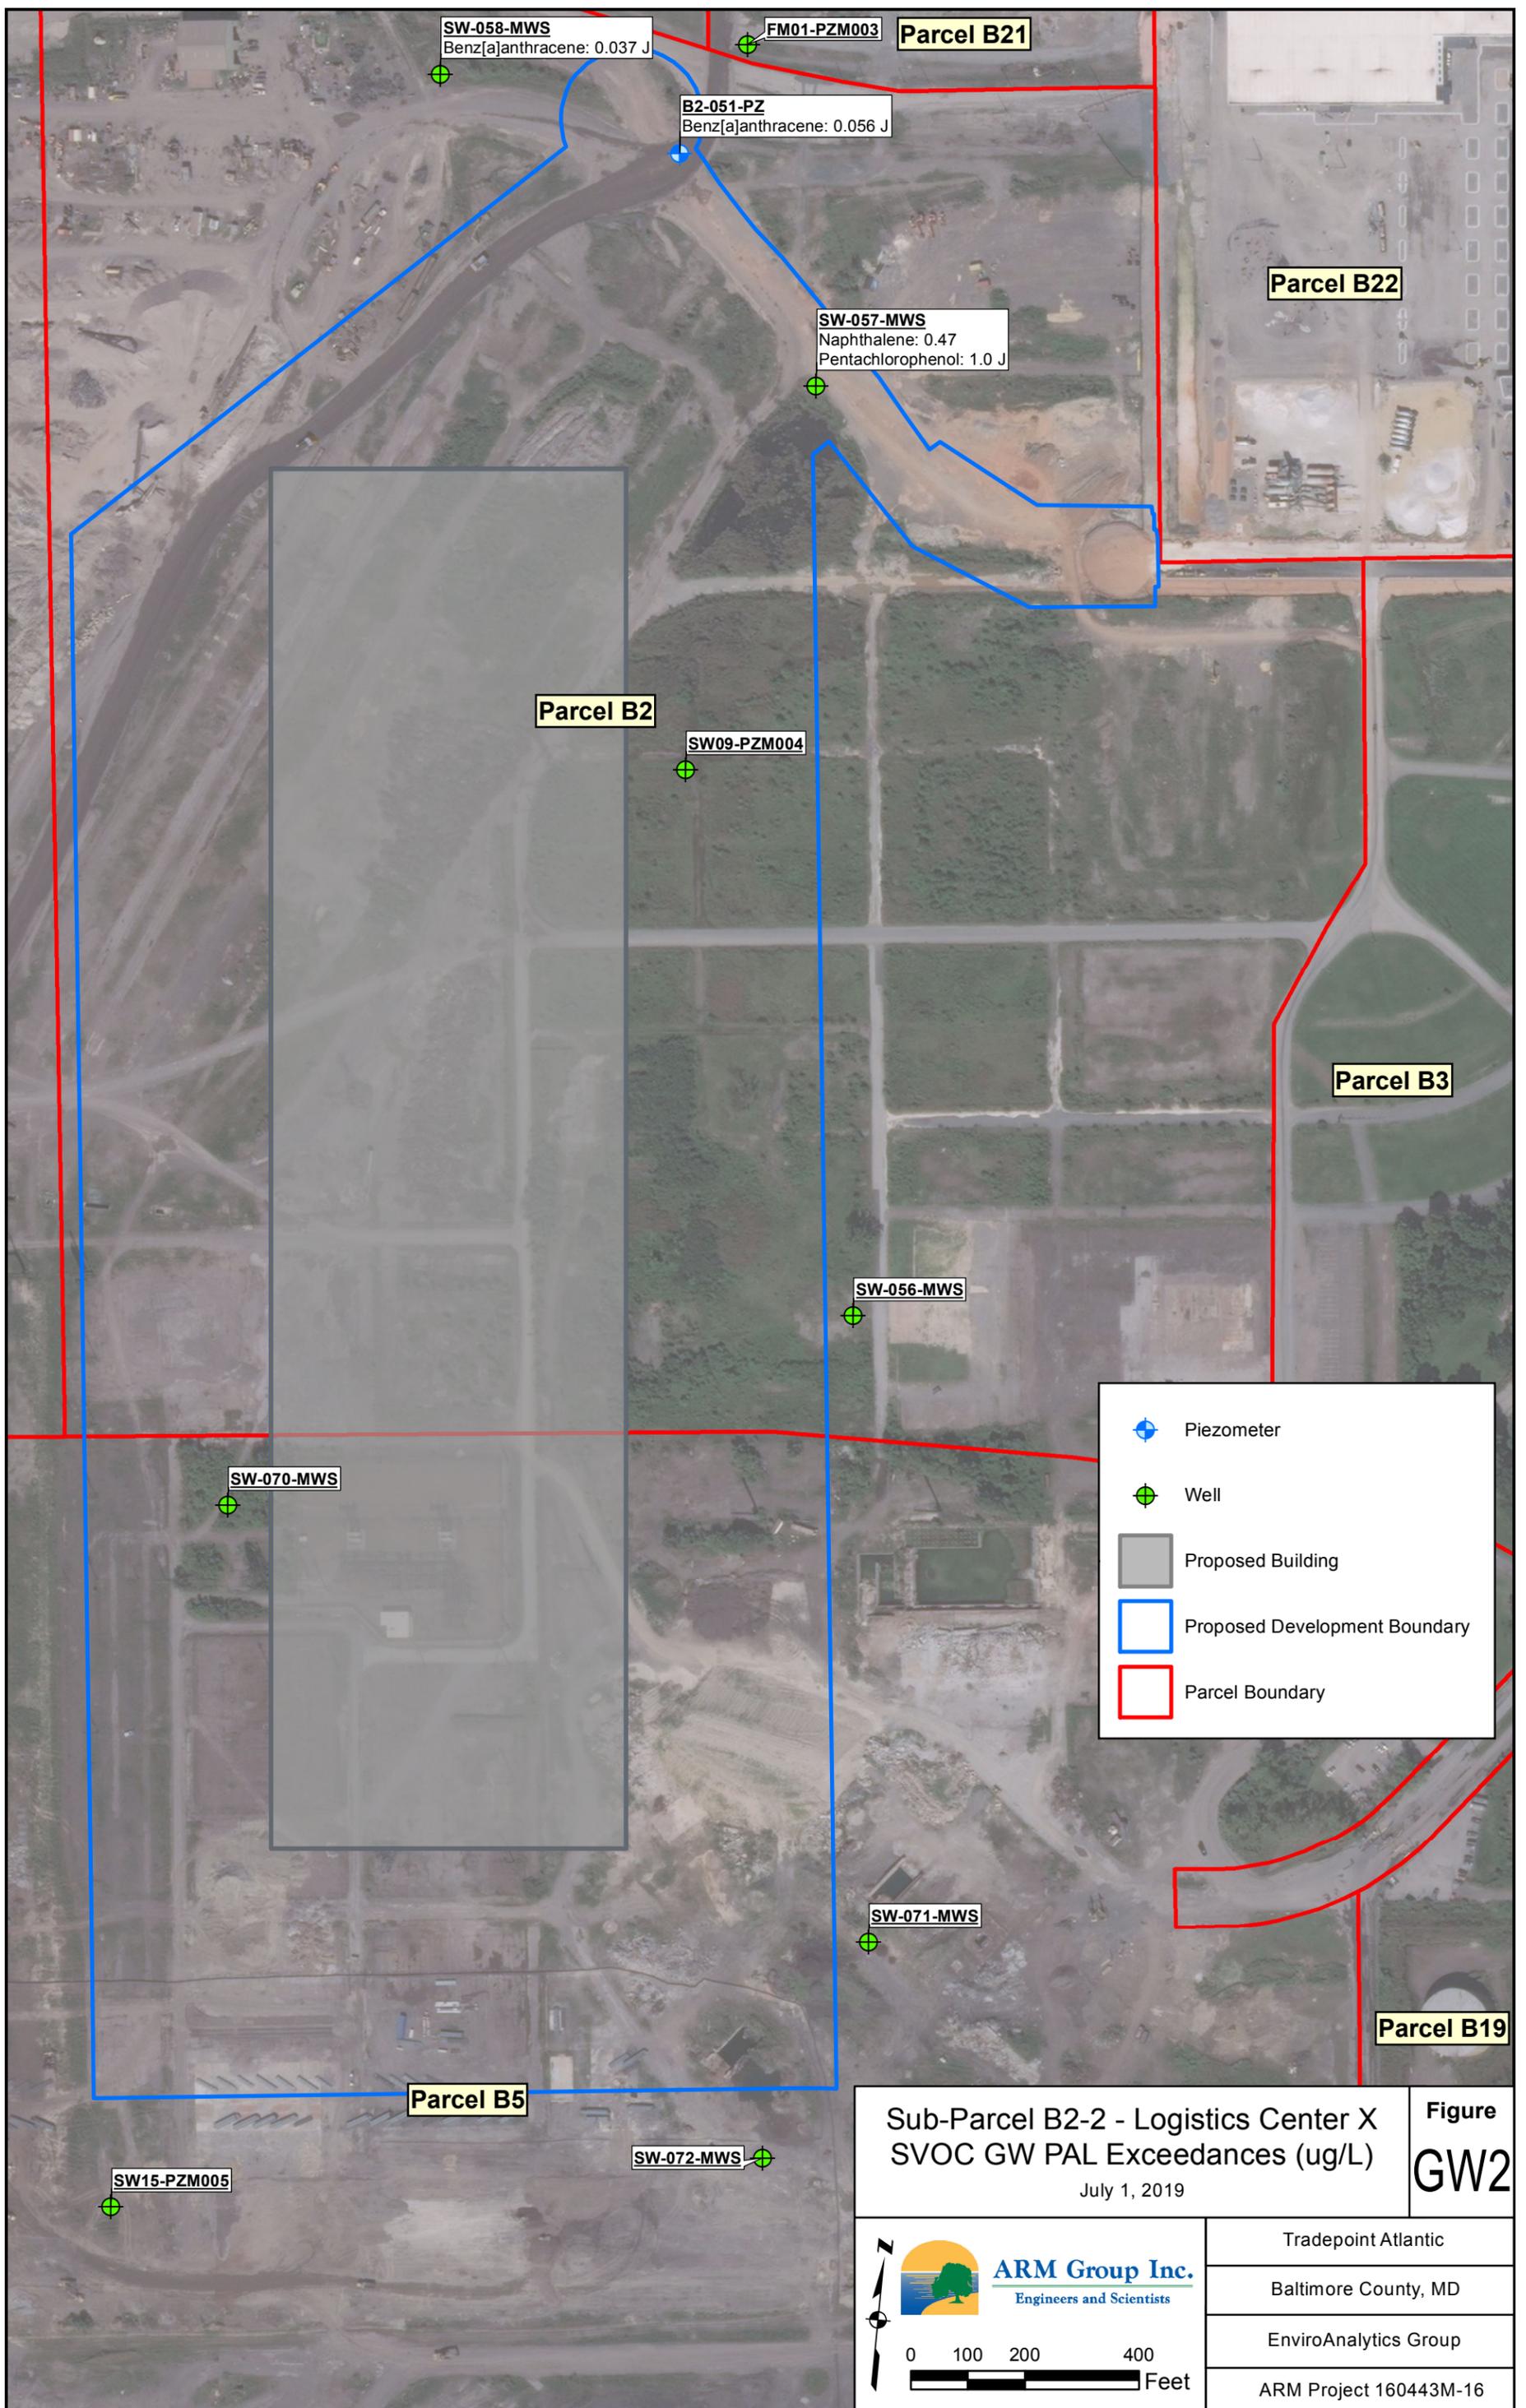

SW-058-MWS
Benz[a]anthracene: 0.037 J

FM01-PZM003

Parcel B21

B2-051-PZ
Benz[a]anthracene: 0.056 J

Parcel B22

SW-057-MWS
Naphthalene: 0.47
Pentachlorophenol: 1.0 J

Parcel B2

SW09-PZM004

Parcel B3

SW-056-MWS

SW-070-MWS

	Piezometer
	Well
	Proposed Building
	Proposed Development Boundary
	Parcel Boundary

SW-071-MWS

Parcel B19

Parcel B5

SW-072-MWS

SW15-PZM005

**Sub-Parcel B2-2 - Logistics Center X
SVOC GW PAL Exceedances (ug/L)**


July 1, 2019


**Figure
GW2**


ARM Group Inc.
Engineers and Scientists

0 100 200 400
Feet

Tradepoint Atlantic
Baltimore County, MD
EnviroAnalytics Group
ARM Project 160443M-16

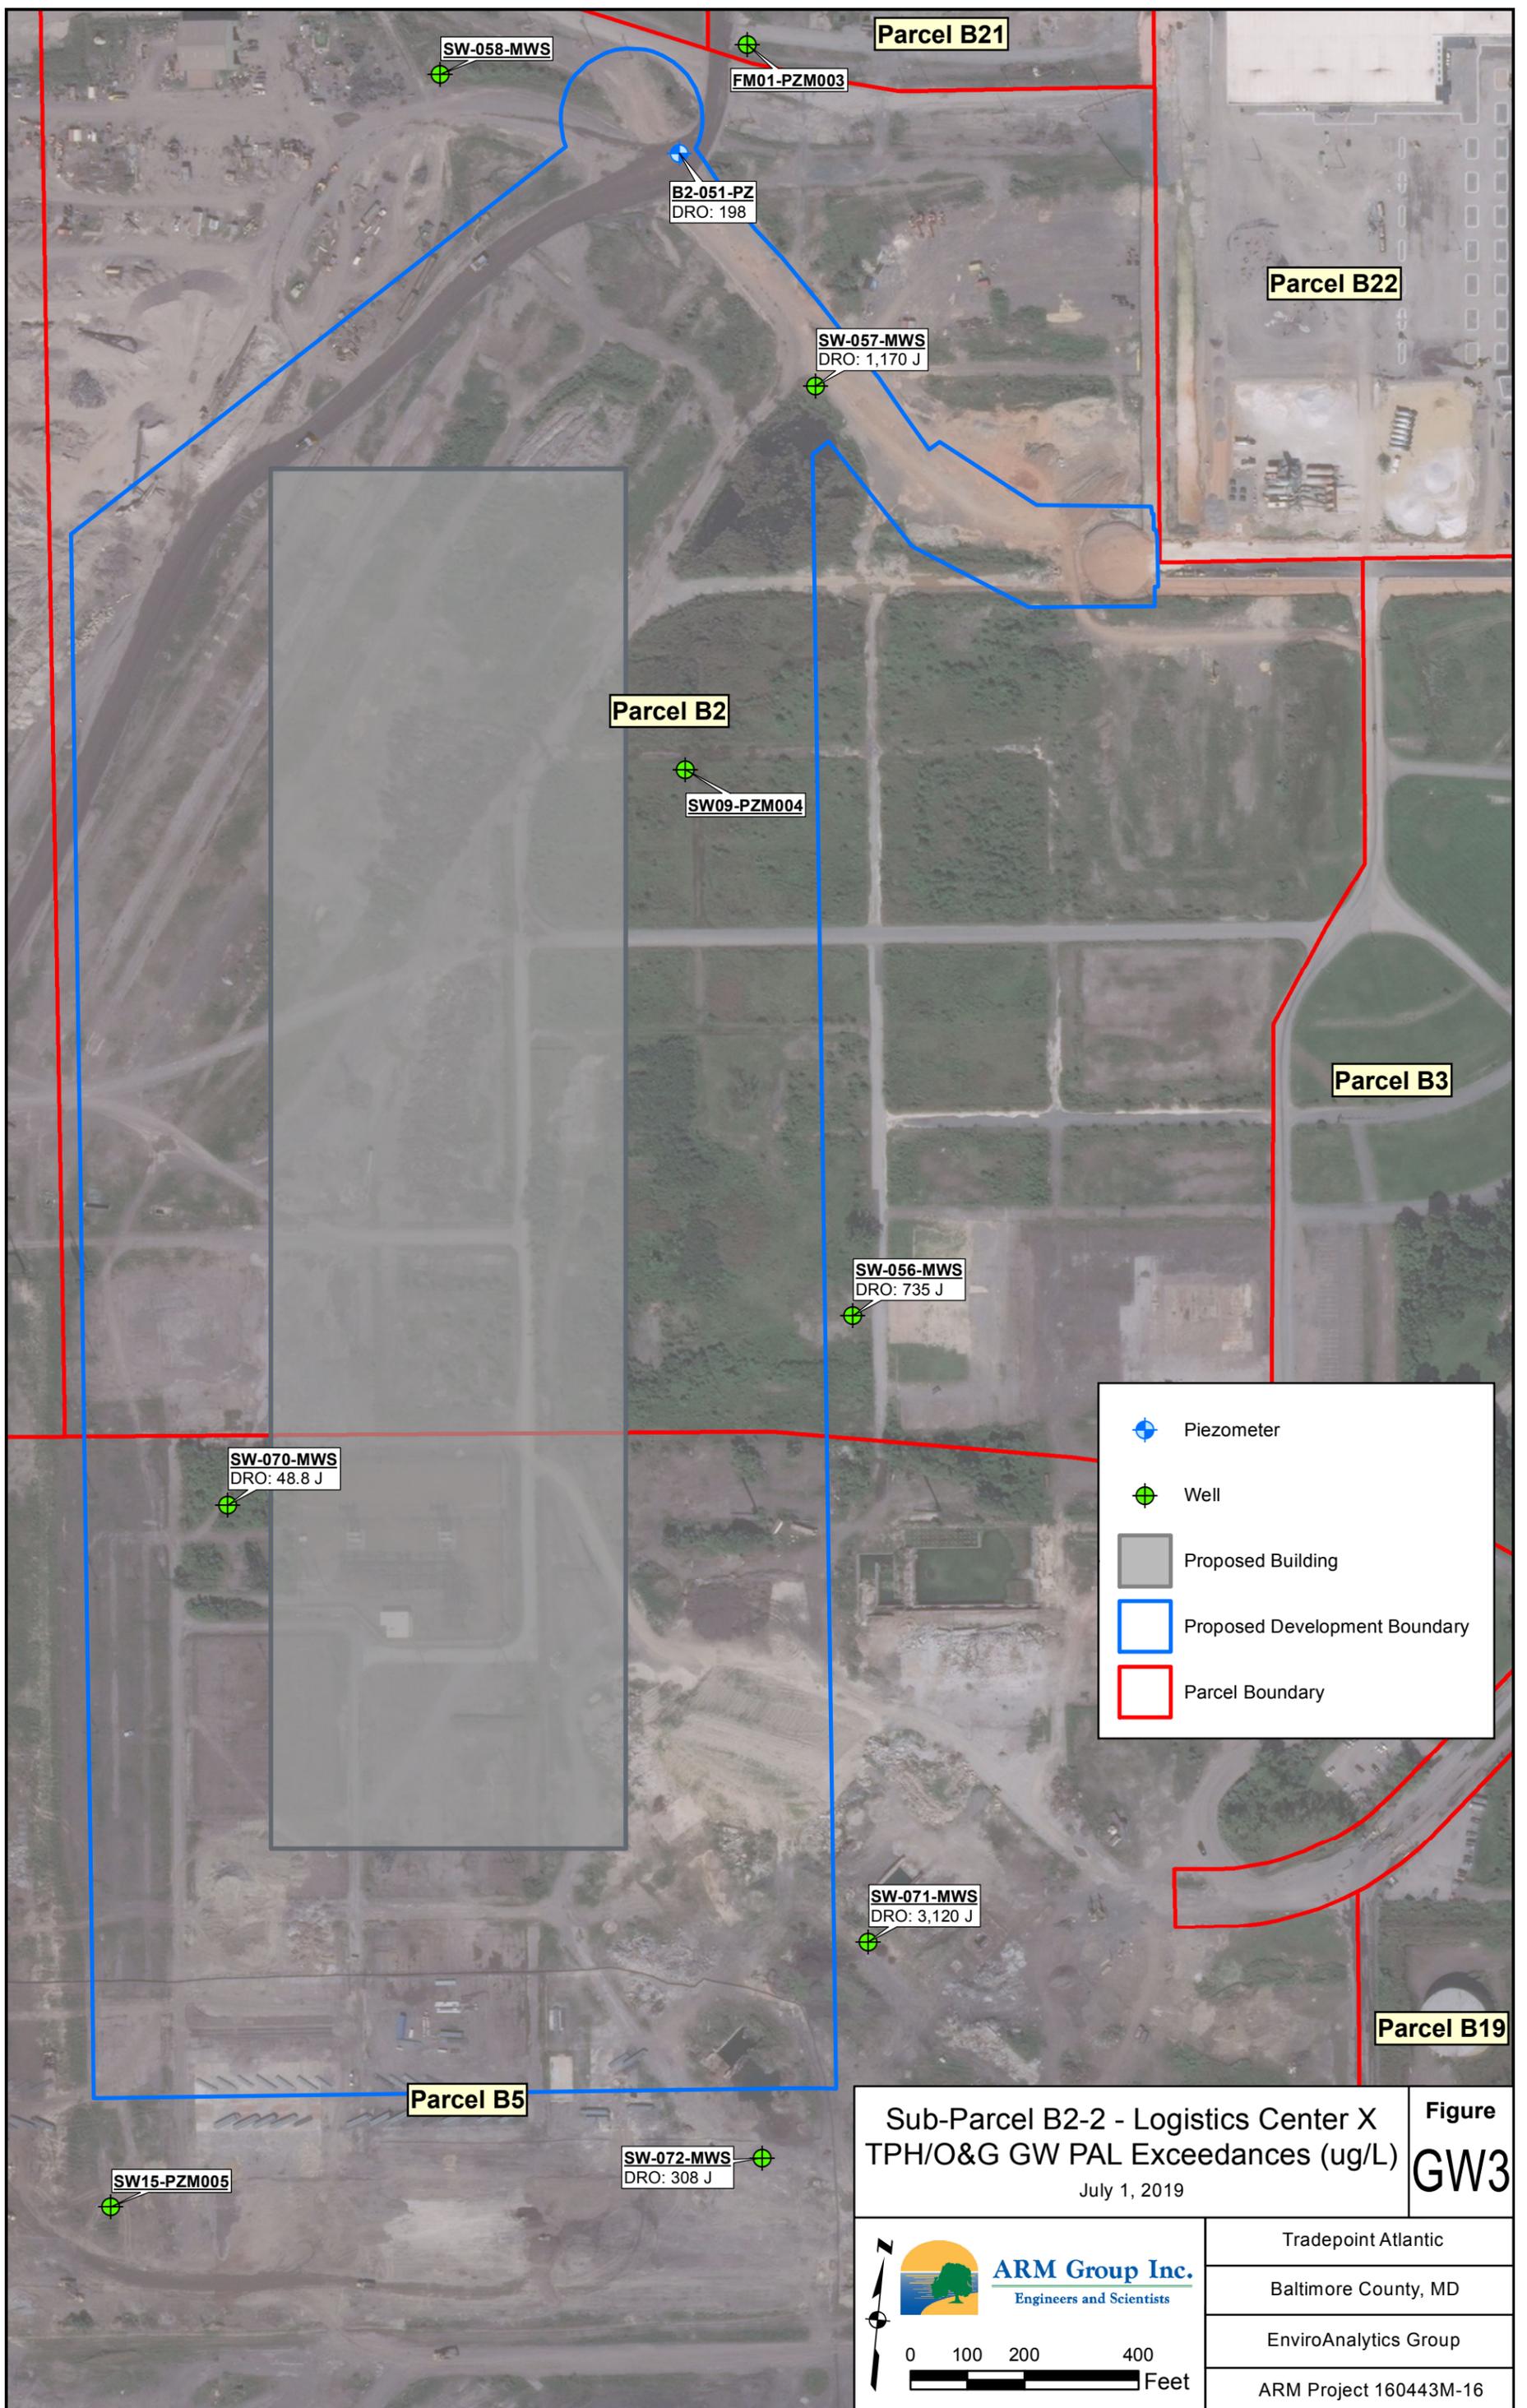

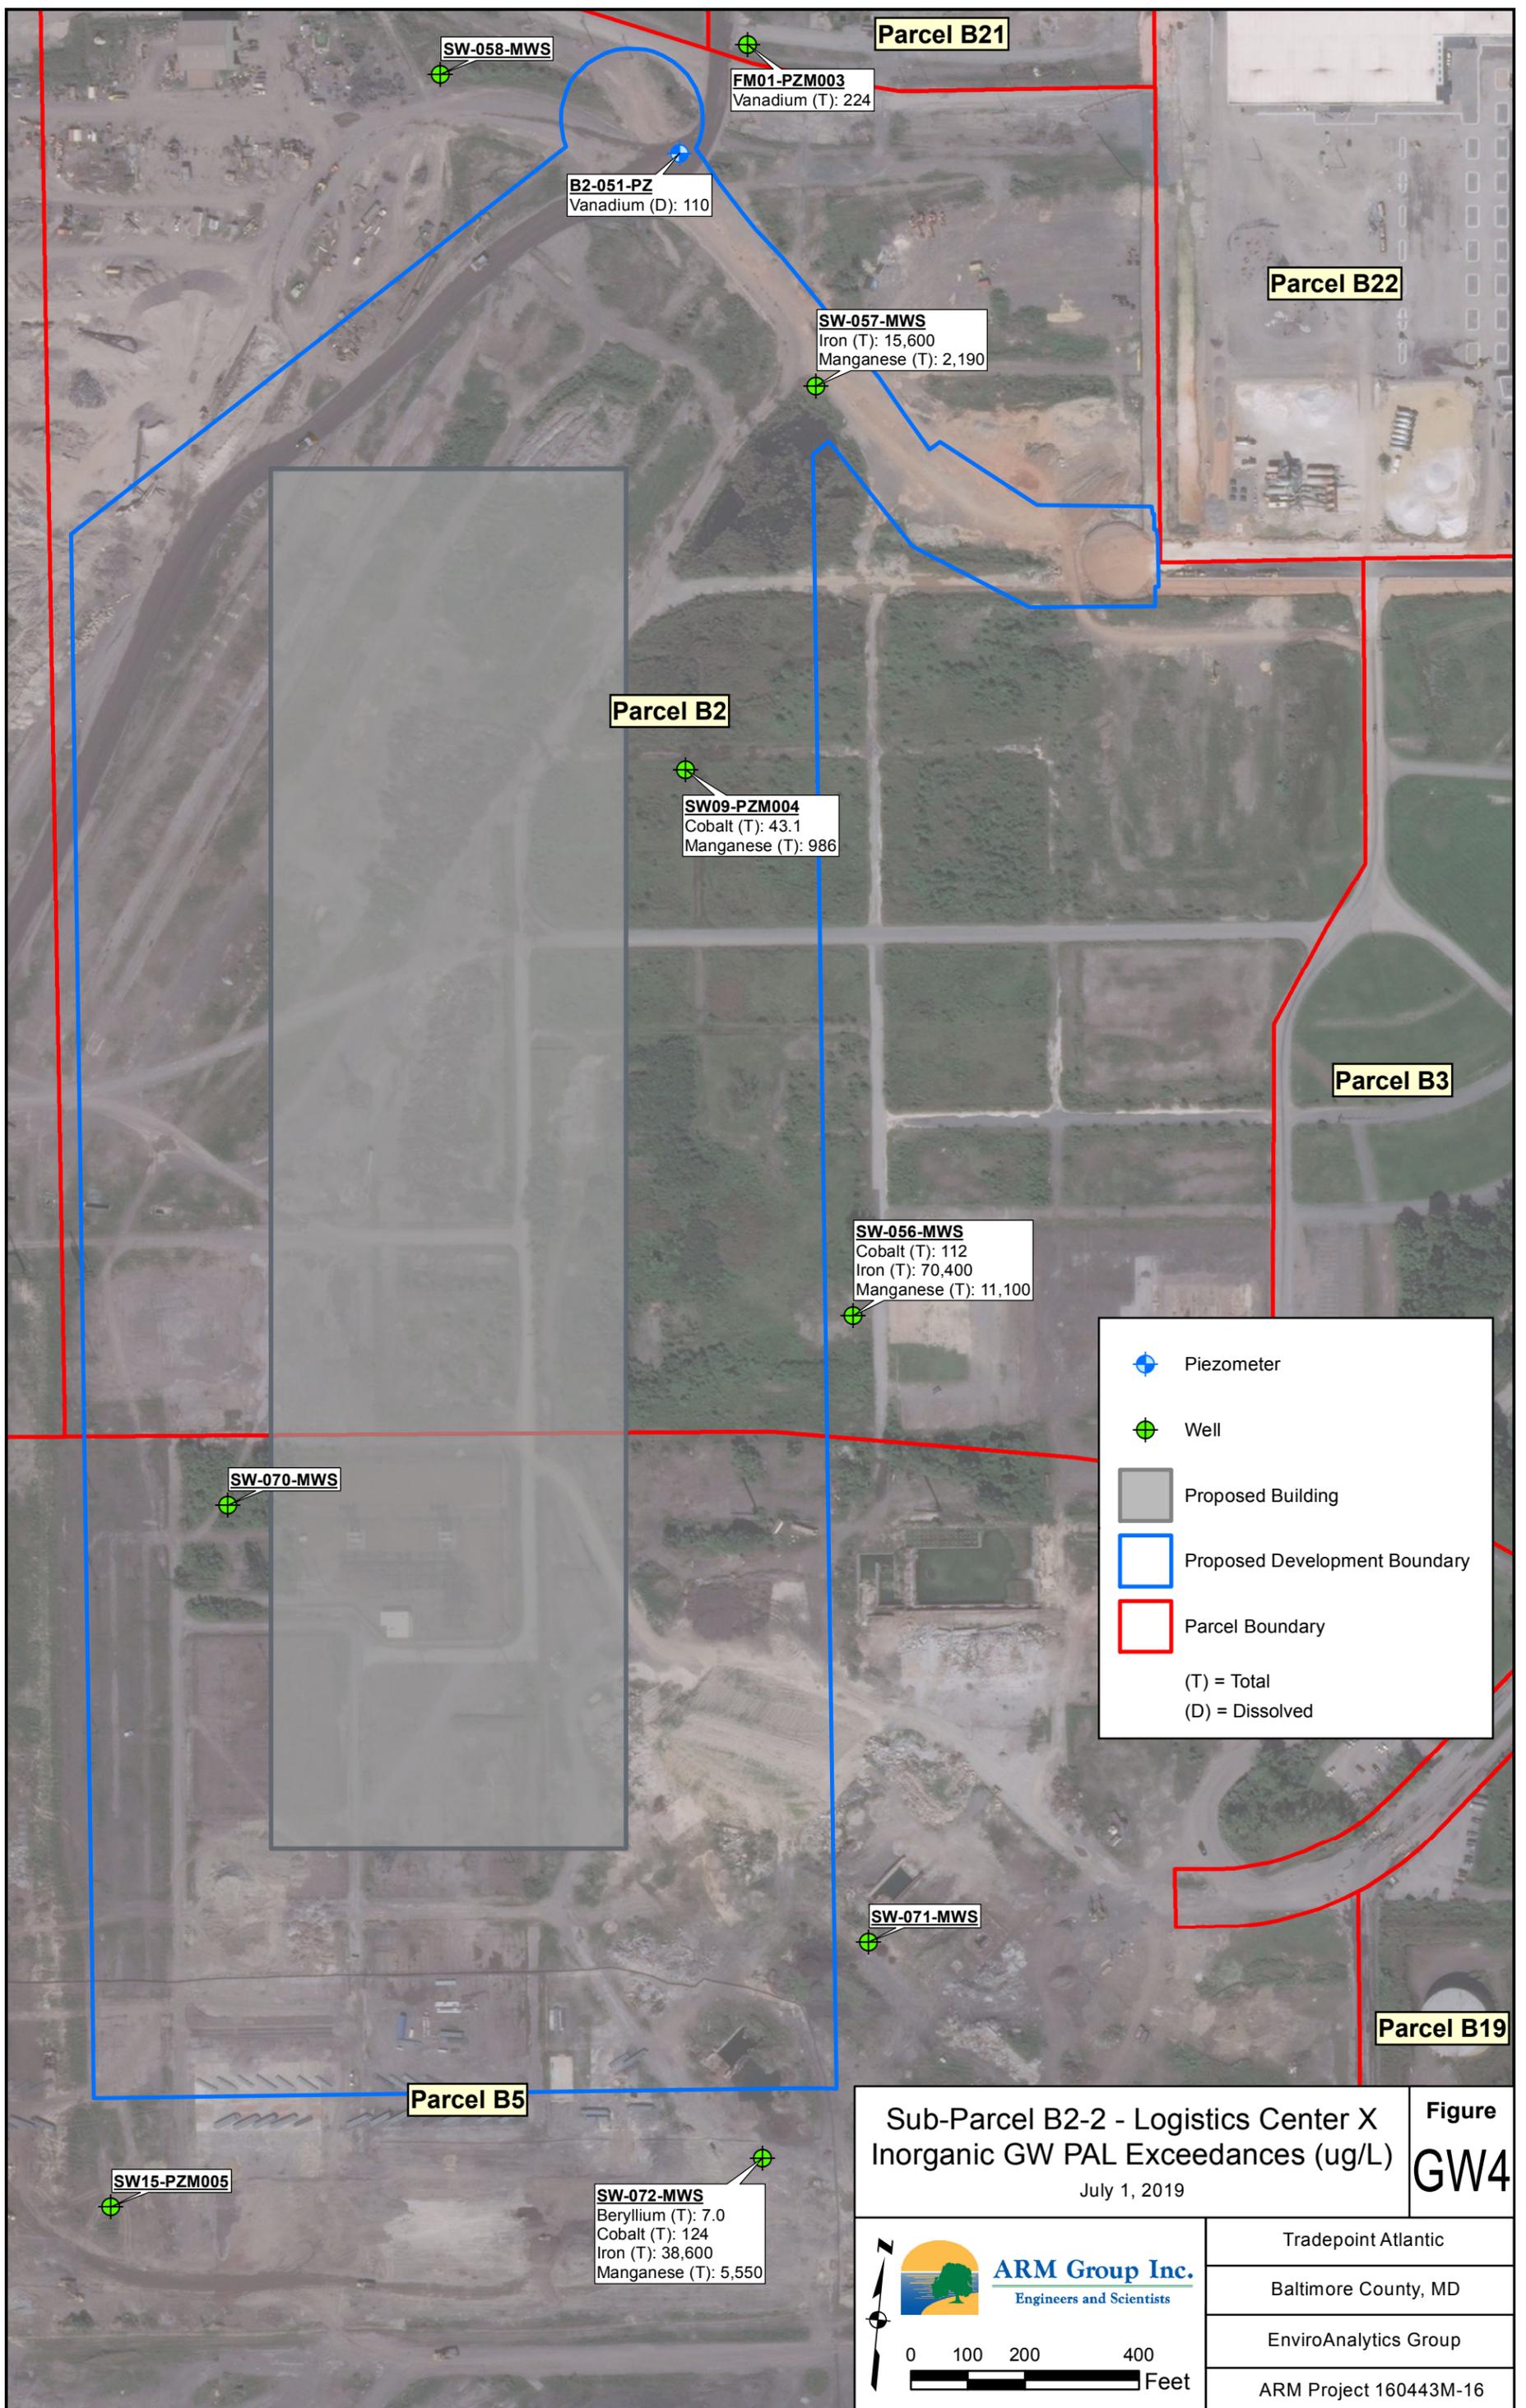

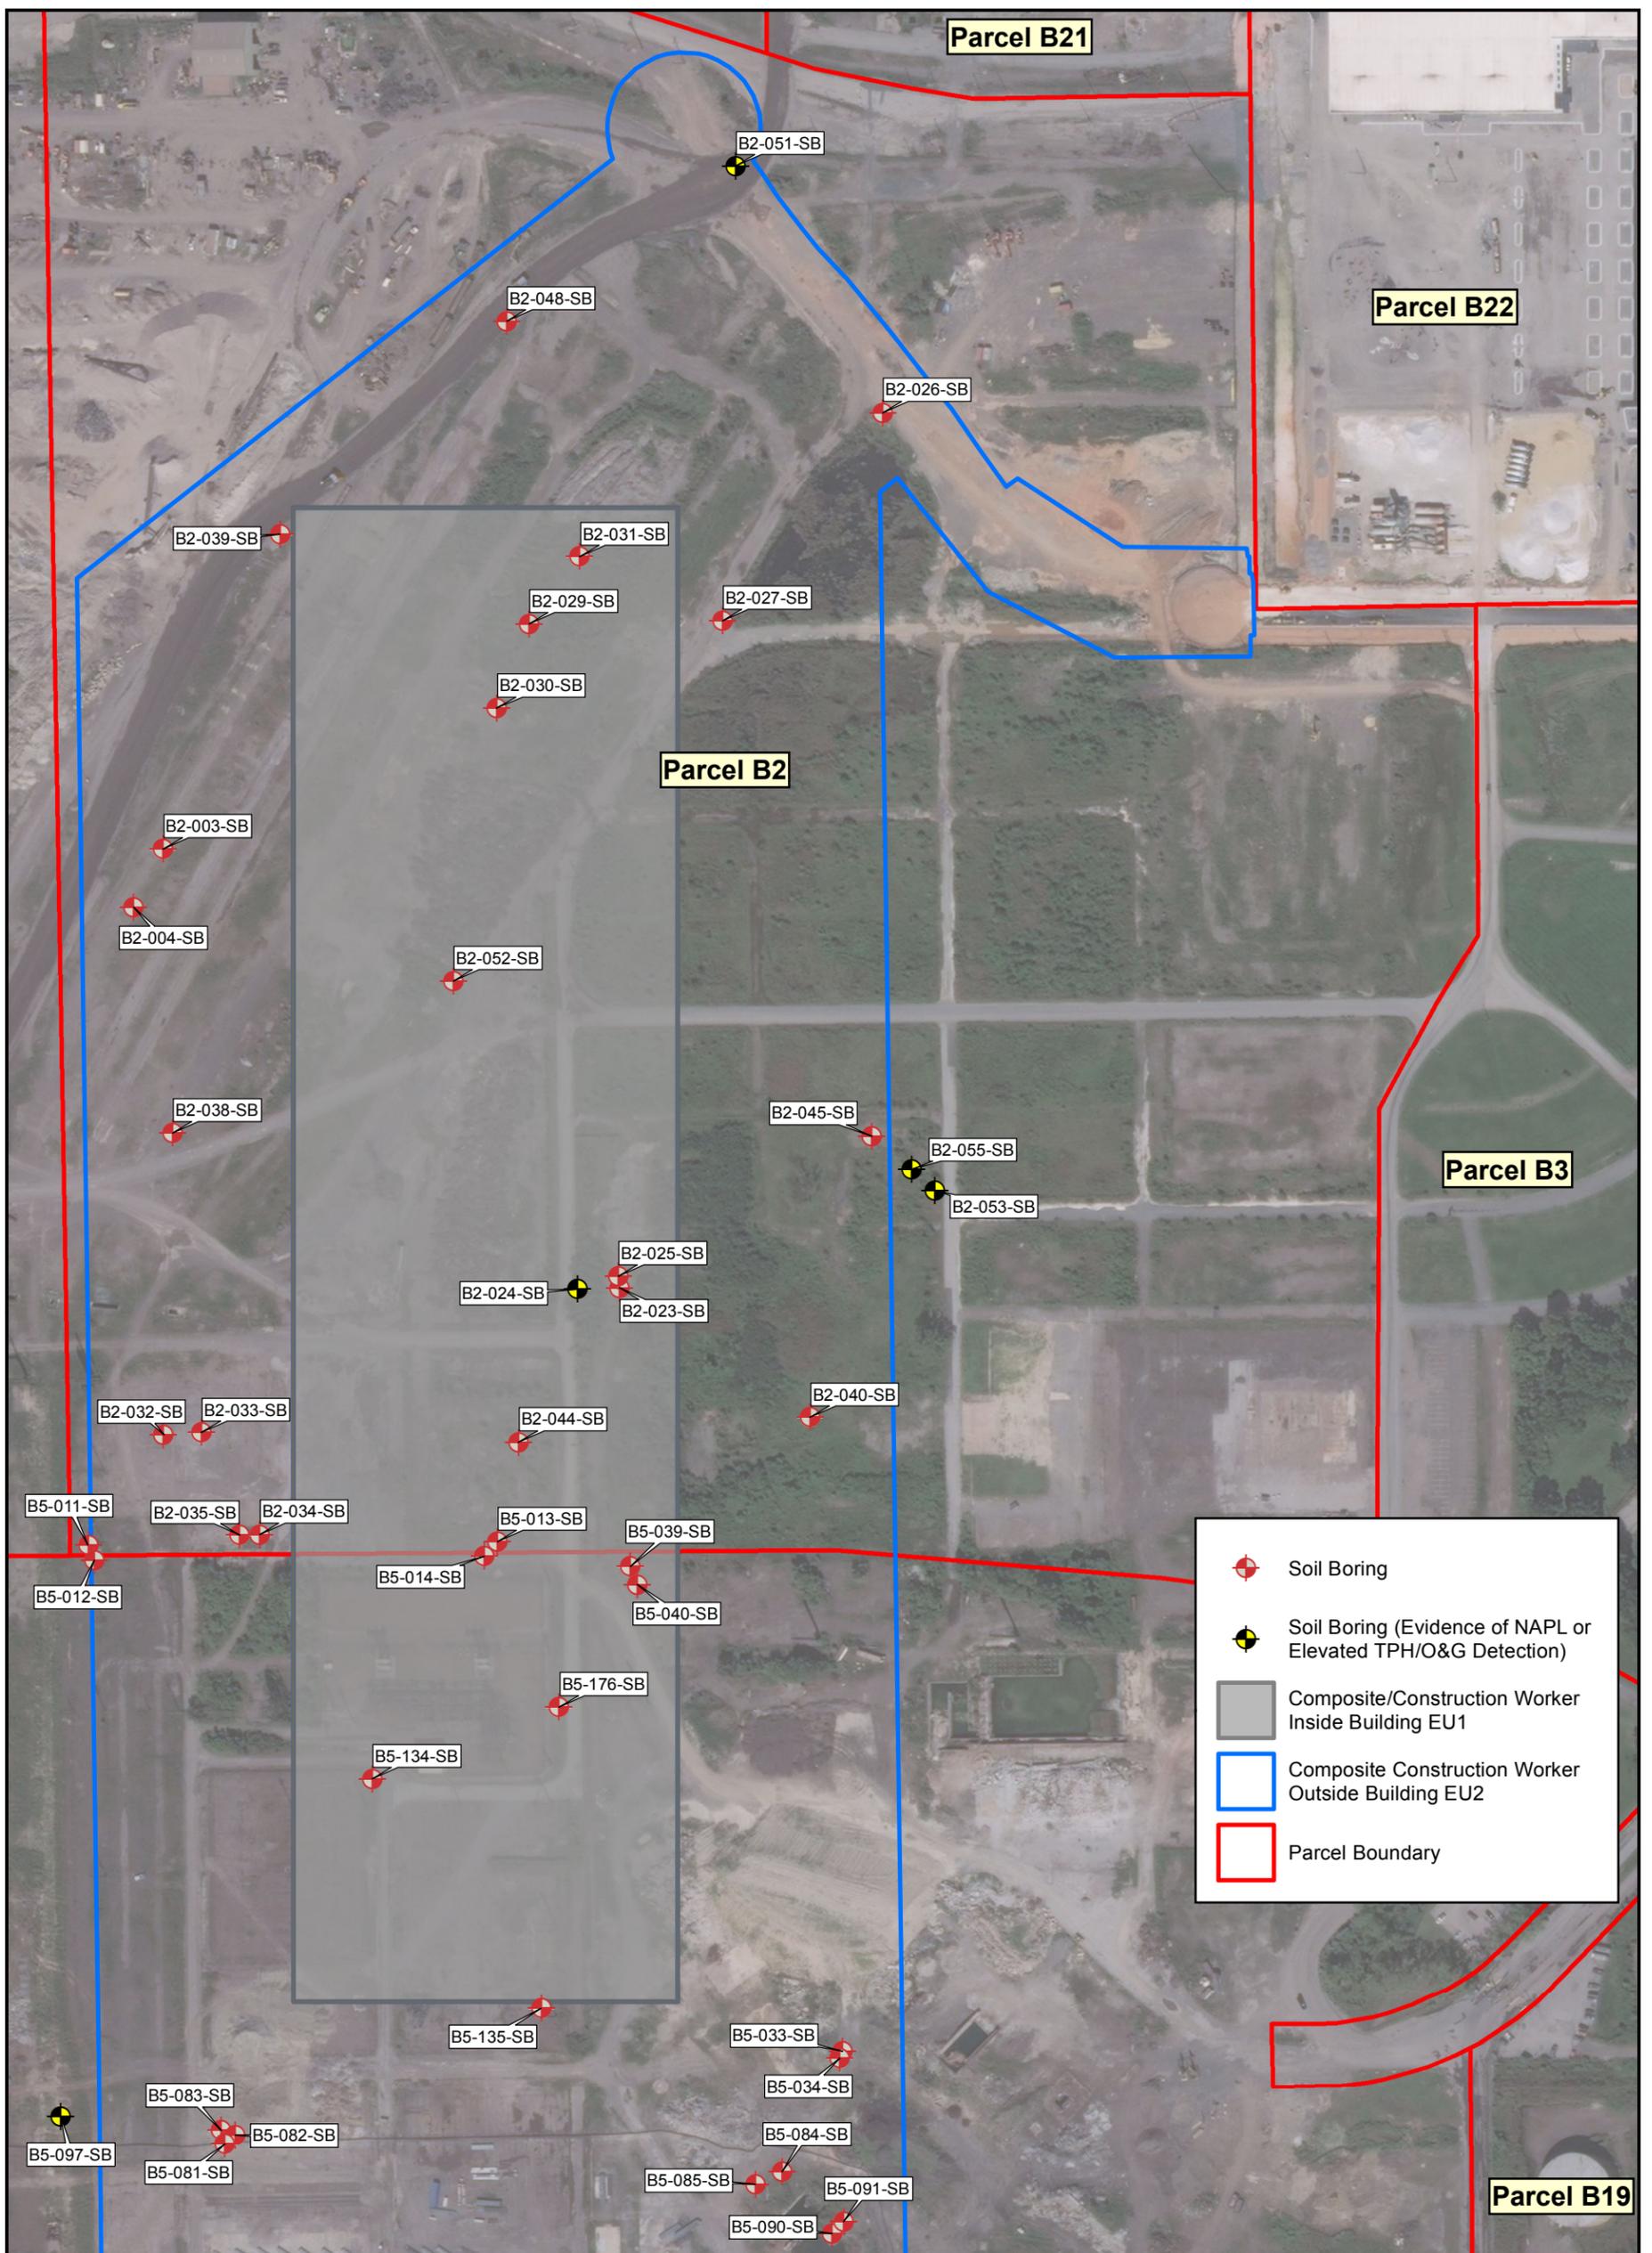

Sub-Parcel B2-2 - Logistics Center X
Risk Assessment Exposure Units


Figure
5

July 1, 2019

ARM Group Inc.
Engineers and Scientists

0 100 200 400
Feet

Tradepoint Atlantic
Baltimore County, MD
EnviroAnalytics Group
ARM Project 160443M-16

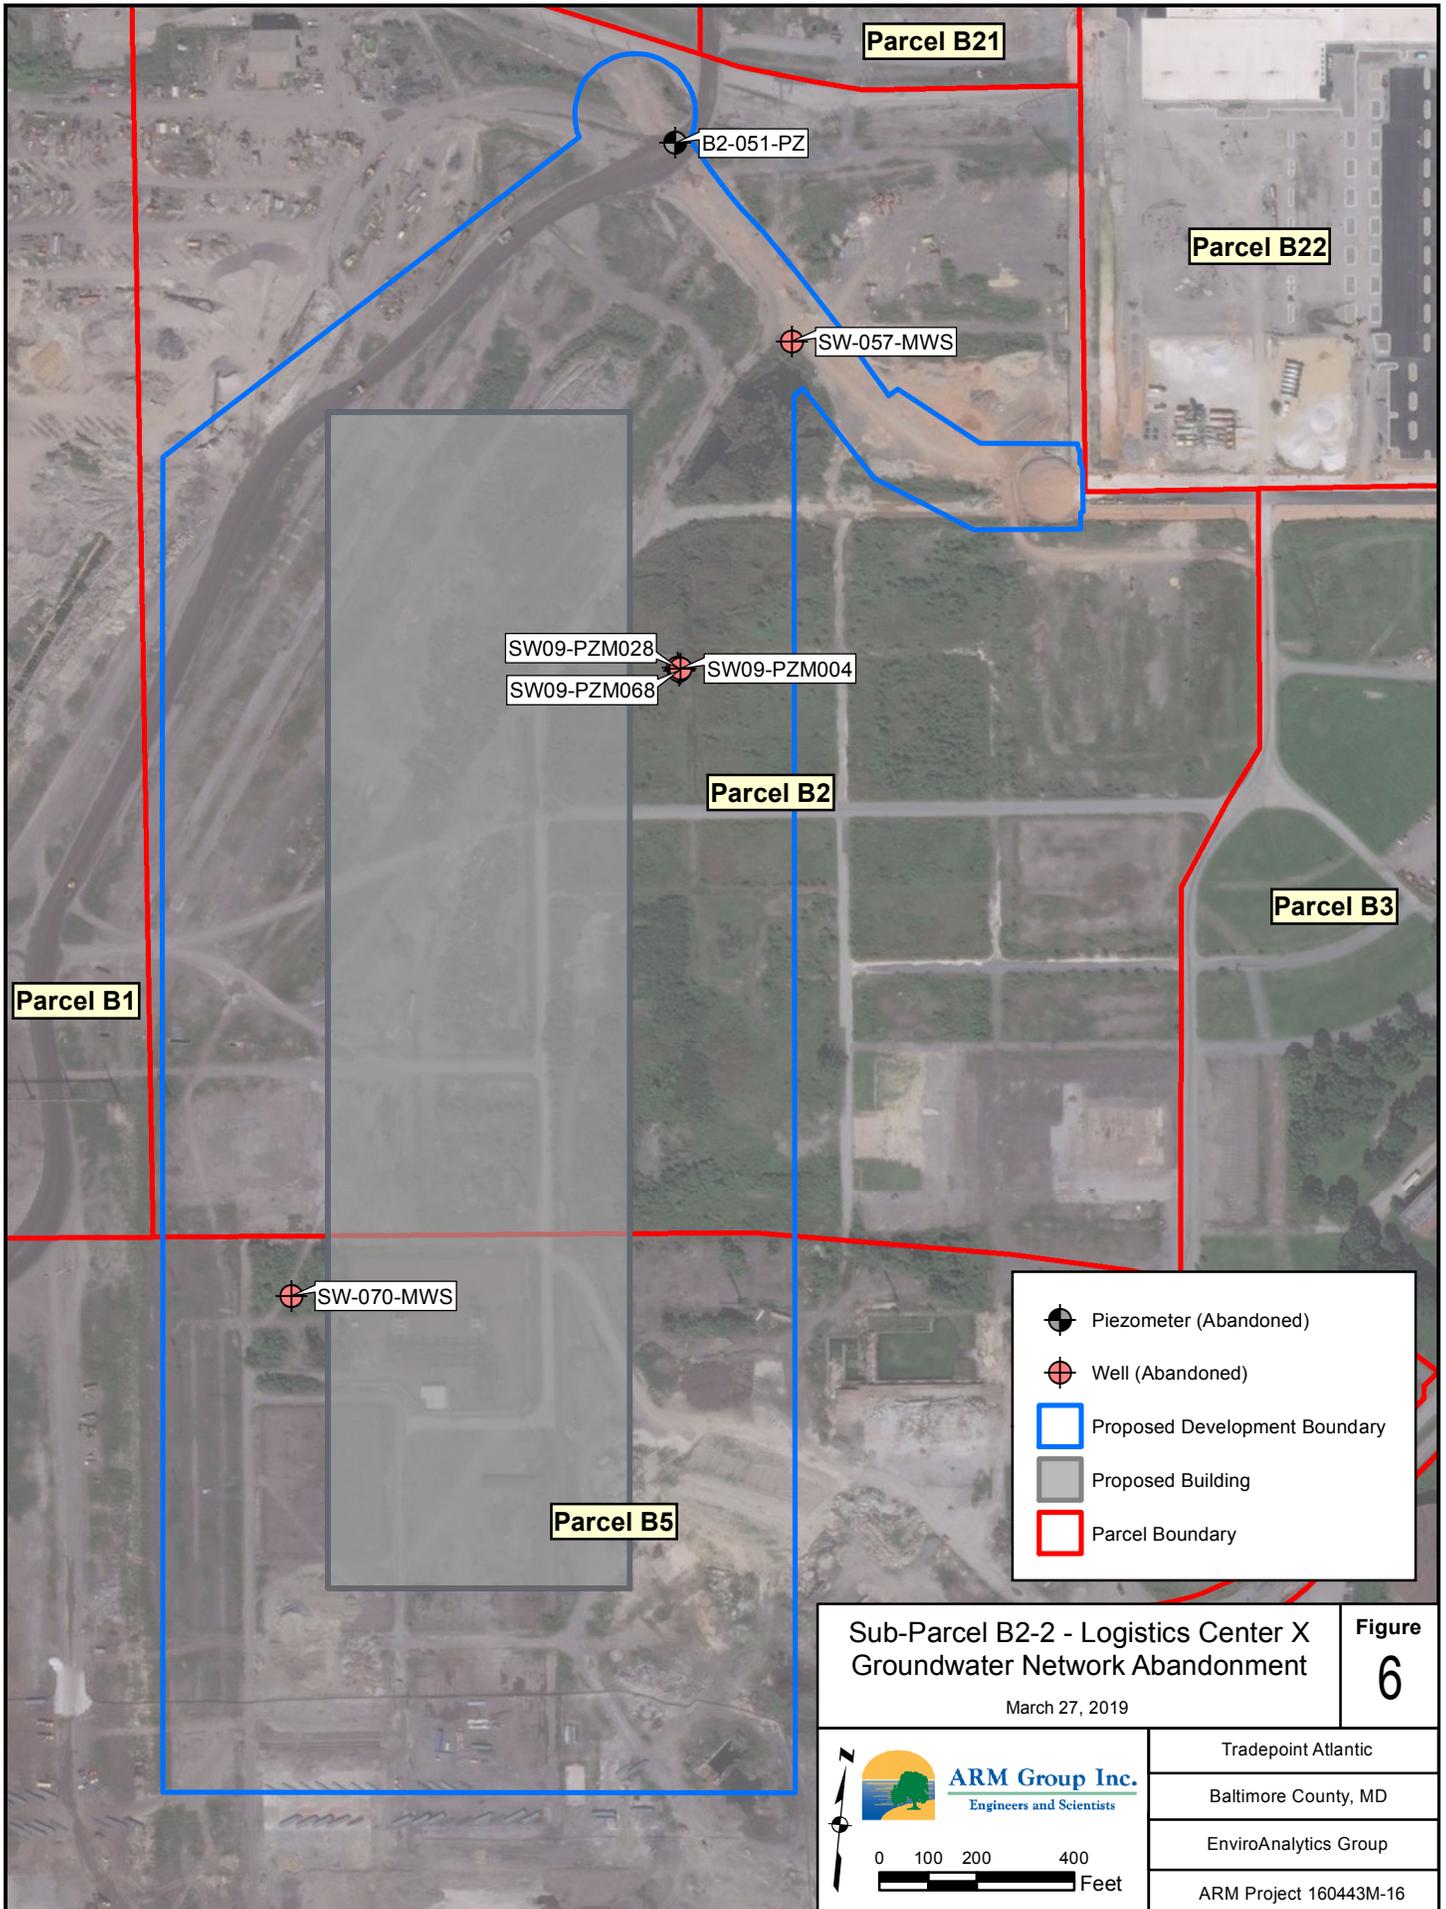

Parcel B21

Parcel B22

B2-051-PZ

SW-057-MWS

SW09-PZM028

SW09-PZM004

SW09-PZM068

Parcel B2

Parcel B3

Parcel B1

SW-070-MWS

Parcel B5

-  Piezometer (Abandoned)
-  Well (Abandoned)
-  Proposed Development Boundary
-  Proposed Building
-  Parcel Boundary

Sub-Parcel B2-2 - Logistics Center X
Groundwater Network Abandonment

Figure
6

March 27, 2019



ARM Group Inc.
Engineers and Scientists



0 100 200 400 Feet

Tradepoint Atlantic
Baltimore County, MD
EnviroAnalytics Group
ARM Project 160443M-16

TABLES

Table 1 - Sub-Parcel B2-2
Summary of Organics Detected in Soil

Parameter	Units	PAL	B2-003-SB-1*	B2-003-SB-4.5*	B2-004-SB-1*	B2-004-SB-5*	B2-023-SB-1*	B2-023-SB-4*	B2-024-SB-1*	B2-025-SB-1*	B2-025-SB-4*	B2-026-SB-1	B2-026-SB-5	B2-027-SB-1	B2-029-SB-1*	B2-029-SB-8*	B2-030-SB-1*	B2-030-SB-5*	B2-031-SB-1*	B2-031-SB-7*	B2-032-SB-1*
Volatile Organic Compounds																					
1,1,1-Trichloroethane	mg/kg	36,000	N/A	N/A	N/A	N/A	N/A	0.0054 U	N/A	N/A	N/A	N/A	0.0053 U	N/A	N/A	N/A	N/A	N/A	N/A	0.0062 U	N/A
1,2,3-Trichlorobenzene	mg/kg	930	N/A	N/A	N/A	N/A	N/A	0.0054 U	N/A	N/A	N/A	N/A	0.0034 J	N/A	N/A	N/A	N/A	N/A	N/A	0.0062 U	N/A
1,2,4-Trichlorobenzene	mg/kg	110	N/A	N/A	N/A	N/A	N/A	0.0054 U	N/A	N/A	N/A	N/A	0.011	N/A	N/A	N/A	N/A	N/A	N/A	0.0062 U	N/A
1,2-Dichloroethane	mg/kg	2	N/A	N/A	N/A	N/A	N/A	0.0054 U	N/A	N/A	N/A	N/A	0.0053 U	N/A	N/A	N/A	N/A	N/A	N/A	0.0062 U	N/A
2-Butanone (MEK)	mg/kg	190,000	N/A	N/A	N/A	N/A	N/A	0.011 U	N/A	N/A	N/A	N/A	0.011 U	N/A	N/A	N/A	N/A	N/A	N/A	0.012 U	N/A
2-Hexanone	mg/kg	1,300	N/A	N/A	N/A	N/A	N/A	0.011 U	N/A	N/A	N/A	N/A	0.011 U	N/A	N/A	N/A	N/A	N/A	N/A	0.012 U	N/A
Acetone	mg/kg	670,000	N/A	N/A	N/A	N/A	N/A	0.042	N/A	N/A	N/A	N/A	0.022 J	N/A	N/A	N/A	N/A	N/A	N/A	0.024	N/A
Benzene	mg/kg	5.1	N/A	N/A	N/A	N/A	N/A	0.0054 U	N/A	N/A	N/A	N/A	0.0053 U	N/A	N/A	N/A	N/A	N/A	N/A	0.0062 U	N/A
Carbon disulfide	mg/kg	3,500	N/A	N/A	N/A	N/A	N/A	0.0074	N/A	N/A	N/A	N/A	0.0033 J	N/A	N/A	N/A	N/A	N/A	N/A	0.0062 U	N/A
Cyclohexane	mg/kg	27,000	N/A	N/A	N/A	N/A	N/A	0.011 U	N/A	N/A	N/A	N/A	0.011 U	N/A	N/A	N/A	N/A	N/A	N/A	0.012 U	N/A
Ethylbenzene	mg/kg	25	N/A	N/A	N/A	N/A	N/A	0.0054 U	N/A	N/A	N/A	N/A	0.0053 U	N/A	N/A	N/A	N/A	N/A	N/A	0.0062 U	N/A
Methyl Acetate	mg/kg	1,200,000	N/A	N/A	N/A	N/A	N/A	0.054 U	N/A	N/A	N/A	N/A	0.053 UJ	N/A	N/A	N/A	N/A	N/A	N/A	0.062 U	N/A
Methylene Chloride	mg/kg	1,000	N/A	N/A	N/A	N/A	N/A	0.0054 U	N/A	N/A	N/A	N/A	0.0053 UJ	N/A	N/A	N/A	N/A	N/A	N/A	0.0062 U	N/A
Tetrachloroethene	mg/kg	100	N/A	N/A	N/A	N/A	N/A	0.0054 U	N/A	N/A	N/A	N/A	0.0053 U	N/A	N/A	N/A	N/A	N/A	N/A	0.0062 U	N/A
Toluene	mg/kg	47,000	N/A	N/A	N/A	N/A	N/A	0.0054 U	N/A	N/A	N/A	N/A	0.0053 U	N/A	N/A	N/A	N/A	N/A	N/A	0.0062 U	N/A
Xylenes	mg/kg	2,800	N/A	N/A	N/A	N/A	N/A	0.016 U	N/A	N/A	N/A	N/A	0.016 U	N/A	N/A	N/A	N/A	N/A	N/A	0.019 U	N/A
Semi-Volatile Organic Compounds[^]																					
1,1-Biphenyl	mg/kg	200	0.031 J	0.072 U	0.016 J	0.076 U	0.07 U	0.079 U	0.075 U	0.071 U	0.08 U	0.075 U	0.077 U	0.076 U	0.072 U	0.079 U	0.078 U	0.078 U	0.07 U	0.076 U	0.073 U
1,2,4,5-Tetrachlorobenzene	mg/kg	350	0.073 U	0.072 U	0.074 U	0.076 U	0.07 U	0.079 U	0.075 U	0.071 U	0.08 U	0.075 U	0.077 U	0.076 U	0.072 U	0.079 U	0.078 U	0.078 U	0.07 U	0.076 U	0.073 U
2,4-Dimethylphenol	mg/kg	16,000	0.073 U	0.072 U	0.074 U	0.076 U	0.07 U	0.079 U	0.075 U	0.071 U	0.08 U	0.075 R	0.077 R	0.076 U	0.072 U	0.079 U	0.078 U	0.078 U	0.032 J	0.057 J	0.073 U
2-Chloronaphthalene	mg/kg	60,000	0.073 U	0.072 U	0.074 U	0.076 U	0.07 U	0.079 U	0.075 U	0.071 U	0.08 U	0.075 U	0.077 U	0.076 U	0.072 U	0.079 U	0.078 U	0.078 U	0.07 U	0.076 U	0.073 U
2-Methylnaphthalene	mg/kg	3,000	0.29	0.032	0.067	0.054	0.0071 U	0.0079 J	0.02 J	0.014	0.0046 J	0.0043 J	0.015	0.093	0.015	0.0081 U	0.039	0.0078 J	0.023	0.86	0.027
2-Methylphenol	mg/kg	41,000	0.073 U	0.072 U	0.074 U	0.076 U	0.07 U	0.079 U	0.075 U	0.071 U	0.08 U	0.075 R	0.077 R	0.076 U	0.072 U	0.079 U	0.078 U	0.078 U	0.07 U	0.048 J	0.073 U
3&4-Methylphenol(m&p Cresol)	mg/kg	41,000	0.15 U	0.14 U	0.15 U	0.15 U	0.14 U	0.16 U	0.15 U	0.14 U	0.16 U	0.15 R	0.15 R	0.15 U	0.14 U	0.16 U	0.16 U	0.16 U	0.019 J	0.1 J	0.15 U
Acenaphthene	mg/kg	45,000	0.05	0.013	0.11	0.013	0.0071 U	0.0015 J	0.031 J	0.0043 J	0.0014 J	0.0014 J	0.0011 J	0.0083 J	0.0012 J	0.0081 U	0.0086	0.0042 J	0.002 J	0.073 J	0.002 J
Acenaphthylene	mg/kg	45,000	0.16	0.042	0.051	0.5	0.00053 J	0.0069 J	1.3	0.0066 J	0.0076 J	0.00092 J	0.02	0.017 J	0.0067 J	0.0081 U	0.033	0.0015 J	0.013	0.85	0.0097
Acetophenone	mg/kg	120,000	0.033 J	0.072 U	0.021 J	0.076 U	0.07 U	0.079 U	0.075 U	0.071 U	0.08 U	0.075 U	0.077 U	0.021 J	0.072 U	0.079 U	0.078 U	0.078 U	0.07 U	0.025 J	0.073 U
Anthracene	mg/kg	230,000	0.25	0.12	0.092	0.35	0.00042 B	0.0097	0.33	0.014	0.005 B	0.0074 J	0.014	0.056 J	0.011	0.0081 U	0.061	0.0099	0.023	0.5	0.023
Benz[a]anthracene	mg/kg	21	1.2	0.37	0.44	1.8	0.0021 J	0.042	0.85	0.054	0.026	0.03	0.071	0.11	0.025	0.0081 U	0.3	0.066	0.07 U	2.5	0.069
Benzaldehyde	mg/kg	120,000	0.083	0.072 U	0.031 J	0.076 U	0.07 U	0.087	0.021 J	0.071 U	0.08 U	0.075 U	0.077 U	0.035 J	0.059 J	0.079 U	0.022 J	0.078 U	0.07 U	0.28	0.073 U
Benzo[a]pyrene	mg/kg	2.1	1.1	0.29	0.72	2	0.0013 J	0.053	1.9	0.055	0.029	0.018	0.062	0.094	0.019	0.0081 U	0.24	0.072	0.022 J	2.5	0.052
Benzo[b]fluoranthene	mg/kg	21	2.6	0.49	1.3	2.9	0.0071 U	0.092	2.9	0.087	0.049	0.054	0.12	0.28	0.055	0.0081 U	0.54	0.12	0.092	4.9	0.094
Benzo[g,h,i]perylene	mg/kg		0.73	0.19	0.7	1.4	0.0071 U	0.033	1.6	0.036	0.018	0.0092	0.025	0.065 J	0.025	0.0081 U	0.2	0.063	0.026 B	1.8	0.037
Benzo[k]fluoranthene	mg/kg	210	0.65	0.15	0.98	1.2	0.0071 U	0.022	0.71	0.027	0.012	0.048	0.049	0.24	0.042	0.0081 U	0.42	0.094	0.075	3.8	0.029
bis(2-Ethylhexyl)phthalate	mg/kg	160	0.073 U	0.072 U	0.024 B	0.076 U	0.07 U	0.026 J	0.075 U	0.021 J	0.08 U	0.015 B	0.077 U	0.34	0.034 B	0.079 U	0.053 B	0.078 U	0.07 U	0.076 U	0.073 U
Caprolactam	mg/kg	400,000	0.18 U	0.18 U	0.19 U	0.19 U	0.18 U	0.2 U	0.19 U	0.2 U	0.19 U	0.19 U	0.19 U	0.18 U	0.2 U	0.2 U	0.2 U	0.2 U	0.18 U	0.19 U	0.18 U
Carbazole	mg/kg		0.16	0.11	0.019 J	0.43	0.07 U	0.059 J	0.14	0.071 U	0.08 U	0.075 U	0.077 U	0.076 U	0.072 U	0.079 U	0.035 J	0.078 U	0.07 U	0.33	0.073 U
Chrysene	mg/kg	2,100	1.3	0.33	0.46	1.8	0.001 J	0.053	0.94	0.054	0.031	0.036	0.083	0.24	0.034	0.0081 U	0.32	0.061	0.07 U	2.6	0.071
Dibenz[a,h]anthracene	mg/kg	2.1	0.31	0.069	0.17	0.56	0.0071 U	0.0075 J	0.38	0.0094	0.0048 J	0.0025 J	0.011	0.077 U	0.006 J	0.0081 U	0.057	0.016	0.07 U	0.58	0.009
Diethylphthalate	mg/kg	660,000	0.073 U	0.072 U	0.074 U	0.076 U	0.07 U	0.079 U	0.016 J	0.071 U	0.08 U	0.075 U	0.077 U	0.076 U	0.015 J	0.079 U	0.078 U	0.078 U	0.07 U	0.076 U	0.073 U
Di-n-butylphthalate	mg/kg	82,000	0.073 U	0.038 B	0.074 U	0.076 U	0.064 B	0.065 B	0.022 B	0.018 B	0.047 B	0.043 B	0.026 B	0.06 B	0.05 B	0.023 B	0.042 B	0.043 B	0.07 U	0.076 U	0.039 B
Di-n-octylphthalate	mg/kg	8,200	0.073 U	0.072 U	0.074 U	0.076 U	0.07 U	0.079 U	0.075 U	0.071 U	0.08 U	0.075 U	0.077 U	0.076 UJ	0.072 U	0.079 U	0.078 U	0.078 U	0.07 U	0.076 U	0.073 U
Fluoranthene	mg/kg	30,000	2.6	0.64	0.6	2.4	0.0015 B	0.084	1.2	0.1	0.048	0.073	0.1	0.23	0.059	0.0081 U	0.46	0.063	0.094	4.1	0.19
Fluorene	mg/kg	30,000	0.04	0.022	0.027	0.12	0.0071 U	0.0019 J	0.057 J	0.0053 J	0.0023 J	0.001 J	0.0024 J	0.018 J	0.0039 J	0.0081 U	0.0096	0.0026 J	0.0038 J	0.16	0.0032 J
Hexachloroethane	mg/kg	8	0.073 U	0.072 U	0.074 U	0.076 U	0.07 U	0.079 U	0.075 U	0.071 U	0.08 U	0.075 U	0.077 U	0.076 U	0.072 U	0.079 U	0.078 U	0.078 U	0.07 U	0.043 J	0.073 U
Indeno[1,2,3-c,d]pyrene	mg/kg	21	0.72	0.18	0.57	1.4	0.0071 U	0.03	1.5	0.032	0.017	0.0089	0.029	0.045 J	0.02	0.0081 U	0.17	0.047	0.07 U	1.6	0.034
Isophorone	mg/kg	2,400	0.073 U	0.072 U	0.074 U	0.076 U	0.07 U	0.079 U	0.075 U	0.071 U	0.08 U	0.075 U	0.077 U	0.076 U	0.072 U	0.079 U	0.078 U	0.078 U	0.07 U	0.076 U	0.073 U
Naphthalene	mg/kg	17	0.25	0.069	0.071	0.23	0.0071 U	0.021	0.076	0.019	0.009	0.0046 B									

Table 1 - Sub-Parcel B2-2
Summary of Organics Detected in Soil

Parameter	Units	PAL	B2-032-SB-4*	B2-033-SB-1*	B2-033-SB-5*	B2-034-SB-1*	B2-035-SB-1*	B2-035-SB-4*	B2-038-SB-1	B2-038-SB-5	B2-039-SB-1*	B2-039-SB-5*	B2-040-SB-1	B2-040-SB-7	B2-044-SB-1*	B2-044-SB-7*	B2-045-SB-1*	B2-045-SB-5*	B2-048-SB-1	B2-048-SB-8
Volatile Organic Compounds																				
1,1,1-Trichloroethane	mg/kg	36,000	0.0047 U	N/A	N/A	N/A	N/A	0.0065 U	N/A	N/A	N/A	N/A	N/A	0.0064 U	N/A	N/A	N/A	N/A	N/A	N/A
1,2,3-Trichlorobenzene	mg/kg	930	0.0047 U	N/A	N/A	N/A	N/A	0.0065 U	N/A	N/A	N/A	N/A	N/A	0.0064 U	N/A	N/A	N/A	N/A	N/A	N/A
1,2,4-Trichlorobenzene	mg/kg	110	0.0047 U	N/A	N/A	N/A	N/A	0.0065 U	N/A	N/A	N/A	N/A	N/A	0.0064 U	N/A	N/A	N/A	N/A	N/A	N/A
1,2-Dichloroethane	mg/kg	2	0.0047 U	N/A	N/A	N/A	N/A	0.0065 U	N/A	N/A	N/A	N/A	N/A	0.0064 U	N/A	N/A	N/A	N/A	N/A	N/A
2-Butanone (MEK)	mg/kg	190,000	0.0093 U	N/A	N/A	N/A	N/A	0.013 U	N/A	N/A	N/A	N/A	N/A	0.025 J	N/A	N/A	N/A	N/A	N/A	N/A
2-Hexanone	mg/kg	1,300	0.0093 U	N/A	N/A	N/A	N/A	0.013 U	N/A	N/A	N/A	N/A	N/A	0.013 U	N/A	N/A	N/A	N/A	N/A	N/A
Acetone	mg/kg	670,000	0.0093 U	N/A	N/A	N/A	N/A	0.036	N/A	N/A	N/A	N/A	N/A	0.14 J	N/A	N/A	N/A	N/A	N/A	N/A
Benzene	mg/kg	5.1	0.0047 U	N/A	N/A	N/A	N/A	0.0065 U	N/A	N/A	N/A	N/A	N/A	0.0064 U	N/A	N/A	N/A	N/A	N/A	N/A
Carbon disulfide	mg/kg	3,500	0.0047 U	N/A	N/A	N/A	N/A	0.0065 U	N/A	N/A	N/A	N/A	N/A	0.0064 U	N/A	N/A	N/A	N/A	N/A	N/A
Cyclohexane	mg/kg	27,000	0.0093 U	N/A	N/A	N/A	N/A	0.013 U	N/A	N/A	N/A	N/A	N/A	0.013 UJ	N/A	N/A	N/A	N/A	N/A	N/A
Ethylbenzene	mg/kg	25	0.0047 U	N/A	N/A	N/A	N/A	0.0065 U	N/A	N/A	N/A	N/A	N/A	0.0064 U	N/A	N/A	N/A	N/A	N/A	N/A
Methyl Acetate	mg/kg	1,200,000	0.047 U	N/A	N/A	N/A	N/A	0.065 U	N/A	N/A	N/A	N/A	N/A	0.064 UJ	N/A	N/A	N/A	N/A	N/A	N/A
Methylene Chloride	mg/kg	1,000	0.0047 U	N/A	N/A	N/A	N/A	0.0065 U	N/A	N/A	N/A	N/A	N/A	0.0064 U	N/A	N/A	N/A	N/A	N/A	N/A
Tetrachloroethene	mg/kg	100	0.0047 U	N/A	N/A	N/A	N/A	0.0065 U	N/A	N/A	N/A	N/A	N/A	0.0064 U	N/A	N/A	N/A	N/A	N/A	N/A
Toluene	mg/kg	47,000	0.0047 U	N/A	N/A	N/A	N/A	0.0065 U	N/A	N/A	N/A	N/A	N/A	0.0064 U	N/A	N/A	N/A	N/A	N/A	N/A
Xylenes	mg/kg	2,800	0.014 U	N/A	N/A	N/A	N/A	0.019 U	N/A	N/A	N/A	N/A	N/A	0.019 U	N/A	N/A	N/A	N/A	N/A	N/A
Semi-Volatile Organic Compounds[^]																				
1,1-Biphenyl	mg/kg	200	0.017 J	0.073 U	0.074 U	0.077 U	0.079 U	0.081 U	0.029 J	0.071 U	0.074 U	0.075 U	0.081 U	0.1 U	0.079 U	0.073 U	0.082 U	0.083 U	0.074 U	0.082 U
1,2,4,5-Tetrachlorobenzene	mg/kg	350	0.078 U	0.073 U	0.074 U	0.077 U	0.079 U	0.081 U	0.071 U	0.071 U	0.074 U	0.075 U	0.081 U	0.1 U	0.079 U	0.073 U	0.082 U	0.083 U	0.074 U	0.082 U
2,4-Dimethylphenol	mg/kg	16,000	0.078 U	0.073 U	0.074 U	0.077 U	0.079 U	0.081 U	0.071 R	0.071 U	0.074 U	0.075 U	0.081 U	0.1 U	0.079 U	0.073 U	0.082 U	0.083 U	0.074 R	0.082 U
2-Chloronaphthalene	mg/kg	60,000	0.078 U	0.073 U	0.074 U	0.077 U	0.079 U	0.081 U	0.073 U	0.071 U	0.074 U	0.075 U	0.081 U	0.1 U	0.079 U	0.073 U	0.082 U	0.083 U	0.074 U	0.082 U
2-Methylnaphthalene	mg/kg	3,000	0.094	0.01	0.025	0.0095	0.001 J	0.056	0.24	0.035	0.0063 J	0.0011 J	0.0023 J	0.038	0.031 J	0.024	0.046 J	0.0084 U	0.15	0.0019 J
2-Methylphenol	mg/kg	41,000	0.078 U	0.073 U	0.074 U	0.077 U	0.079 U	0.081 U	0.071 R	0.071 U	0.074 U	0.075 U	0.081 U	0.1 U	0.079 U	0.073 U	0.082 U	0.083 U	0.074 R	0.082 U
3&4-Methylphenol(m&p Cresol)	mg/kg	41,000	0.16 U	0.15 U	0.15 U	0.15 U	0.16 U	0.16 U	0.14 R	0.14 U	0.15 U	0.15 U	0.16 U	0.2 U	0.16 U	0.15 U	0.16 U	0.16 U	0.15 R	0.16 U
Acenaphthene	mg/kg	45,000	0.27	0.0012 J	0.0039 J	0.00099 J	0.0079 U	0.085	0.0024 J	0.0078	0.00067 J	0.0074 U	0.0081 U	0.0067 J	0.13	0.14	0.077 J	0.0084 U	0.0058 J	0.0083 U
Acenaphthylene	mg/kg	45,000	0.023 J	0.0043 J	0.009	0.0047 J	0.0079 U	0.019	0.0049 J	0.078	0.0015 J	0.00062 J	0.0027 J	0.013	0.067 J	0.0044 J	0.027 J	0.0084 U	0.0054 J	0.0011 J
Acetophenone	mg/kg	120,000	0.078 U	0.073 U	0.074 U	0.077 U	0.079 U	0.081 U	0.071 U	0.071 U	0.074 U	0.075 U	0.081 U	0.1 U	0.079 U	0.073 U	0.082 U	0.083 U	0.074 U	0.082 U
Anthracene	mg/kg	230,000	0.17	0.011	0.019	0.0037 B	0.00055 B	0.31	0.026	0.1	0.0037 J	0.0011 J	0.0017 J	0.02	0.13	0.028	0.28	0.00083 B	0.016 J	0.0018 J
Benz[a]anthracene	mg/kg	21	0.19	0.029	0.052	0.021	0.0039 J	0.79	0.033 J	0.56 J	0.0092	0.0074 U	0.014	0.058	0.69	0.22	0.18	0.0044 J	0.072 J	0.008 J
Benzaldehyde	mg/kg	120,000	0.078 U	0.073 U	0.074 U	0.077 U	0.079 U	0.081 U	0.071 U	0.071 U	0.074 U	0.075 U	0.081 U	0.076 J	0.021 J	0.073 U	0.026 J	0.083 U	0.04 J	0.082 U
Benzo[a]pyrene	mg/kg	2.1	0.12	0.022	0.046	0.022	0.0033 J	0.66	0.071 U	0.57 J	0.0068 J	0.0074 U	0.01	0.053	0.86	0.51	1.7	0.0041 J	0.044 J	0.0071 J
Benzo[b]fluoranthene	mg/kg	21	0.17	0.049	0.11	0.036	0.0052 J	0.96	0.14	1.3	0.02	0.0074 U	0.019	0.093	1.2	0.65	2.6	0.0065 J	0.13	0.018
Benzo[g,h,i]perylene	mg/kg		0.059 J	0.017	0.045	0.017	0.0027 J	0.37	0.019 J	0.37	0.0057 B	0.0074 U	0.0058 J	0.046	0.67	0.52	0.95	0.004 J	0.062 J	0.0024 J
Benzo[k]fluoranthene	mg/kg	210	0.063 J	0.038	0.086	0.01	0.002 J	0.3	0.13	1.1	0.015	0.0074 U	0.016	0.03	0.41	0.21	0.99	0.002 J	0.12	0.016
bis(2-Ethylhexyl)phthalate	mg/kg	160	0.078 U	0.073 U	0.074 U	0.077 U	0.079 U	0.081 U	0.071 U	0.053 B	0.074 U	0.075 U	0.081 U	0.1 U	0.024 J	0.073 U	0.056 J	0.02 J	0.074 UJ	0.082 U
Caprolactam	mg/kg	400,000	0.2 U	0.18 U	0.19 U	0.19 U	0.2 U	0.2 U	0.18 U	0.18 U	0.18 U	0.19 U	0.2 U	0.25 U	0.2 U	0.18 U	0.2 U	0.21 U	0.19 U	0.2 U
Carbazole	mg/kg		0.066 J	0.073 U	0.074 U	0.077 U	0.079 U	0.081 U	0.021 J	0.058 J	0.074 U	0.075 U	0.081 U	0.048 J	0.079 U	0.018 J	0.082 U	0.083 U	0.074 U	0.082 U
Chrysene	mg/kg	2,100	0.18	0.03	0.06	0.023	0.0039 J	0.76	0.17	0.54 J	0.016	0.00091 J	0.011	0.069	0.64	0.22	1.8	0.004 J	0.16	0.011
Dibenz[a,h]anthracene	mg/kg	2.1	0.079 U	0.0034 J	0.011	0.0053 J	0.0079 U	0.12	0.071 U	0.14	0.0015 J	0.0074 U	0.0018 J	0.013	0.18	0.15	0.25	0.0084 U	0.074 U	0.0083 U
Diethylphthalate	mg/kg	660,000	0.078 U	0.073 U	0.074 U	0.018 J	0.018 J	0.021 J	0.071 U	0.071 U	0.074 U	0.075 U	0.043 B	0.053 B	0.02 J	0.016 J	0.082 U	0.083 U	0.074 U	0.082 U
Di-n-butylphthalate	mg/kg	82,000	0.025 B	0.073 U	0.074 U	0.039 B	0.046 B	0.058 B	0.031 B	0.52 J	0.02 B	0.025 B	0.088 B	0.081 B	0.049 B	0.038 B	0.032 B	0.23	0.041 B	0.037 B
Di-n-octylphthalate	mg/kg	8,200	0.078 U	0.073 U	0.074 U	0.077 U	0.079 U	0.081 U	0.071 U	0.029 J	0.074 U	0.075 U	0.081 U	0.1 U	0.079 U	0.073 U	0.082 U	0.083 U	0.16 J	0.082 U
Fluoranthene	mg/kg	30,000	0.86	0.061	0.14	0.039	0.0062 B	1.8	0.52	0.82 J	0.015	0.0033 J	0.018	0.12	1.2	0.25	3.5	0.0076 B	0.12	0.013
Fluorene	mg/kg	30,000	0.31	0.0016 J	0.0024 J	0.0013 J	0.0079 U	0.093	0.0031 J	0.0097	0.0012 J	0.0074 U	0.0081 U	0.012	0.032 J	0.012	0.075 J	0.0084 U	0.0077 J	0.0083 U
Hexachloroethane	mg/kg	8	0.078 U	0.073 U	0.074 U	0.077 U	0.079 U	0.081 U	0.071 U	0.071 U	0.074 U	0.075 U	0.081 U	0.1 U	0.079 U	0.073 U	0.082 U	0.083 U	0.074 U	0.082 U
Indeno[1,2,3-c,d]pyrene	mg/kg	21	0.053 J	0.014	0.037	0.015	0.002 J	0.35	0.021 J	0.35 J	0.0045 J	0.0074 U	0.0053 J	0.041	0.6	0.48	0.92	0.0031 J	0.018 J	0.0025 J
Isophorone	mg/kg	2,400	0.078 U	0.073 U	0.074 U	0.077 U	0.079 U	0.081 U	0.071 U	0.071 U	0.074 U	0.075 U	0.081 U	0.1 U	0.079 U	0.073 U	0.082 U	0.083 U	0.074 U	0.082 U
Naphthalene	mg/kg	17	0.12	0.025	0.11	0.016	0.0079 U	0.08	0.28	0.043	0.0064 J	0.0035 J	0.0071 J	0.31	0.044 J	0.039	0.064 J	0.0084 U	0.092	0.0083 U
N-Nitrosodiphenylamine	mg/kg	470	0.078 U	0.073 U	0.074 U	0.077 U	0.079 U	0.081 U	0.071 U	0.071 U	0.074 U	0.075 U	0.081 U	0.1 U	0.079 U	0.073 U	0.082 U	0.083 U	0.074 U	0.082 U
Phenanthrene	mg/kg		1.2	0.059	0.13	0.02														

Table 1 - Sub-Parcel B2-2
Summary of Organics Detected in Soil

Parameter	Units	PAL	B2-051-SB-1	B2-051-SB-5	B2-052-SB-1	B2-052-SB-5	B5-011-SB-1	B5-011-SB-5	B5-012-SB-1	B5-012-SB-5	B5-013-SB-1	B5-013-SB-4.5	B5-014-SB-1	B5-014-SB-4	B5-033-SB-1*	B5-033-SB-8*	B5-034-SB-1*	B5-039-SB-1	B5-039-SB-5	B5-040-SB-1	B5-040-SB-5
Volatile Organic Compounds																					
1,1,1-Trichloroethane	mg/kg	36,000	N/A	N/A	N/A	N/A	0.0068 U	0.0052 U	0.0056 U	0.005 U	0.0061 U	0.042	0.0064 U	0.0063 U	0.25 U	0.29 U	0.004 U	0.0045 U	0.0049 U	0.0043 U	0.0058 U
1,2,3-Trichlorobenzene	mg/kg	930	N/A	N/A	N/A	N/A	0.0068 U	0.0052 U	0.0056 U	0.005 U	0.0061 U	0.0077 U	0.0064 U	0.0063 U	0.24 J	0.29 U	0.004 U	0.0045 U	0.0049 U	0.0043 U	0.0058 U
1,2,4-Trichlorobenzene	mg/kg	110	N/A	N/A	N/A	N/A	0.0068 U	0.0052 U	0.0056 U	0.005 U	0.0061 U	0.0077 U	0.0064 U	0.0063 U	0.22 J	0.29 U	0.004 U	0.0045 U	0.0049 U	0.0043 U	0.0058 U
1,2-Dichloroethane	mg/kg	2	N/A	N/A	N/A	N/A	0.0068 U	0.0052 U	0.0056 U	0.005 U	0.0061 U	0.0077 U	0.0064 U	0.0063 U	0.25 U	0.29 U	0.004 U	0.0045 U	0.0049 U	0.0043 U	0.0058 U
2-Butanone (MEK)	mg/kg	190,000	N/A	N/A	N/A	N/A	0.014 U	0.01 U	0.011 U	0.01 U	0.012 U	0.015 U	0.013 U	0.013 U	0.5 U	0.59 U	0.0081 U	0.0091 U	0.0098 U	0.0086 U	0.012 U
2-Hexanone	mg/kg	1,300	N/A	N/A	N/A	N/A	0.014 U	0.01 U	0.011 U	0.01 U	0.012 U	0.015 U	0.013 U	0.013 U	0.5 U	0.59 U	0.0081 U	0.0091 U	0.0098 U	0.0086 U	0.012 U
Acetone	mg/kg	670,000	N/A	N/A	N/A	N/A	0.058	0.04	0.1	0.032	0.012 U	0.047	0.013 U	0.013 U	0.5 U	0.59 U	0.086	0.05	0.0098 U	0.031	0.046
Benzene	mg/kg	5.1	N/A	N/A	N/A	N/A	0.0068 U	0.0052 U	0.0056 U	0.005 U	0.0061 U	0.0077 U	0.0064 U	0.0084	0.25 U	0.29 U	0.004 J	0.0045 U	0.0049 U	0.0043 U	0.0058 U
Carbon disulfide	mg/kg	3,500	N/A	N/A	N/A	N/A	0.0068 U	0.0052 U	0.0056 U	0.005 U	0.0061 U	0.0077 U	0.0064 U	0.0063 U	0.25 U	0.29 U	0.004 U	0.0045 U	0.0049 U	0.0043 U	0.0058 U
Cyclohexane	mg/kg	27,000	N/A	N/A	N/A	N/A	0.014 U	0.01 U	0.014	0.01 U	0.012 U	0.015 U	0.013 U	0.013 U	0.5 U	0.59 U	0.0081 U	0.0091 U	0.0098 U	0.0086 U	0.012 U
Ethylbenzene	mg/kg	25	N/A	N/A	N/A	N/A	0.0068 U	0.0052 U	0.0056 U	0.005 U	0.0061 U	0.0077 U	0.0064 U	0.0063 U	0.25 U	0.29 U	0.004 U	0.0045 U	0.0049 U	0.0043 U	0.0058 U
Methyl Acetate	mg/kg	1,200,000	N/A	N/A	N/A	N/A	0.068 U	0.052 U	0.056 U	0.05 U	0.061 U	0.077 U	0.064 U	0.063 U	2.5 U	2.9 U	0.04 U	0.045 U	0.049 U	0.043 U	0.058 U
Methylene Chloride	mg/kg	1,000	N/A	N/A	N/A	N/A	0.0068 U	0.0052 U	0.0056 U	0.005 U	0.0061 U	0.0077 U	0.0064 U	0.0063 U	0.25 U	0.29 U	0.004 U	0.0045 U	0.0049 U	0.0043 U	0.0058 U
Tetrachloroethene	mg/kg	100	N/A	N/A	N/A	N/A	0.0068 U	0.0052 U	0.0056 U	0.005 U	0.0061 U	0.0077 U	0.0064 U	0.0063 U	0.25 U	0.29 U	0.004 U	0.0045 U	0.0049 U	0.0042 J	0.0038 J
Toluene	mg/kg	47,000	N/A	N/A	N/A	N/A	0.0068 U	0.0052 U	0.0031 J	0.005 U	0.0061 U	0.0042 J	0.0064 U	0.0044 J	0.25 U	0.29 U	0.0018 J	0.0045 U	0.0049 U	0.0043 U	0.0058 U
Xylenes	mg/kg	2,800	N/A	N/A	N/A	N/A	0.021 U	0.016 U	0.017 U	0.015 U	0.018 U	0.023 U	0.019 U	0.019 U	0.75 U	0.88 U	0.012 U	0.014 U	0.015 U	0.013 U	0.018 U
Semi-Volatile Organic Compounds[^]																					
1,1-Biphenyl	mg/kg	200	0.021 J	0.07 U	0.074 U	0.078 U	7.1 U	7.7 U	8 U	8.2 U	7.1 U	7.6 U	7.9 U	7.5 U	7.1 U	7.4 U	7.4 U	7.3 U	7.3 U	7.3 U	8.6 U
1,2,4,5-Tetrachlorobenzene	mg/kg	350	0.071 U	0.07 U	0.074 U	0.078 U	7.1 U	7.7 U	8 U	8.2 U	7.1 U	7.6 U	7.9 U	7.5 U	7.1 U	7.4 U	7.4 U	7.3 U	7.3 U	7.3 U	8.6 U
2,4-Dimethylphenol	mg/kg	16,000	0.071 R	0.07 R	0.074 U	0.078 U	7.1 U	7.7 U	8 U	8.2 U	7.1 U	7.6 U	7.9 U	7.5 U	7.1 U	7.4 U	7.4 U	7.3 U	7.3 U	7.3 U	8.6 U
2-Chloronaphthalene	mg/kg	60,000	0.071 U	0.07 U	0.074 U	0.078 U	7.1 U	7.7 U	8 U	8.2 U	7.1 U	7.6 U	7.9 U	7.5 U	7.1 U	7.4 U	7.4 U	7.3 U	7.3 U	7.3 U	8.6 U
2-Methylnaphthalene	mg/kg	3,000	0.12	0.11	0.098	0.0041 J	0.036 J	0.15 U	0.2	0.023	0.14 U	0.25	0.14 J	0.12	3.6 U	0.37 U	0.21	0.0074 U	0.075	0.0097	0.13
2-Methylphenol	mg/kg	41,000	0.071 R	0.07 R	0.074 U	0.078 U	7.1 U	7.7 U	8 U	8.2 U	7.1 U	7.6 U	7.9 U	7.5 U	7.1 U	7.4 U	7.4 U	7.3 U	7.3 U	7.3 U	8.6 U
3&4-Methylphenol(m&p Cresol)	mg/kg	41,000	0.14 R	0.14 R	0.15 U	0.16 U	14.3 U	15.4 U	15.9 U	16.3 U	14.3 U	15.3 U	15.9 U	14.9 U	14.2 U	14.8 U	14.8 U	14.6 U	14.6 U	14.6 U	17.2 U
Acenaphthene	mg/kg	45,000	0.071 U	0.0083 J	0.059 J	0.035	0.03 J	0.15 U	0.53	0.16	0.14 U	0.0092	0.16 U	0.0075 J	3.6 U	0.37 U	1	0.0074 U	0.0065 J	0.0073 U	0.0073 J
Acenaphthylene	mg/kg	45,000	0.071 U	0.073	0.17	0.0023 J	0.047 J	0.022 J	0.074 J	0.028	0.052 J	0.075	0.13 J	0.11	0.45 J	0.053 J	0.024 J	0.00074 J	0.0074 J	0.0073 U	0.014
Acetophenone	mg/kg	120,000	0.071 U	0.07 U	0.074 U	0.078 U	7.1 U	7.7 U	8 U	8.2 U	7.1 U	7.6 U	7.9 U	7.5 U	7.1 U	7.4 U	7.4 U	7.3 U	7.3 U	7.3 U	8.6 U
Anthracene	mg/kg	230,000	0.071 U	0.1	0.28	0.094	0.067 J	0.023 J	1.3	0.41	0.14 U	0.11	0.12 J	0.032	0.099	0.37 U	0.8	0.0074 U	0.052	0.0047 J	0.043
Benz[a]anthracene	mg/kg	21	0.04 J	0.49	0.78	0.15	0.34	0.087 J	2.6	1.5	0.1 J	0.37	0.76	0.13	0.29	0.099	2.9	0.002 J	0.37	0.024	0.12
Benzaldehyde	mg/kg	120,000	0.071 R	0.07 R	0.018 J	0.078 U	7.1 U	7.7 U	8 U	8.2 U	7.1 U	7.6 U	7.9 U	7.5 U	7.1 U	7.4 U	7.4 U	7.3 U	7.3 U	7.3 U	8.6 U
Benzo[a]pyrene	mg/kg	2.1	0.016 J	0.37	0.75	0.13	0.26	0.057 J	1.8	1.1	0.031 J	0.29	0.56	0.12	0.46	0.22	1.4	0.0011 J	0.38	0.026	0.096
Benzo[b]fluoranthene	mg/kg	21	0.063 J	0.92	1.9	0.23	0.65	0.14 J	3.8	1.6	0.14 J	0.59	1.5	0.27	1.1	0.42	4.1	0.003 J	1.4	0.04	0.19
Benzo[g,h,i]perylene	mg/kg		0.047 J	0.11	0.38	0.044	0.13 J	0.049 J	0.85	0.48	0.05 J	0.08	0.29	0.053	0.22	0.083	0.57	0.0018 J	0.45	0.026	0.081
Benzo[k]fluoranthene	mg/kg	210	0.043 J	0.63	1.7	0.21	0.64	0.14 J	3.8	0.64	0.13 J	0.24	1.5	0.093	1.1	0.42	2	0.001 J	1.4	0.026	0.068
bis(2-Ethylhexyl)phthalate	mg/kg	160	0.071 U	0.07 U	0.081	0.016 B	7.1 U	7.7 U	8 U	8.2 U	7.1 U	7.6 U	7.9 U	7.5 U	7.1 U	7.4 U	7.4 U	7.3 U	7.3 U	7.3 U	8.6 U
Caprolactam	mg/kg	400,000	0.18 U	0.18 U	0.18 U	0.2 U	17.8 U	19.2 U	19.9 U	20.4 U	17.9 U	19.1 U	19.9 U	18.7 U	17.8 U	18.5 U	18.5 U	18.3 U	18.3 U	18.3 U	21.5 U
Carbazole	mg/kg		0.071 U	0.032 J	0.071 J	0.078 U	7.1 U	7.7 U	8 U	8.2 U	7.1 U	7.6 U	7.9 U	7.5 U	7.1 U	7.4 U	7.4 U	7.3 U	7.3 U	7.3 U	8.6 U
Chrysene	mg/kg	2,100	0.12	0.32	0.85	0.14	0.44	0.082 J	2.6	1.4	0.061 J	0.6	0.82	0.24	0.42	0.13	4.6	0.0025 J	0.75	0.032	0.32
Dibenz[a,h]anthracene	mg/kg	2.1	0.071 U	0.035 J	0.13	0.015	0.051 J	0.15 U	0.4	0.22	0.14 U	0.058	0.11 J	0.03	0.079	0.032	0.22	0.0074 U	0.21	0.0091	0.045
Diethylphthalate	mg/kg	660,000	0.071 U	0.07 U	0.074 U	0.078 U	7.1 U	7.7 U	8 U	8.2 U	7.1 U	7.6 U	7.9 U	7.5 U	7.1 U	7.4 U	7.4 U	7.3 U	7.3 U	7.3 U	8.6 U
Di-n-butylphthalate	mg/kg	82,000	0.071 U	0.07 U	0.077	0.081	7.1 U	7.7 U	8 U	8.2 U	7.1 U	7.6 U	7.9 U	7.5 U	7.1 U	7.4 U	7.4 U	7.3 U	7.3 U	7.3 U	8.6 U
Di-n-octylphthalate	mg/kg	8,200	0.071 U	0.07 U	0.074 U	0.078 U	7.1 U	7.7 U	8 U	8.2 U	7.1 U	7.6 U	7.9 U	7.5 U	7.1 U	7.4 U	7.4 U	7.3 U	7.3 U	7.3 U	8.6 U
Fluoranthene	mg/kg	30,000	0.12	0.74	1.1	0.38	0.61	0.1 J	5.6	5.8	0.03 J	0.65	1	0.23	0.61	0.097 J	6.2	0.0027 J	0.42	0.027	0.2
Fluorene	mg/kg	30,000	0.071 U	0.0063 J	0.031 J	0.026	0.024 J	0.15 U	0.77	0.16	0.14 U	0.025	0.027 J	0.018	0.49 J	0.37 U	0.46	0.0074 U	0.0064 J	0.00067 J	0.011
Hexachloroethane	mg/kg	8	0.071 U	0.07 U	0.074 U	0.078 U	7.1 U	7.7 U	8 U	8.2 U	7.1 U	7.6 U	7.9 U	7.5 U	7.1 U	7.4 U	7.4 U	7.3 U	7.3 U	7.3 U	8.6 U
Indeno[1,2,3-c,d]pyrene	mg/kg	21	0.071 U	0.12	0.37	0.046	0.12 J	0.031 J	0.85	0.51	0.14 U	0.089	0.27	0.058	0.2	0.078	0.57	0.0012 J			

Table 1 - Sub-Parcel B2-2
Summary of Organics Detected in Soil

Parameter	Units	PAL	B5-081-SB-1*	B5-081-SB-5*	B5-082-SB-1*	B5-082-SB-5*	B5-083-SB-1*	B5-083-SB-5*	B5-084-SB-1*	B5-085-SB-1	B5-090-SB-1	B5-090-SB-4.75	B5-091-SB-1*	B5-091-SB-7*	B5-134-SB-1	B5-135-SB-1	B5-135-SB-5	B5-176-SB-1	B5-176-SB-5	
Volatile Organic Compounds																				
1,1,1-Trichloroethane	mg/kg	36,000	0.0056 U	0.0052 U	0.0062 U	0.0046 U	0.0049 U	0.0038 U	0.0044 U	0.0048 U	0.0053 U	0.0045 U	0.0039 U	0.0042 U	0.0076 U	0.0059 U	0.0042 U	0.0056 U	0.0094 U	
1,2,3-Trichlorobenzene	mg/kg	930	0.0056 U	0.0052 U	0.0062 U	0.0046 U	0.0049 U	0.0038 U	0.0044 U	0.0048 U	0.0053 U	0.0045 U	0.0039 U	0.0042 U	0.0076 U	0.0059 U	0.0042 U	0.0056 U	0.0094 U	
1,2,4-Trichlorobenzene	mg/kg	110	0.0056 U	0.0052 U	0.0062 U	0.0046 U	0.0049 U	0.0038 U	0.0044 U	0.0048 U	0.0053 U	0.0045 U	0.0039 U	0.0042 U	0.0076 U	0.0059 U	0.0042 U	0.0056 U	0.0094 U	
1,2-Dichloroethane	mg/kg	2	0.0056 U	0.0052 U	0.0062 U	0.0046 U	0.0049 U	0.0038 U	0.0044 U	0.0048 U	0.0053 U	0.0045 U	0.0039 U	0.0042 U	0.0076 U	0.0059 U	0.0042 U	0.0056 U	0.0094 U	
2-Butanone (MEK)	mg/kg	190,000	0.011 U	0.01 U	0.012 U	0.0092 U	0.0098 U	0.0076 U	0.0087 U	0.0097 U	0.011 U	0.0031 J	0.0078 U	0.0084 U	0.015 U	0.012 U	0.0084 U	0.011 U	0.019 U	
2-Hexanone	mg/kg	1,300	0.011 U	0.01 U	0.012 U	0.0092 U	0.0098 U	0.0076 U	0.0087 U	0.0097 U	0.011 U	0.009 U	0.0078 U	0.0084 U	0.015 U	0.012 U	0.0084 U	0.011 U	0.019 U	
Acetone	mg/kg	670,000	0.011 U	0.046	0.098	0.0092 U	0.049	0.0076 U	0.073	0.07	0.011 U	0.035 B	0.096	0.0084 U	0.1	0.012 U	0.0084 U	0.09	0.019 U	
Benzene	mg/kg	5.1	0.0056 U	0.0052 U	0.0062 U	0.0046 U	0.0049 U	0.0038 U	0.0083	0.0064	0.0053 U	0.0045 U	0.0039 U	0.0042 U	0.0076 U	0.0059 U	0.0042 U	0.0056 U	0.0094 U	
Carbon disulfide	mg/kg	3,500	0.0056 U	0.0052 U	0.0062 U	0.0046 U	0.0049 U	0.0038 U	0.0044 U	0.0048 U	0.0053 U	0.0045 U	0.0039 U	0.0042 U	0.0076 U	0.0059 U	0.0042 U	0.0056 U	0.0094 U	
Cyclohexane	mg/kg	27,000	0.011 U	0.01 U	0.012 U	0.0092 U	0.0098 U	0.0076 U	0.0087 U	0.0097 U	0.011 U	0.009 U	0.0078 U	0.0084 U	0.015 U	0.012 U	0.0084 U	0.011 U	0.019 U	
Ethylbenzene	mg/kg	25	0.0056 U	0.0052 U	0.0062 U	0.0046 U	0.0049 U	0.0038 U	0.0044 U	0.0048 U	0.0053 U	0.003 J	0.0039 U	0.0042 U	0.0076 U	0.0059 U	0.0042 U	0.0056 U	0.0094 U	
Methyl Acetate	mg/kg	1,200,000	0.056 U	0.052 U	0.062 U	0.046 U	0.049 U	0.038 U	0.044 U	0.048 U	0.053 U	0.045 U	0.039 U	0.042 U	0.076 U	0.059 U	0.042 U	0.056 U	0.094 U	
Methylene Chloride	mg/kg	1,000	0.0056 U	0.0052 U	0.0062 U	0.0046 U	0.0049 U	0.0038 U	0.0044 U	0.0048 U	0.0053 U	0.0045 U	0.0039 U	0.0042 U	0.0076 U	0.0059 U	0.0042 U	0.0056 U	0.0094 U	
Tetrachloroethene	mg/kg	100	0.0056 U	0.0052 U	0.0062 U	0.0046 U	0.0049 U	0.0038 U	0.0044 U	0.0048 U	0.0053 U	0.0045 U	0.0039 U	0.0042 U	0.0076 U	0.0059 U	0.0042 U	0.0056 U	0.0094 U	
Toluene	mg/kg	47,000	0.0056 U	0.0052 U	0.0062 U	0.0046 U	0.0049 U	0.0038 U	0.0021 J	0.0043 J	0.0053 U	0.0045 U	0.0039 U	0.0042 U	0.0076 U	0.0059 U	0.0042 U	0.0056 U	0.0094 U	
Xylenes	mg/kg	2,800	0.017 U	0.016 U	0.019 U	0.014 U	0.015 U	0.011 U	0.013 U	0.015 U	0.016 U	0.0068 J	0.012 U	0.013 U	0.023 U	0.018 U	0.013 U	0.017 U	0.028 U	
Semi-Volatile Organic Compounds^																				
1,1-Biphenyl	mg/kg	200	7.2 U	8.2 U	7.4 U	7.9 U	7.7 U	7.9 U	7.1 U	7.4 U	0.073 U	0.08 U	7.2 U	7.6 U	9.3 U	7.5 U	7.8 U	7.5 U	7.9 U	
1,2,4,5-Tetrachlorobenzene	mg/kg	350	7.2 U	8.2 U	7.4 U	7.9 U	7.7 U	7.9 U	7.1 U	7.4 U	0.073 U	0.08 U	7.2 U	7.6 U	9.3 U	7.5 U	7.8 U	7.5 U	7.9 U	
2,4-Dimethylphenol	mg/kg	16,000	7.2 U	8.2 U	7.4 U	7.9 U	7.7 U	7.9 U	7.1 U	7.4 U	0.073 U	0.08 U	7.2 U	7.6 U	9.3 U	7.5 U	7.8 U	7.5 U	7.9 U	
2-Chloronaphthalene	mg/kg	60,000	7.2 U	8.2 U	7.4 U	7.9 U	7.7 U	7.9 U	7.1 U	7.4 U	0.073 U	0.08 U	7.2 U	7.6 U	9.3 U	7.5 U	7.8 U	7.5 U	7.9 U	
2-Methylnaphthalene	mg/kg	3,000	0.023 J	0.0016 J	0.15 U	0.0079 U	0.068 J	0.0011 J	0.013	0.037	0.025 J	0.0063 J	0.059	0.034	0.41	0.15 U	0.0079 U	0.074	0.12 J	
2-Methylphenol	mg/kg	41,000	7.2 U	8.2 U	7.4 U	7.9 U	7.7 U	7.9 U	7.1 U	7.4 U	0.073 U	0.08 U	7.2 U	7.6 U	9.3 U	7.5 U	7.8 U	7.5 U	7.9 U	
3&4-Methylphenol(m&p Cresol)	mg/kg	41,000	14.5 U	16.4 U	14.9 U	15.7 U	15.5 U	15.7 U	14.2 U	14.7 U	0.15 U	0.16 U	14.4 U	15.2 U	18.6 U	14.9 U	15.6 U	15 U	15.9 U	
Acenaphthene	mg/kg	45,000	0.15 U	0.0082 U	0.15 U	0.0079 U	0.15 U	0.008 U	0.019	0.032	0.0026 J	0.035	0.054	0.054	0.018 J	0.15 U	0.0079 U	0.0056 J	0.16 U	
Acenaphthylene	mg/kg	45,000	0.15 U	0.0082 U	0.15 U	0.0079 U	0.02 J	0.008 U	0.0024 J	0.0063 J	0.0027 J	0.008 U	0.019	0.0026 J	0.037 J	0.15 U	0.0079 U	0.018	0.16 U	
Acetophenone	mg/kg	120,000	7.2 U	8.2 U	7.4 U	7.9 U	7.7 U	7.9 U	7.1 U	7.4 U	0.073 U	0.08 U	7.2 U	7.6 U	9.3 U	7.5 U	7.8 U	7.5 U	7.9 U	
Anthracene	mg/kg	230,000	0.15 U	0.0013 J	0.15 U	0.0079 U	0.071 J	0.0011 J	0.029	0.1	0.019	0.023	0.25	0.038	0.14 J	0.015 J	0.0079 U	0.046	0.065 J	
Benz[a]anthracene	mg/kg	21	0.057 J	0.0044 J	0.055 J	0.0079 U	0.36	0.0022 J	0.23	0.82	0.24 J	0.0071 J	0.75	0.086	0.29	0.15 U	0.0079 U	0.11	0.15 J	
Benzaldehyde	mg/kg	120,000	7.2 U	8.2 U	7.4 U	7.9 U	7.7 U	7.9 U	7.1 U	7.4 U	0.073 U	0.08 U	7.2 U	7.6 U	9.3 U	7.5 U	7.8 U	7.5 U	7.9 U	
Benzo[a]pyrene	mg/kg	2.1	0.15 U	0.0031 J	0.022 J	0.0079 U	0.34 J	0.0043 J	0.34	1.1	0.22 J	0.0064 J	0.95	0.11	0.31	0.05 J	0.0079 U	0.11	0.17	
Benzo[b]fluoranthene	mg/kg	21	0.069 J	0.0094	0.056 J	0.00071 J	0.49	0.01	0.78	3.5	0.63 J	0.02	3.1	0.29	0.67	0.1 J	0.0079 U	0.34	0.41	
Benzo[g,h,i]perylene	mg/kg		0.15 U	0.0026 J	0.026 J	0.0079 U	0.31 J	0.0045 J	0.14	0.36	0.19 J	0.0066 J	0.44	0.035	0.28	0.029 J	0.0079 U	0.04	0.12 J	
Benzo[k]fluoranthene	mg/kg	210	0.057 J	0.0077 J	0.021 J	0.0079 U	0.22 J	0.0086	0.77	3.4	0.62 J	0.02	3.1	0.29	0.27	0.028 J	0.0079 U	0.34	0.33	
bis(2-Ethylhexyl)phthalate	mg/kg	160	7.2 U	8.2 U	7.4 U	7.9 U	7.7 U	7.9 U	7.1 U	7.4 U	0.073 U	0.08 U	7.2 U	7.6 U	9.3 U	7.5 U	7.8 U	7.5 U	7.9 U	
Caprolactam	mg/kg	400,000	18.1 U	20.5 U	18.6 U	19.6 U	19.4 U	19.6 U	17.8 U	18.4 U	0.18 U	0.2 U	18 U	19 U	23.2 U	18.6 U	19.5 U	18.8 U	19.9 U	
Carbazole	mg/kg		7.2 U	8.2 U	7.4 U	7.9 U	7.7 U	7.9 U	7.1 U	7.4 U	0.073 U	0.08 U	7.2 U	7.6 U	9.3 U	7.5 U	7.8 U	7.5 U	7.9 U	
Chrysene	mg/kg	2,100	0.024 J	0.0037 J	0.027 J	0.0079 U	0.47	0.0092	0.33	0.99	0.37 J	0.014	0.86	0.12	0.49	0.095 J	0.0079 U	0.18	0.27	
Dibenz[a,h]anthracene	mg/kg	2.1	0.15 U	0.0082 U	0.15 U	0.0079 U	0.11 J	0.0022 J	0.047	0.14	0.072 J	0.0018 J	0.14	0.012	0.1 J	0.15 U	0.0079 U	0.019	0.048 J	
Diethylphthalate	mg/kg	660,000	7.2 U	8.2 U	7.4 U	7.9 U	7.7 U	7.9 U	7.1 U	7.4 U	0.073 U	0.08 U	7.2 U	7.6 U	9.3 U	7.5 U	7.8 U	7.5 U	7.9 U	
Di-n-butylphthalate	mg/kg	82,000	7.2 U	8.2 U	7.4 U	7.9 U	7.7 U	7.9 U	7.1 U	7.4 U	0.073 U	0.08 U	7.2 U	7.6 U	9.3 U	7.5 U	7.8 U	7.5 U	7.9 U	
Di-n-octylphthalate	mg/kg	8,200	7.2 U	8.2 U	7.4 U	7.9 U	7.7 U	7.9 U	7.1 U	7.4 U	0.073 U	0.08 U	7.2 U	7.6 U	9.3 U	7.5 U	7.8 U	7.5 U	7.9 U	
Fluoranthene	mg/kg	30,000	0.028 J	0.0078 J	0.042 J	0.00057 J	0.47	0.0029 J	0.29	1.1	0.37 J	0.025	2.6	0.23	0.63	0.054 J	0.0079 U	0.19	0.28	
Fluorene	mg/kg	30,000	0.016 J	0.00072 J	0.15 U	0.0079 U	0.019 J	0.008 U	0.012	0.025	0.0025 J	0.025	0.055	0.042	0.036 J	0.15 U	0.0079 U	0.0067 J	0.16 U	
Hexachloroethane	mg/kg	8	7.2 U	8.2 U	7.4 U	7.9 U	7.7 U	7.9 U	7.1 U	7.4 U	0.073 U	0.08 U	7.2 U	7.6 U	9.3 U	7.5 U	7.8 U	7.5 U	7.9 U	
Indeno[1,2,3-c,d]pyrene	mg/kg	21	0.15 U	0.0025 J	0.15 U	0.0079 U	0.25 J	0.002 J	0.12	0.33	0.17 J	0.0051 J	0.39	0.031	0.19 J	0.02 J	0.0079 U	0.038	0.11 J	
Isophorone	mg/kg	2,400	7.2 U	8.2 U	7.4 U	7.9 U	7.7 U	7.9 U	7.1 U	7.4 U	0.073 U	0.08 U	7.2 U	7.6 U	9.3 U	7.5 U	7.8 U	7.5 U	7.9 U	
Naphthalene	mg/kg	17	0.061 B	0.004 B	0.063 B	0.002 B	0.093 B	0.0021 B	0.013	0.028	0.03 J	0.024	0.046	0.037	0.29 B	0.031 B	0.0021 B	0.043	0.068 B	
N-Nitrosodiphenylamine	mg/kg	470	7.2 U	8.2 U	7.4 U	7.9 U	7.7 U	7.9 U	7.1 U	7.4 U	0.073 U	0.08 U	7.2 U	7.6 U	9.3 U	7.5 U	7.8 U	7.5 U	7.9 U	

**Table 2 - Sub-Parcel B2-2
Summary of Inorganics Detected in Soil**

Parameter	Units	PAL	B2-003-SB-1*	B2-003-SB-4.5*	B2-004-SB-1*	B2-004-SB-5*	B2-023-SB-1*	B2-023-SB-4*	B2-024-SB-1*	B2-025-SB-1*
Metals										
Aluminum	mg/kg	1,100,000	9,600	11,600	16,000	4,610	51,000	15,700	42,000	13,400
Antimony	mg/kg	470	2.8 U	2.3 U	2.7 U	2.3 U	2.7 U	2.6 U	2.6 U	2.5 U
Arsenic	mg/kg	3	13.3	10.3	2.2 U	5.6	2.3 U	24.3	2.4	10.6
Barium	mg/kg	220,000	176	552	50.2	45.6	329	105	840	92.6
Beryllium	mg/kg	2,300	0.64 J	0.56 J	0.13 J	0.17 J	7.1	1.1	3.1	1.1
Cadmium	mg/kg	980	5.9	2.3	0.59 J	1.1 U	1.4 U	1.3 J	0.69 J	1.5
Chromium	mg/kg	120,000	306	642	1,180	55.6	8.5	346	171	28.9
Chromium VI	mg/kg	6.3	0.69 B	1 B	5.2	0.56 B	0.49 B	0.65 B	0.76 B	0.58 B
Cobalt	mg/kg	350	16.4	14.8	2.3 J	6.3	4.5 U	27.2	5.1	7
Copper	mg/kg	47,000	160	131	36.9	47.4	1.5 J	71.4	34.6	27.4
Iron	mg/kg	820,000	118,000	179,000	180,000	51,800	3,290	105,000	28,800	25,500
Lead	mg/kg	800	401	1,920	106	68.5	2.3 U	213	46.8	92.6
Manganese	mg/kg	26,000	7,140	13,400	24,500	1,220	2,850	7,800	7,350	736
Mercury	mg/kg	350	0.13	0.044 B	0.018 B	0.044 B	0.12 U	0.19	0.098 U	0.17
Nickel	mg/kg	22,000	49.1	33.1	19.3	16.7	9 U	30.4	14.7	14.3
Selenium	mg/kg	5,800	3.7 U	3.1 U	3.5 U	3.1 U	2.5 J	3.5 U	2.8 J	3.3 U
Silver	mg/kg	5,800	15	21.4	22.8	3.6	11.2	8.3	20.2	3.5
Thallium	mg/kg	12	9.3 U	7.8 U	8.9 U	7.7 U	9 U	8.7 U	8.6 U	8.3 U
Vanadium	mg/kg	5,800	720	3,260	806	320	9.2	396	163	43.8
Zinc	mg/kg	350,000	1,070	752	121	207	1.7 B	453	155	308
Other										
Cyanide	mg/kg	150	0.54 J	3.2	0.34 J	0.35 J	0.55 J	0.78 J	1.3	0.34 J

Detections in bold

Values in red indicate an exceedance of the Project Action Limit (PAL)

N/A indicates that the parameter was not analyzed for this sample

* indicates non-validated data

U: This analyte was not detected in the sample. The numeric value represents the sample quantitation/detection limit.

UJ: This analyte was not detected in the sample. The actual quantitation/detection limit may be higher than reported.

J: The positive result reported for this analyte is a quantitative estimate.

J+: The positive result reported for this analyte is a quantitative estimate but may be biased high.

J-: The positive result reported for this analyte is a quantitative estimate but may be biased low.

B: This analyte was not detected substantially above the level of the associated method blank/preparation or field blank.

R: The result for this analyte is unreliable. Additional data is needed to confirm or disprove the presence of this compound/analyte in the sample.

**Table 2 - Sub-Parcel B2-2
Summary of Inorganics Detected in Soil**

Parameter	Units	PAL	B2-025-SB-4*	B2-026-SB-1	B2-026-SB-5	B2-026-SB-10	B2-027-SB-1	B2-029-SB-1*	B2-029-SB-8*	B2-029-SB-10*
Metals										
Aluminum	mg/kg	1,100,000	5,020	16,800	26,000	N/A	18,100	18,000	18,800	N/A
Antimony	mg/kg	470	2.7 U	2.4 UJ	2.4 UJ	N/A	3.1 UJ	2.3 U	2.9 U	N/A
Arsenic	mg/kg	3	5.5	3.4	6.1	5.7	4.9	10.9	7.7	8.3
Barium	mg/kg	220,000	45.6	95.1	286	N/A	185	212	31.8	N/A
Beryllium	mg/kg	2,300	0.36 J	0.64 B	1.9	N/A	1.7	0.76 J	0.79 J	N/A
Cadmium	mg/kg	980	1.4 U	1.2 U	0.4 J	N/A	2.3	1.7	1.4 U	N/A
Chromium	mg/kg	120,000	23.3	1,190	957	N/A	798	537	45.1	N/A
Chromium VI	mg/kg	6.3	0.64 B	3.1 J-	0.68 B	N/A	0.98 B	1.3	0.6 B	N/A
Cobalt	mg/kg	350	4 J	0.52 B	5.1	N/A	4.6 B	14.8	9.4	N/A
Copper	mg/kg	47,000	30.9	19 J	30.6 J	N/A	284 J	203	14.1	N/A
Iron	mg/kg	820,000	17,600	185,000	132,000	N/A	152,000	198,000	27,600	N/A
Lead	mg/kg	800	55.7	1.7 J	35.8	N/A	87.4	127	11.8	N/A
Manganese	mg/kg	26,000	130	29,600	31,100	551 J	17,900	17,000	466	N/A
Mercury	mg/kg	350	0.036 J	0.0085 B	0.024 B	N/A	0.08 B	0.086 B	0.01 B	N/A
Nickel	mg/kg	22,000	10.8	14.7 J	20.8 J	N/A	46.7 J	72.9	16.9	N/A
Selenium	mg/kg	5,800	3.6 U	3.1 U	3.1 U	N/A	4.1 U	3.1 U	3.8 U	N/A
Silver	mg/kg	5,800	1.9 J	21.7 J	29.3 J	N/A	19.3 J	13.3	5	N/A
Thallium	mg/kg	12	9.1 U	7.9 UJ	7.9 UJ	N/A	10.3 UJ	7.8 U	9.6 U	N/A
Vanadium	mg/kg	5,800	22.1	906	1,140	N/A	405	313	55.2	N/A
Zinc	mg/kg	350,000	90.7	55.4 J	70.7 J	N/A	462 J	542	47.6	N/A
Other										
Cyanide	mg/kg	150	1.1 U	0.15 J	1 J+	N/A	0.56 J	0.44 J	1.1 U	N/A

Detections in bold

Values in red indicate an exceedance of the Project Action Limit (PAL)

N/A indicates that the parameter was not analyzed for this sample

* indicates non-validated data

U: This analyte was not detected in the sample. The numeric value represents the sample quantitation/detection limit.

UJ: This analyte was not detected in the sample. The actual quantitation/detection limit may be higher than reported.

J: The positive result reported for this analyte is a quantitative estimate.

J+: The positive result reported for this analyte is a quantitative estimate but may be biased high.

J-: The positive result reported for this analyte is a quantitative estimate but may be biased low.

B: This analyte was not detected substantially above the level of the associated method blank/preparation or field blank.

R: The result for this analyte is unreliable. Additional data is needed to confirm or disprove the presence of this compound/analyte in the sample.

**Table 2 - Sub-Parcel B2-2
Summary of Inorganics Detected in Soil**

Parameter	Units	PAL	B2-030-SB-1*	B2-030-SB-5*	B2-031-SB-1*	B2-031-SB-7*	B2-032-SB-1*	B2-032-SB-4*	B2-033-SB-1*	B2-033-SB-5*	B2-034-SB-1*
Metals											
Aluminum	mg/kg	1,100,000	21,700 B	47,800	17,200	15,900	12,500	16,100	13,600	12,700	13,400
Antimony	mg/kg	470	2.7 U	2.7 U	2.3 U	2.7 U	2.5 U	2.5 U	2.7 U	2.5 U	2.7 U
Arsenic	mg/kg	3	7.2	2.3 U	8	13.5	2.4	4.2	2.3 U	2.1 U	7.5
Barium	mg/kg	220,000	207	409	691	373	72.3	57.3	76	107	67.4
Beryllium	mg/kg	2,300	1.7	8.3	2.1	1.4	0.84 U	0.76 J	0.9 U	0.88	0.71 J
Cadmium	mg/kg	980	1.3 J	1.4 U	0.7 J	2.8	0.48 J	1.2 U	0.62 J	0.42 J	1.4
Chromium	mg/kg	120,000	653	13.3	348	94.3	1,270	59.1	1,160	1,160	45.6
Chromium VI	mg/kg	6.3	0.65 B	0.52 B	0.62 B	0.57 B	0.74 B	0.53 B	0.76 B	0.72 B	0.72 B
Cobalt	mg/kg	350	9	0.62 J	10.8	8.1	1.8 J	44.1	1.6 J	1.4 J	7.7
Copper	mg/kg	47,000	88.6	6.3	88.5	97.5	36.9	59.2	42	25.3	42.3
Iron	mg/kg	820,000	162,000	6,240	263,000	31,200	212,000	31,600	209,000	189,000	37,700
Lead	mg/kg	800	302	2.3 U	82.5	443	9.8	27.1	6.3	5.6	166
Manganese	mg/kg	26,000	16,400	2,730	9,320	4,390	27,800	862	31,200	29,600	620
Mercury	mg/kg	350	0.24	0.0068 B	0.036 B	0.45	0.11 U	0.078 J	0.0077 B	0.018 B	0.12
Nickel	mg/kg	22,000	51.9	3.3 J	56.3	32.9	16	30.6	19.8	12.1	19.1
Selenium	mg/kg	5,800	3.6 U	3.6 U	3.1 U	3.6 U	3.4 U	3.3 U	3.6 U	3.3 U	3.6 U
Silver	mg/kg	5,800	19.4	10.1	16.2	9	22.9	2.8	28.6	29.6	2.9
Thallium	mg/kg	12	9 U	9 U	7.7 U	8.9 U	8.4 U	8.3 U	9 U	8.3 U	9.1 U
Vanadium	mg/kg	5,800	527	15.2	492	141	608	75	712	689	55.3
Zinc	mg/kg	350,000	585	7.2	840	659	262	56	221	69.4	593
Other											
Cyanide	mg/kg	150	1 J	0.32 J	0.42 J	1.9	0.24 B	0.14 B	0.36 J	0.52 J	0.13 B

Detections in bold

Values in red indicate an exceedance of the Project Action Limit (PAL)

N/A indicates that the parameter was not analyzed for this sample

* indicates non-validated data

U: This analyte was not detected in the sample. The numeric value represents the sample quantitation/detection limit.

UJ: This analyte was not detected in the sample. The actual quantitation/detection limit may be higher than reported.

J: The positive result reported for this analyte is a quantitative estimate.

J+: The positive result reported for this analyte is a quantitative estimate but may be biased high.

J-: The positive result reported for this analyte is a quantitative estimate but may be biased low.

B: This analyte was not detected substantially above the level of the associated method blank/preparation or field blank.

R: The result for this analyte is unreliable. Additional data is needed to confirm or disprove the presence of this compound/analyte in the sample.

**Table 2 - Sub-Parcel B2-2
Summary of Inorganics Detected in Soil**

Parameter	Units	PAL	B2-035-SB-1*	B2-035-SB-4*	B2-038-SB-1	B2-038-SB-5	B2-039-SB-1*	B2-039-SB-5*	B2-040-SB-1	B2-040-SB-7
Metals										
Aluminum	mg/kg	1,100,000	21,300	18,600	12,500	16,000	12,200	26,000	14,400	20,500
Antimony	mg/kg	470	3 U	2.9 U	2.5 UJ	2.5 UJ	3 U	2.5 U	2.8 UJ	3.9 UJ
Arsenic	mg/kg	3	4	4.5	3.3	14.4	2.5 U	2.1 U	4.6 J	18.3 J
Barium	mg/kg	220,000	67.1	103	56.2	216	55.5	53.5	52.7	133
Beryllium	mg/kg	2,300	0.55 J	0.92 J	0.38 B	2.3	0.24 J	0.85 U	0.73 B	0.8 B
Cadmium	mg/kg	980	1.5 U	1.4 U	0.83 J	1.9	0.59 J	0.49 J	1.4 U	1.9 U
Chromium	mg/kg	120,000	25.3	46.2	743	261	1,550	2,480	25.3	72.7
Chromium VI	mg/kg	6.3	0.85 B	0.97 B	5.3 J-	0.68 B	1.3	16.9	0.55 B	0.96 B
Cobalt	mg/kg	350	3.8 J	8.2	2.9 B	11.5	1.6 J	4.2 U	4 J	8.1
Copper	mg/kg	47,000	12.3	28.7	67.2 J	162 J	37.8	14.6	10	71.4
Iron	mg/kg	820,000	22,200	29,800	191,000	150,000	226,000	179,000	20,800	39,200
Lead	mg/kg	800	17.7	60.1	31.5	198	6.4	2.1 U	14.1	248
Manganese	mg/kg	26,000	49.3	980	20,100	6,090	30,400	44,900	130	257
Mercury	mg/kg	350	0.028 J	0.025 J	0.041 B	0.19 J-	0.017 B	0.0044 B	0.11 U	0.52
Nickel	mg/kg	22,000	12.2	20.8	26.9 J	104 J	15.4	10.9	11.1 J	23.4 J
Selenium	mg/kg	5,800	4 U	3.8 U	3.3 U	3.3 U	3.9 U	3.4 U	3.8 U	5.2 U
Silver	mg/kg	5,800	2.5 J	3	17.5 J	10.9 J	25.9	26.8	2.1 J	2.8 J
Thallium	mg/kg	12	10 U	9.5 U	8.2 UJ	8.3 UJ	9.9 U	8.5 U	9.4 UJ	5.2 UJ
Vanadium	mg/kg	5,800	34.3	71.3	472	336	870	946	43.1	69
Zinc	mg/kg	350,000	49.3	163	195 J	572 J	62.5	16.4	61.9	237
Other										
Cyanide	mg/kg	150	1 U	2.1	0.59 J+	0.61 J+	0.39 J	0.29 J	0.21 J	0.24 J

Detections in bold

Values in red indicate an exceedance of the Project Action Limit (PAL)

N/A indicates that the parameter was not analyzed for this sample

* indicates non-validated data

U: This analyte was not detected in the sample. The numeric value represents the sample quantitation/detection limit.

UJ: This analyte was not detected in the sample. The actual quantitation/detection limit may be higher than reported.

J: The positive result reported for this analyte is a quantitative estimate.

J+: The positive result reported for this analyte is a quantitative estimate but may be biased high.

J-: The positive result reported for this analyte is a quantitative estimate but may be biased low.

B: This analyte was not detected substantially above the level of the associated method blank/preparation or field blank.

R: The result for this analyte is unreliable. Additional data is needed to confirm or disprove the presence of this compound/analyte in the sample.

**Table 2 - Sub-Parcel B2-2
Summary of Inorganics Detected in Soil**

Parameter	Units	PAL	B2-040-SB-10*	B2-044-SB-1*	B2-044-SB-7*	B2-045-SB-1*	B2-045-SB-5*	B2-045-SB-10	B2-048-SB-1	B2-048-SB-8
Metals										
Aluminum	mg/kg	1,100,000	N/A	24,700	7,810	19,700	15,900	N/A	18,000	17,500
Antimony	mg/kg	470	N/A	3 U	2.8 U	3 J	3 U	N/A	3.2 UJ	3.5 UJ
Arsenic	mg/kg	3	8.8	5.9	3.2	18.4	3.2	5.1	3.3	11.3
Barium	mg/kg	220,000	N/A	331	60	308	52.8	N/A	74	67.8
Beryllium	mg/kg	2,300	N/A	3.1	0.93 U	1.5	0.39 J	N/A	0.89 B	0.83 B
Cadmium	mg/kg	980	N/A	2.3	1.4 U	2.4	1.5 U	N/A	1.6 U	1.7 U
Chromium	mg/kg	120,000	N/A	313	1,160	31.6	25.5	N/A	1,380	36.9
Chromium VI	mg/kg	6.3	N/A	0.64 B	1.2	0.67 B	0.62 B	N/A	1.8 J-	0.71 B
Cobalt	mg/kg	350	N/A	4.3 J	5.6	8.2	4.8 J	N/A	0.7 B	4.4 B
Copper	mg/kg	47,000	N/A	116	45.6	95.6	12	N/A	21.1 J	16.8 J
Iron	mg/kg	820,000	N/A	60,700	162,000	67,900	18,100	N/A	207,000	29,000
Lead	mg/kg	800	N/A	153	23.8	361	20.4	N/A	1.5 J	14
Manganese	mg/kg	26,000	N/A	12,900	29,500	5,590	162	N/A	32,900	519
Mercury	mg/kg	350	N/A	0.19	0.14 U	0.045 J	0.039 J	N/A	0.012 B	0.021 B
Nickel	mg/kg	22,000	N/A	16.4	18.8	13.1	13.6	N/A	18 J	12 J
Selenium	mg/kg	5,800	N/A	4 U	3.7 U	4.1 U	4 U	N/A	4.3 U	4.6 U
Silver	mg/kg	5,800	N/A	41.1	77.2	9.3	3.6	N/A	25.3 J	2 J
Thallium	mg/kg	12	N/A	9.9 U	9.3 U	10.3 U	10 U	N/A	10.8 UJ	11.5 UJ
Vanadium	mg/kg	5,800	N/A	1,100	2,800	57.7	29.9	N/A	905	42.5
Zinc	mg/kg	350,000	N/A	3,490	129	417	46	N/A	31.7 J	41.3 J
Other										
Cyanide	mg/kg	150	N/A	1.3	0.61 B	0.44 J	1.3 U	N/A	0.55 J+	0.42 J+

Detections in bold

Values in red indicate an exceedance of the Project Action Limit (PAL)

N/A indicates that the parameter was not analyzed for this sample

* indicates non-validated data

U: This analyte was not detected in the sample. The numeric value represents the sample quantitation/detection limit.

UJ: This analyte was not detected in the sample. The actual quantitation/detection limit may be higher than reported.

J: The positive result reported for this analyte is a quantitative estimate.

J+: The positive result reported for this analyte is a quantitative estimate but may be biased high.

J-: The positive result reported for this analyte is a quantitative estimate but may be biased low.

B: This analyte was not detected substantially above the level of the associated method blank/preparation or field blank.

R: The result for this analyte is unreliable. Additional data is needed to confirm or disprove the presence of this compound/analyte in the sample.

**Table 2 - Sub-Parcel B2-2
Summary of Inorganics Detected in Soil**

Parameter	Units	PAL	B2-051-SB-1	B2-051-SB-5	B2-052-SB-1	B2-052-SB-5	B2-052-SB-10	B5-011-SB-1	B5-011-SB-5	B5-012-SB-1
Metals										
Aluminum	mg/kg	1,100,000	18,300	14,900	21,300	16,900	N/A	34,400	21,100	14,200
Antimony	mg/kg	470	2.5 UJ	2.6 UJ	2.3 UJ	2.4 UJ	N/A	3.1 UJ	2.5 UJ	2.7 UJ
Arsenic	mg/kg	3	2.5	16.3	8.2	6	3.7	4.8	4	5.3
Barium	mg/kg	220,000	127	90.2	672	70.9	N/A	478 J	289 J	313 J
Beryllium	mg/kg	2,300	1.8	0.18 J	2.6	0.57 J	N/A	3.2	2.2	0.58 B
Cadmium	mg/kg	980	1.3 U	0.55 J	1.6	0.45 J	N/A	1.1 B	0.61 B	1.2 B
Chromium	mg/kg	120,000	1,210 J	1,440 J	220	38.6	N/A	343 J	62.9 J	740 J
Chromium VI	mg/kg	6.3	1.7 J-	2.6 J-	0.6 B	0.63 B	N/A	0.43 J	0.18 J	0.48 J
Cobalt	mg/kg	350	0.55 J	1.9 J	9.8	6.6	N/A	7.2	3.7 B	21.8
Copper	mg/kg	47,000	13.2 J	30.8 J	1,220 J	9.6 J	N/A	54.1	11.7	143
Iron	mg/kg	820,000	151,000 J	184,000 J	116,000	25,600	N/A	49,700	38,000	79,300
Lead	mg/kg	800	2.1 UJ	36.9 J	198	10.3	N/A	81.9	25.8	110
Manganese	mg/kg	26,000	27,700	37,400	14,400	588	N/A	12,800	5,880	34,500
Mercury	mg/kg	350	0.097 U	0.089 U	0.25 J-	0.081 B	N/A	0.1 UJ	0.11 UJ	0.035 J-
Nickel	mg/kg	22,000	12.3 J	25.7 J	53.2 J	13.1 J	N/A	26	7.7 B	121
Selenium	mg/kg	5,800	3.3 U	3.5 U	3.1 U	3.2 U	N/A	3 B	3 B	3.6 U
Silver	mg/kg	5,800	25.3	29.3	13.7 J	3.7 J	N/A	3.1 U	2.5 U	2.7 U
Thallium	mg/kg	12	8.4 U	8.7 U	7.7 UJ	8 UJ	N/A	5.4 B	8.2 UJ	12.9 J
Vanadium	mg/kg	5,800	778	837	152	50.5	N/A	1,540 J	137 J	4,710 J
Zinc	mg/kg	350,000	37.5 J	95 J	653 J	125 J	N/A	389	68.7	373
Other										
Cyanide	mg/kg	150	0.22 J-	0.33 J-	0.58 J	0.84 J	N/A	2.3 J-	0.27 J	3.8 J-

Detections in bold

Values in red indicate an exceedance of the Project Action Limit (PAL)

N/A indicates that the parameter was not analyzed for this sample

* indicates non-validated data

U: This analyte was not detected in the sample. The numeric value represents the sample quantitation/detection limit.

UJ: This analyte was not detected in the sample. The actual quantitation/detection limit may be higher than reported.

J: The positive result reported for this analyte is a quantitative estimate.

J+: The positive result reported for this analyte is a quantitative estimate but may be biased high.

J-: The positive result reported for this analyte is a quantitative estimate but may be biased low.

B: This analyte was not detected substantially above the level of the associated method blank/preparation or field blank.

R: The result for this analyte is unreliable. Additional data is needed to confirm or disprove the presence of this compound/analyte in the sample.

**Table 2 - Sub-Parcel B2-2
Summary of Inorganics Detected in Soil**

Parameter	Units	PAL	B5-012-SB-5	B5-013-SB-1	B5-013-SB-4.5	B5-014-SB-1	B5-014-SB-4	B5-033-SB-1*	B5-033-SB-8*	B5-033-SB-10*
Metals										
Aluminum	mg/kg	1,100,000	14,000	35,800	27,600	17,700	17,000	6,880	20,200	N/A
Antimony	mg/kg	470	2.8 UJ	2.6 UJ	2.7 UJ	2.8 UJ	3.3 UJ	3 U	3.2 U	N/A
Arsenic	mg/kg	3	6.9	3.4	2.2 U	7.8	2.8 U	2.5 U	4	3.4
Barium	mg/kg	220,000	103 J	733 J	205 J	86.4 J	152 J	37.7	89.2	N/A
Beryllium	mg/kg	2,300	0.95 U	4	1.3	0.89 B	0.84 B	0.38 J	0.51 J	N/A
Cadmium	mg/kg	980	0.46 B	0.58 B	0.41 B	0.83 B	0.49 B	0.42 B	1.6 U	N/A
Chromium	mg/kg	120,000	481 J	37.7 J	5,180 J	280 J	3,980 J	122	25.3	N/A
Chromium VI	mg/kg	6.3	1.1 J	0.39 J	0.6 J	0.81 J	0.44 J	1.1 U	1.1 U	N/A
Cobalt	mg/kg	350	6.1	8.7	23.4	5.3	98.8	2.1 J	4.2 J	N/A
Copper	mg/kg	47,000	25.5	24.3	68.8	63.3	270	36.8	9.2	N/A
Iron	mg/kg	820,000	34,900	34,000	38,100	40,500	144,000	49,300	15,700	N/A
Lead	mg/kg	800	40.3	15.3	27.2	56.1	59.1	59.9	9.3	N/A
Manganese	mg/kg	26,000	12,600	8,040	15,200	6,070	12,900	1,750	69.7	N/A
Mercury	mg/kg	350	0.042 J-	0.029 J-	0.0097 J-	0.093 J-	0.047 J-	0.13	0.0036 J	N/A
Nickel	mg/kg	22,000	25.6	13.1	171	17.3	738	29.4	12	N/A
Selenium	mg/kg	5,800	3.8 U	4.5	3.5 U	3.7 U	3.9 B	4 U	4.3 U	N/A
Silver	mg/kg	5,800	2.8 U	2.6 U	2.7 U	2.8 U	1.7 B	3 U	3.2 U	N/A
Thallium	mg/kg	12	14.4 J	8.7 UJ	8.9 UJ	9.3 UJ	11.2 UJ	10 U	10.7 U	N/A
Vanadium	mg/kg	5,800	3,540 J	335 J	241 J	607 J	197 J	59.5	28	N/A
Zinc	mg/kg	350,000	78.8	87.7	264	232	239	314	33.2	N/A
Other										
Cyanide	mg/kg	150	0.13 J-	5.7 J+	1.4 J+	14.2 J-	29.3 J+	13.6	0.51 J	N/A

Detections in bold

Values in red indicate an exceedance of the Project Action Limit (PAL)

N/A indicates that the parameter was not analyzed for this sample

* indicates non-validated data

U: This analyte was not detected in the sample. The numeric value represents the sample quantitation/detection limit.

UJ: This analyte was not detected in the sample. The actual quantitation/detection limit may be higher than reported.

J: The positive result reported for this analyte is a quantitative estimate.

J+: The positive result reported for this analyte is a quantitative estimate but may be biased high.

J-: The positive result reported for this analyte is a quantitative estimate but may be biased low.

B: This analyte was not detected substantially above the level of the associated method blank/preparation or field blank.

R: The result for this analyte is unreliable. Additional data is needed to confirm or disprove the presence of this compound/analyte in the sample.

**Table 2 - Sub-Parcel B2-2
Summary of Inorganics Detected in Soil**

Parameter	Units	PAL	B5-034-SB-1*	B5-039-SB-1	B5-039-SB-5	B5-040-SB-1	B5-040-SB-5	B5-081-SB-1*	B5-081-SB-5*	B5-082-SB-1*
Metals										
Aluminum	mg/kg	1,100,000	5,990	4,510	11,700	7,200	14,500	45,100	22,800	42,300
Antimony	mg/kg	470	3.2 U	2.7 UJ	3 UJ	2.5 UJ	2.6 UJ	2.5 U	3.6 U	2.2 U
Arsenic	mg/kg	3	2.6 U	3.9	4.7	2.1 U	4.7	1.9 J	6.3	1.9 U
Barium	mg/kg	220,000	40.9	50.6 J	36.7	72 J	58.1 J	401	54	428
Beryllium	mg/kg	2,300	0.45 J	0.9 U	0.51 B	0.34 J	1.1	8	0.74 J	7.6
Cadmium	mg/kg	980	0.43 B	0.67 B	0.4 B	0.63 B	0.21 B	0.4 B	1.8 U	0.36 B
Chromium	mg/kg	120,000	104	2,200 J	514 J	1,040 J	55.1 J	8.4	31.4	9.3
Chromium VI	mg/kg	6.3	1.1 U	0.18 J-	1.1 UJ	0.18 J-	0.21 J-	0.52 J	0.5 J	0.59 J
Cobalt	mg/kg	350	3.6 J	3.3 B	12.7	1.1 B	16.2	1.2 J	5.7 J	0.84 J
Copper	mg/kg	47,000	181	68	113	31	29.6	2.2 J	12.6	5.3
Iron	mg/kg	820,000	115,000	267,000	40,900	158,000	21,500	10,100	26,700	8,920
Lead	mg/kg	800	60.7	13.8	25.6	12.3	15.6	2.5	11.1	18.5
Manganese	mg/kg	26,000	1,680	24,900	2,030	27,700	328	2,910	93.1	2,750
Mercury	mg/kg	350	0.067 J	0.017 J-	0.022 J	0.0031 J-	0.029 J-	0.11 U	0.12 J	0.11 U
Nickel	mg/kg	22,000	38.5	28.2	77.1	13.7	64.3	2.7 J	14.6	2.6 J
Selenium	mg/kg	5,800	4.2 U	3.6 U	4 U	3.3 U	3.5 U	4.2	4.8 U	3.1
Silver	mg/kg	5,800	1 J	3.7	3 U	1.7 B	2.6 U	2.5 U	3.6 U	2.2 U
Thallium	mg/kg	12	10.5 U	9 UJ	9.9 UJ	8.4 UJ	8.8 UJ	8.4 U	11.9 U	7.4 U
Vanadium	mg/kg	5,800	47.8	768 J	42.8 J	958 J	27 J	47	39	32
Zinc	mg/kg	350,000	650	246	118 J	169	89.8	7.4	44.9	28.4
Other										
Cyanide	mg/kg	150	2.4	0.068 J+	2.3 J+	0.17 J+	3 J+	0.67 U	0.6 U	0.071 J

Detections in bold

Values in red indicate an exceedance of the Project Action Limit (PAL)

N/A indicates that the parameter was not analyzed for this sample

* indicates non-validated data

U: This analyte was not detected in the sample. The numeric value represents the sample quantitation/detection limit.

UJ: This analyte was not detected in the sample. The actual quantitation/detection limit may be higher than reported.

J: The positive result reported for this analyte is a quantitative estimate.

J+: The positive result reported for this analyte is a quantitative estimate but may be biased high.

J-: The positive result reported for this analyte is a quantitative estimate but may be biased low.

B: This analyte was not detected substantially above the level of the associated method blank/preparation or field blank.

R: The result for this analyte is unreliable. Additional data is needed to confirm or disprove the presence of this compound/analyte in the sample.

**Table 2 - Sub-Parcel B2-2
Summary of Inorganics Detected in Soil**

Parameter	Units	PAL	B5-082-SB-5*	B5-083-SB-1*	B5-083-SB-5*	B5-084-SB-1*	B5-085-SB-1	B5-090-SB-1	B5-090-SB-4.75	B5-091-SB-1*
Metals										
Aluminum	mg/kg	1,100,000	19,000	13,200	20,300	35,500	18,800	25,200	16,300	14,300
Antimony	mg/kg	470	3.4 U	3.1 U	3 U	2.3 U	2.4 UJ	3.1 UJ	3.1 UJ	2.5 U
Arsenic	mg/kg	3	3.8	6.4	6.3	2.2	12.8	6.4	3.1	4
Barium	mg/kg	220,000	63.4	93	27.1	364	204 J	223 J	51.4 J	142
Beryllium	mg/kg	2,300	0.74 J	0.78 J	1.2	5.6	2.8	3	0.3 J	1.5
Cadmium	mg/kg	980	1.7 U	1.6	1.5 U	0.28 J	0.52 B	0.61 B	1.6 U	0.96 J
Chromium	mg/kg	120,000	25.2	86.6	21.9	44.2	161	87.1 J	24.2 J	41.5
Chromium VI	mg/kg	6.3	1 J	0.51 J	1.3	1.1 U	0.27 J	0.4 B	0.42 B	1.1 U
Cobalt	mg/kg	350	4.3 J	8.8	4.6 J	1.6 J	11.1	6.5	3.6 B	3.2 J
Copper	mg/kg	47,000	9.7	34.8	9.1	7.2	137	33	7.8	29
Iron	mg/kg	820,000	16,400	61,900	19,800	88,900	344,000	40,500 J	18,400 J	54,100
Lead	mg/kg	800	8.7	114	8.5	9.6	153 J	157 J	10.2 J	151
Manganese	mg/kg	26,000	73.5	2,070	46.6	3,250	4,620	4,400	152	1,170
Mercury	mg/kg	350	0.11 U	0.024 J	0.0053 J	0.0026 J	0.03 J	0.11 R	0.052 J-	0.063 J
Nickel	mg/kg	22,000	12.2	22.3	11.9	9.5	69.7	16.7	7.7 J	17.1
Selenium	mg/kg	5,800	4.5 U	4.2 U	4.1 U	2.7 J	3.2 U	4.2 U	4.2 U	3.4 U
Silver	mg/kg	5,800	3.4 U	3.1 U	3 U	2.3 U	4.1	3.1 U	3.1 U	2.5 U
Thallium	mg/kg	12	11.2 U	10.4 U	10.2 U	7.6 U	7.9 U	10.4 U	10.4 U	8.4 U
Vanadium	mg/kg	5,800	31.4	87.6	34.4	30.9	101	56.8 J	29.7 J	22.9
Zinc	mg/kg	350,000	32.7	477	31	38.6	339 J	211 J	31.6 J	293
Other										
Cyanide	mg/kg	150	0.58 U	0.21 J	0.72 U	6	3.3 J+	2.2 J-	0.69 UJ	3.5

Detections in bold

Values in red indicate an exceedance of the Project Action Limit (PAL)

N/A indicates that the parameter was not analyzed for this sample

* indicates non-validated data

U: This analyte was not detected in the sample. The numeric value represents the sample quantitation/detection limit.

UJ: This analyte was not detected in the sample. The actual quantitation/detection limit may be higher than reported.

J: The positive result reported for this analyte is a quantitative estimate.

J+: The positive result reported for this analyte is a quantitative estimate but may be biased high.

J-: The positive result reported for this analyte is a quantitative estimate but may be biased low.

B: This analyte was not detected substantially above the level of the associated method blank/preparation or field blank.

R: The result for this analyte is unreliable. Additional data is needed to confirm or disprove the presence of this compound/analyte in the sample.

**Table 2 - Sub-Parcel B2-2
Summary of Inorganics Detected in Soil**

Parameter	Units	PAL	B5-091-SB-7*	B5-134-SB-1	B5-135-SB-1	B5-135-SB-5	B5-176-SB-1	B5-176-SB-5
Metals								
Aluminum	mg/kg	1,100,000	16,000	18,100	27,500	15,600	29,900	27,400
Antimony	mg/kg	470	2.5 U	3.6 UJ	2.5 UJ	2.7 UJ	2.8 UJ	3.4 UJ
Arsenic	mg/kg	3	4.3	4.8	3.1	3.8	6.9	10
Barium	mg/kg	220,000	66.6	229 J	294 J	32.5 J	226 J	241 J
Beryllium	mg/kg	2,300	0.54 J	2.3	3.2	0.69 B	3	2.4
Cadmium	mg/kg	980	1.2 U	2.1	0.43 B	1.3 U	1 B	1.3 B
Chromium	mg/kg	120,000	36.5	298 J	526 J	16.9 J	125 J	52.5 J
Chromium VI	mg/kg	6.3	1.1 U	1.4 UJ	1.1 UJ	0.6 J-	1.1 UJ	0.19 J-
Cobalt	mg/kg	350	4.3	8	3.4 B	2.7 B	10.6	20.5
Copper	mg/kg	47,000	17.3	85.7	22.6	8.7	265	311
Iron	mg/kg	820,000	15,800	142,000	88,700	9,540	89,400	133,000
Lead	mg/kg	800	26.1	112	13.7	10.1	91.4	80.8
Manganese	mg/kg	26,000	690	8,690	11,400	39	16,100	37,500
Mercury	mg/kg	350	0.015 J	0.06 J-	0.11 UJ	0.0041 J-	0.01 J-	0.018 J-
Nickel	mg/kg	22,000	8 J	69.8	11.9	8.9	12.5	16.5
Selenium	mg/kg	5,800	3.3 U	4.8 U	5.3	3.5 U	3.8 U	4.5 U
Silver	mg/kg	5,800	2.5 U	2.6 B	2.5 U	2.7 U	2.7 B	6.9
Thallium	mg/kg	12	8.3 U	9.7 UJ	8.3 UJ	8.9 UJ	9.4 UJ	11.3 UJ
Vanadium	mg/kg	5,800	55.7	167 J	681 J	26.6 J	90.4 J	120 J
Zinc	mg/kg	350,000	57.4	1,010	52.3	18.5	462	596
Other								
Cyanide	mg/kg	150	4.8 U	1 J+	0.55 U	0.57 U	1.2 J+	4.4 J+

Detections in bold

Values in red indicate an exceedance of the Project Action Limit (PAL)

N/A indicates that the parameter was not analyzed for this sample

* indicates non-validated data

U: This analyte was not detected in the sample. The numeric value represents the sample quantitation/detection limit.

UJ: This analyte was not detected in the sample. The actual quantitation/detection limit may be higher than reported.

J: The positive result reported for this analyte is a quantitative estimate.

J+: The positive result reported for this analyte is a quantitative estimate but may be biased high.

J-: The positive result reported for this analyte is a quantitative estimate but may be biased low.

B: This analyte was not detected substantially above the level of the associated method blank/preparation or field blank.

R: The result for this analyte is unreliable. Additional data is needed to confirm or disprove the presence of this compound/analyte in the sample.

**Table 3 - Sub-Parcel B2-2
Summary of Organics Detected in Groundwater**

Parameter	Units	PAL	B2-051-PZ*	FM01-PZM003	SW-056-MWS	SW-057-MWS	SW-058-MWS	SW-070-MWS	SW-071-MWS	SW-072-MWS	SW09-PZM004	SW15-PZM005
Volatile Organic Compounds												
1,1-Dichloroethane	µg/L	2.7	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U
4-Methyl-2-pentanone (MIBK)	µg/L	1,200	10 U	10 U	10 U	10 U	10 U	10 U	4.4 J	10 U	10 U	10 U
Acetone	µg/L	14,000	10 U	10 R	10 U	10 U	10 U	10 R	7.2 J	10 UJ	10 R	10 U
Benzene	µg/L	5	1 U	1 U	1 U	14	1 U	1 U	1 U	1 U	1 U	1 U
Carbon disulfide	µg/L	810	1 U	1 U	1 U	0.79 J	1 U	1 U	1 U	1 U	1 U	1 U
Chloroform	µg/L	0.22	1 U	27.9	1 U	1 U	31	1 U	1 U	1 U	1 U	1 U
Ethylbenzene	µg/L	700	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U
Isopropylbenzene	µg/L	450	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U
Methyl tert-butyl ether (MTBE)	µg/L	14	1 U	1 U	14.3	1 U	1 U	1 U	1 U	1 U	1 U	1 U
Toluene	µg/L	1,000	0.84 J	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U
Trichloroethene	µg/L	5	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U
Xylenes	µg/L	10,000	3 U	3 U	3 U	3 U	3 U	3 U	3 U	3 U	3 U	3 U
Semi-Volatile Organic Compounds^												
1,1-Biphenyl	µg/L	0.83	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U
1,4-Dioxane	µg/L	0.46	0.025 J	0.1 U	0.2	0.16	0.1 U	0.052 J	0.1 U	0.071 J	0.1 U	0.1 U
2,4-Dimethylphenol	µg/L	360	0.52 J	1 U	1 U	1 U	1 U	1 U	1.4	1 U	1 U	1 U
2-Methylnaphthalene	µg/L	36	0.55	0.1 U	0.1 U	0.14	0.1 U	0.1 U	0.24	0.1 U	0.1 U	0.1 U
2-Methylphenol	µg/L	930	0.31 J	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U
3&4-Methylphenol(m&p Cresol)	µg/L	930	0.85 J	2.1 U	2 U	2 U	2 U	2 U	0.65 J	2 U	2 U	2 U
Acenaphthene	µg/L	530	0.49	0.1 U	0.1 U	0.11	0.1 U	0.1 U	0.29	0.1 U	0.1 U	0.1 U
Acenaphthylene	µg/L	530	0.42	0.1 U	0.1 U	0.028 J	0.1 U	0.1 U	0.038 J	0.1 U	0.1 U	0.1 U
Acetophenone	µg/L	1,900	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U
Anthracene	µg/L	1,800	0.27	0.014 J	0.1 U	0.042 J	0.1 U	0.1 U	0.2	0.1 U	0.1 U	0.1 U
Benz[a]anthracene	µg/L	0.03	0.056 J	0.022 J	0.1 U	0.1 U	0.037 J	0.1 U	0.1 U	0.1 U	0.1 U	0.1 U
Benzo[a]pyrene	µg/L	0.2	0.1 U	0.014 J	0.1 U	0.1 U	0.021 J	0.1 U	0.1 U	0.1 U	0.1 U	0.1 U
Benzo[b]fluoranthene	µg/L	0.25	0.1 U	0.1 U	0.1 U	0.1 U	0.095 Jip	0.1 U	0.1 U	0.1 U	0.1 U	0.1 U
Benzo[g,h,i]perylene	µg/L		0.1 U	0.1 U	0.1 U	0.1 U	0.025 J	0.1 U	0.1 U	0.1 U	0.1 U	0.1 U
Benzo[k]fluoranthene	µg/L	2.5	0.1 U	0.1 U	0.1 U	0.1 U	0.075 Jip	0.1 U	0.1 U	0.1 U	0.1 U	0.1 U
bis(2-Ethylhexyl)phthalate	µg/L	6	1 U	1 U	0.48 J	0.25 B	1 U	1 U	0.32 B	1 U	1 U	1 U
Carbazole	µg/L		1.6	1 U	1 U	1 U	1 U	1 U	0.43 J	1 U	1 U	1 U
Chrysene	µg/L	25	0.1 U	0.012 J	0.1 U	0.1 U	0.046 J	0.1 U	0.1 U	0.1 U	0.1 U	0.1 U
Fluoranthene	µg/L	800	0.45	0.059 J	0.1 U	0.049 J	0.039 J	0.1 U	0.015 J	0.011 J	0.1 U	0.1 U
Fluorene	µg/L	290	0.99	0.1 U	0.1 U	0.12	0.1 U	0.1 U	0.11	0.1 U	0.1 U	0.1 U
Indeno[1,2,3-c,d]pyrene	µg/L	0.25	0.1 U	0.1 U	0.1 U	0.1 U	0.1 U	0.1 U	0.1 U	0.1 U	0.1 U	0.1 U
Naphthalene	µg/L	0.17	4.1 B	0.052 B	0.019 B	0.47	0.022 B	0.1 U	0.16	0.033 B	0.047 B	0.023 B
Pentachlorophenol	µg/L	1	2.6 U	2.6 U	2.5 U	1 J	2.5 U	2.5 U	2.5 U	2.5 U	2.5 U	2.5 U
Phenanthrene	µg/L		1.8	0.056 J	0.1 U	0.12	0.1 U	0.1 U	0.073 J	0.1 U	0.1 U	0.1 U
Phenol	µg/L	5,800	1 U	1 U	1 U	0.42 J	1 U	1 U	5.3 J	1 U	1 U	1 U
Pyrene	µg/L	120	0.28	0.05 J	0.1 U	0.038 J	0.042 J	0.1 U	0.029 J	0.1 U	0.1 U	0.1 U
PCBs												
PCBs (total)	µg/L	0.5	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A
Trichlorobiphenyl	µg/L	0.044	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A
TPH/Oil and Grease												
Diesel Range Organics	µg/L	47	198	47.9 B	735 J	1,170 J	105 UJ	48.8 J	3,120 J	308 J	41.8 B	101 UJ
Oil and Grease	µg/L	47	4,770 U	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A

Detections in bold

Values in red indicate an exceedance of the Project Action Limit (PAL)

N/A indicates that the parameter was not analyzed for this sample

* indicates non-validated data

^ PAH compounds were analyzed via SIM

U: This analyte was not detected in the sample. The numeric value represents the sample quantitation/detection limit.

UJ: This analyte was not detected in the sample. The actual quantitation/detection limit may be higher than reported.

J: The positive result reported for this analyte is a quantitative estimate.

B: This analyte was not detected substantially above the level of the associated method blank/preparation or field blank.

R: The result for this analyte is unreliable. Additional data is needed to confirm or disprove the presence of this compound/analyte in the sample.

**Table 4 - Sub-Parcel B2-2
Summary of Inorganics Detected in Groundwater**

Parameter	Units	PAL	B2-051-PZ*	FM01-PZM003	SW-056-MWS	SW-057-MWS	SW-058-MWS	SW-070-MWS	SW-071-MWS	SW-072-MWS	SW09-PZM004	SW15-PZM005
Total Metals												
Aluminum	µg/L	20,000	N/A	118	420	537	295	64.5	73.5	7,650	1,490	165
Antimony	µg/L	6	N/A	6 U	6 U	6 U	6 U	6 U	6 U	6 U	6 U	6 U
Arsenic	µg/L	10	N/A	5 U	5 U	3.7 J	5 U	5 U	5 U	5 U	5 U	5 U
Barium	µg/L	2,000	N/A	25.8	19.4	60.7	27.4	78.4	49.2	16.9	72.8	30.2
Beryllium	µg/L	4	N/A	1 U	1 U	1 U	1 U	1 U	1 U	7	0.41 B	1 U
Cadmium	µg/L	5	N/A	3 U	0.77 J	3 U	3 U	3 U	3 U	1.1 J	1.5 J	3 U
Chromium	µg/L	100	N/A	1.6 B	2.2 J	2.6 B	8.6	2.3 B	1.1 B	1.4 J	2.2 B	0.89 B
Chromium VI	µg/L	0.035	N/A	10 U	10 U	10 U	10 U	10 U	10 U	10 U	10 U	N/A
Cobalt	µg/L	6	N/A	5 U	112	3.7 J	5 U	5 U	5 U	124	43.1	4 J
Copper	µg/L	1,300	N/A	1.7 B	1.7 B	5 U	5 U	5 U	5 U	4.8 J	8.8	2.1 B
Iron	µg/L	14,000	N/A	50 B	70,400	15,600	451	535	103	38,600	1,230	899
Lead	µg/L	15	N/A	5 U	5 U	5 U	4.2 B	5 U	5 U	5 U	5 U	5 U
Manganese	µg/L	430	N/A	7.6	11,100	2,190	17.2	350	193	5,550	986	256
Nickel	µg/L	390	N/A	0.71 J	38.1	5.7 B	10 U	0.98 B	0.73 J	166	40.7	4.2 B
Selenium	µg/L	50	N/A	8 U	8 U	8 U	8 U	8 U	11.2	8 U	8 U	8 U
Thallium	µg/L	2	N/A	10 U	10 U	10 U	10 U	10 U	5.6 B	10 U	10 U	10 U
Vanadium	µg/L	86	N/A	224	5 U	53.3	21.4	0.77 J	3.3 B	5 U	4.6 B	5 U
Zinc	µg/L	6,000	N/A	10 U	28.4	18.9	8.2 J	2.1 B	10 U	411	66.1	7.5 B
Dissolved Metals												
Aluminum, Dissolved	µg/L	20,000	1,130	102	33.4 B	38.1 J	51.4	21.1 J	45 J	7,800	89	144
Antimony, Dissolved	µg/L	6	6 U	2.6 B	6 U	6 U	6 U	6 U	6 U	6 U	6 U	6 U
Arsenic, Dissolved	µg/L	10	5.1	5 U	5 U	6.4	5 U	5 U	4.7 B	5 U	5 U	5 U
Barium, Dissolved	µg/L	2,000	100	25.7	18.8	50.6	22.4	77.7	43.7	16.5	73.8	30.7
Beryllium, Dissolved	µg/L	4	1 U	1 U	1 U	1 U	1 U	1 U	1 U	7.3	1 U	1 U
Cadmium, Dissolved	µg/L	5	3 U	3 U	0.87 J	3 U	3 U	3 U	3 U	0.93 J	1.8 J	3 U
Chromium, Dissolved	µg/L	100	1 J	1.3 B	1 B	1.6 B	8.1	2.5 B	1.4 B	0.85 J	5 U	0.79 B
Cobalt, Dissolved	µg/L	6	5 U	5 U	114	2.9 J	5 U	5 U	5 U	123	57.4	4.5 B
Copper, Dissolved	µg/L	1,300	5 U	5 U	5 U	5 U	1.5 B	5 U	5 U	4.9 J	5.9	1.9 J
Iron, Dissolved	µg/L	14,000	121	23.9 J	65,100	13,600	19.4 B	217	45.6 B	44,100	626	957
Manganese, Dissolved	µg/L	430	5.6	5.8 J	11,200	2,110	2.9 B	321	186	5,360	1,280 J	273
Nickel, Dissolved	µg/L	390	10 U	10 U	38.8	4.7 B	10 U	0.93 B	10 U	165	51.3	3.6 B
Selenium, Dissolved	µg/L	50	8 U	8 U	8 U	8 U	8 U	8 U	4.8 B	8 U	8 U	8 U
Silver, Dissolved	µg/L	94	6 U	6 U	1.4 J	0.62 B	6 U	6 U	6 U	6 U	6 U	6 U
Thallium, Dissolved	µg/L	2	10 U	10 U	10 U	10 U	10 U	10 U	10 U	10 U	10 U	10 U
Vanadium, Dissolved	µg/L	86	110	233	5 U	29.3	17.7	5 U	2.5 B	5 U	2.2 B	5 U
Zinc, Dissolved	µg/L	6,000	3.9 B	0.94 B	28.3	3.2 B	0.93 B	1.4 B	10 U	410	75.5	8 B
Other												
Available Cyanide	µg/L	200	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A
Cyanide	µg/L	200	16	10 U	10 U	10 U	10 U	10 U	10.4	10 U	10 U	10 U

Detections in bold

Values in red indicate an exceedance of the Project Action Limit (PAL)

* indicates non-validated data

N/A indicates that the parameter was not analyzed for this sample

U: This analyte was not detected in the sample. The numeric value represents the sample quantitation/detection limit.

UJ: This analyte was not detected in the sample. The actual quantitation/detection limit may be higher than reported.

J: The positive result reported for this analyte is a quantitative estimate.

J+: The positive result reported for this analyte is a quantitative estimate but may be biased high.

B: This analyte was not detected substantially above the level of the associated method blank/preparation or field blank.

**Table 5 - Sub-Parcel B2-2
COPC Screening Analysis**

Parameter	CAS#	Location of Max Result	Max Detection (mg/kg)	Final Flag	Min Detection (mg/kg)	Average Detection (mg/kg)	Total Samples	Frequency of Detection (%)	Cancer TR=1E-06 (mg/kg)	Non-Cancer HQ=0.1 (mg/kg)	COPC?
1,1,1-Trichloroethane	71-55-6	B5-013-SB-4.5	0.042		0.042	0.04	34	2.94		3,600	no
1,1-Biphenyl	92-52-4	B2-003-SB-1	0.031	J	0.016	0.02	67	5.97	410	20	no
1,2,3-Trichlorobenzene	87-61-6	B5-033-SB-1	0.24	J	0.0034	0.12	34	5.88		93	no
1,2,4-Trichlorobenzene	120-82-1	B5-033-SB-1	0.22	J	0.011	0.12	34	5.88	110	26	no
2,4-Dimethylphenol	105-67-9	B2-031-SB-7	0.057	J	0.032	0.04	63	3.17		1,600	no
2-Butanone (MEK)	78-93-3	B2-040-SB-7	0.025	J	0.025	0.03	34	2.94		19,000	no
2-Methylnaphthalene	91-57-6	B2-031-SB-7	0.86		0.001	0.08	67	82.09		300	no
2-Methylphenol	95-48-7	B2-031-SB-7	0.048	J	0.048	0.05	63	1.59		4,100	no
Acenaphthene	83-32-9	B5-034-SB-1	1		0.0006	0.07	67	65.67		4,500	no
Acenaphthylene	208-96-8	B2-024-SB-1	1.3		0.00053	0.08	67	82.09			no
Acetone	67-64-1	B2-040-SB-7	0.14	J	0.022	0.06	34	61.76		67,000	no
Acetophenone	98-86-2	B2-003-SB-1	0.033	J	0.021	0.03	67	5.97		12,000	no
Aluminum	7429-90-5	B2-023-SB-1	51,000		4,510	19,506	67	98.51		110,000	no
Anthracene	120-12-7	B5-012-SB-1	1.3		0.0011	0.13	67	80.60		23,000	no
Antimony	7440-36-0	B2-045-SB-1	3	J	3	3.00	67	1.49		47	no
Aroclor 1016	12674-11-2	B5-085-SB-1	0.14		0.14	0.14	37	2.70	27	5.1	no
Aroclor 1248	12672-29-6	B2-029-SB-1	0.15		0.15	0.15	37	2.70	0.95		no
Aroclor 1254	11097-69-1	B2-029-SB-1	0.15		0.025	0.08	37	10.81	0.97	1.5	no
Aroclor 1260	11096-82-5	B2-027-SB-1	0.18		0.012	0.10	37	18.92	0.99		no
Arsenic	7440-38-2	B2-023-SB-4	24.3		1.9	6.82	73	82.19	3	48	YES (C)
Barium	7440-39-3	B2-024-SB-1	840		27.1	192	67	100.00		22,000	no
Benz[a]anthracene	56-55-3	B5-034-SB-1	2.9		0.002	0.41	67	91.04	21		no
Benzaldehyde	100-52-7	B2-031-SB-7	0.28		0.018	0.06	67	19.40	820	12,000	no
Benzene	71-43-2	B5-014-SB-4	0.0084		0.004	0.007	34	11.76	5.1	42	no
Benzo[a]pyrene	50-32-8	B2-031-SB-7	2.5		0.0011	0.39	67	91.04	2.1	22	YES (C)
Benzo[b]fluoranthene	205-99-2	B2-031-SB-7	4.9		0.00071	0.77	67	94.03	21		no
Benzo[g,h,i]perylene	191-24-2	B2-031-SB-7	1.8		0.0018	0.26	67	88.06			no
Benzo[k]fluoranthene	207-08-9	B2-031-SB-7 & B5-012-SB-1	3.8		0.001	0.51	67	92.54	210		no
Beryllium	7440-41-7	B2-030-SB-5	8.3		0.13	1.99	67	74.63	6,900	230	no
bis(2-Ethylhexyl)phthalate	117-81-7	B2-027-SB-1	0.34		0.02	0.08	67	10.45	160	1,600	no
Cadmium	7440-43-9	B2-003-SB-1	5.9		0.28	1.44	67	40.30	9,300	98	no
Carbazole	86-74-8	B2-004-SB-5	0.43		0.018	0.11	67	20.90			no
Carbon disulfide	75-15-0	B2-023-SB-4	0.0074		0.0033	0.005	34	5.88		350	no
Chromium	7440-47-3	B5-013-SB-4.5	5,180	J	8.4	538	67	100.00		180,000	no
Chromium VI	18540-29-9	B2-039-SB-5	16.9		0.18	1.66	67	41.79	6.3	350	YES (C)
Chrysene	218-01-9	B5-034-SB-1	4.6		0.00091	0.47	67	94.03	2,100		no

**Table 5 - Sub-Parcel B2-2
COPC Screening Analysis**

Parameter	CAS#	Location of Max Result	Max Detection (mg/kg)	Final Flag	Min Detection (mg/kg)	Average Detection (mg/kg)	Total Samples	Frequency of Detection (%)	Cancer TR=1E-06 (mg/kg)	Non-Cancer HQ=0.1 (mg/kg)	COPC?
Cobalt	7440-48-4	B5-014-SB-4	98.8		0.62	10.2	67	82.09	1,900	35	YES (NC)
Copper	7440-50-8	B2-052-SB-1	1,220	J	1.5	83.0	67	100.00		4,700	no
Cyanide	57-12-5	B5-014-SB-4	29.3	J+	0.068	2.23	67	79.10		120	no
Cyclohexane	110-82-7	B5-012-SB-1	0.014		0.014	0.01	34	2.94		2,700	no
Dibenz[a,h]anthracene	53-70-3	B2-031-SB-7	0.58		0.0015	0.11	67	70.15	2.1		no
Diethylphthalate	84-66-2	B2-035-SB-4	0.021	J	0.015	0.02	67	10.45		66,000	no
Di-n-butylphthalate	84-74-2	B2-038-SB-5	0.52	J	0.077	0.23	67	5.97		8,200	no
Di-n-ocetylphthalate	117-84-0	B2-048-SB-1	0.16	J	0.029	0.09	67	2.99		820	no
Fluoranthene	206-44-0	B5-034-SB-1	6.2		0.00057	0.79	67	92.54		3,000	no
Fluorene	86-73-7	B5-012-SB-1	0.77		0.00067	0.06	67	74.63		3,000	no
Hexachloroethane	67-72-1	B2-031-SB-7	0.043	J	0.043	0.04	67	1.49	8	46	no
Indeno[1,2,3-c,d]pyrene	193-39-5	B2-031-SB-7	1.6		0.0012	0.24	67	86.57	21		no
Iron	7439-89-6	B5-085-SB-1	344,000		3,290	93,357	67	100.00		82,000	YES (NC)
Lead^	7439-92-1	B2-003-SB-4.5	1,920		1.5	106	67	95.52		800	YES (NC)
Manganese	7439-96-5	B2-039-SB-5	44,900		39	10,884	68	100.00		2,600	YES (NC)
Mercury	7439-97-6	B2-040-SB-7	0.52		0.0026	0.09	67	56.72		35	no
Naphthalene	91-20-3	B5-033-SB-1	41.2		0.0035	1.07	67	68.66	17	59	YES (C)
Nickel	7440-02-0	B5-014-SB-4	738		2.6	40.4	67	97.01	64,000	2,200	no
PCBs (total)*	1336-36-3	B2-029-SB-1	0.3		0.039	0.12	37	21.62	0.94		no
Phenanthrene	85-01-8	B5-012-SB-1	5.1		0.00079	0.45	67	92.54			no
Phenol	108-95-2	B2-023-SB-4	0.18		0.058	0.12	63	3.17		25,000	no
Pyrene	129-00-0	B5-034-SB-1	5.4		0.0019	0.68	67	91.04		2,300	no
Selenium	7782-49-2	B5-135-SB-1	5.3		2.5	3.59	67	10.45		580	no
Silver	7440-22-4	B2-044-SB-7	77.2		1	14.4	67	64.18		580	no
Tetrachloroethene	127-18-4	B5-040-SB-1	0.0042	J	0.0038	0.004	34	5.88	100	39	no
Thallium	7440-28-0	B5-012-SB-5	14.4	J	12.9	13.7	67	2.99		1.2	YES (NC)
Toluene	108-88-3	B5-014-SB-4	0.0044	J	0.0018	0.003	34	17.65		4,700	no
Vanadium	7440-62-2	B5-012-SB-1	4,710	J	9.2	516	67	100.00		580	YES (NC)
Zinc	7440-66-6	B2-044-SB-1	3,490		7.2	309	67	98.51		35,000	no

J: The positive result reported for this analyte is a quantitative estimate

J+: The positive result reported for this analyte is a quantitative estimate but may be biased high

COPC = Constituent of Potential Concern

C = Compound was identified as a cancer COPC

TR = Target Risk

NC = Compound was identified as a non-cancer COPC

HQ = Hazard Quotient

*PCBs (total) include the sum of all detected aroclor mixtures, including those without regional screening levels (e.g. Aroclor 1261, Aroclor 1268) which are not displayed.

^The COPC screening level for lead was not adjusted to the HQ=0.1 because lead is not assessed in the SLRA. The 800 mg/kg PAL is relevant to the Adult Lead Model procedure.

**Table 6 - Sub-Parcel B2-2
Assessment of Lead**

Exposure Unit	Surface/Sub-Surface	Arithmetic Mean (mg/kg)
EU1 Inside (34.5 ac.)	Surface	93.2
	Sub-Surface	80.7
	Pooled	87.4
EU2 Outside (63.5 ac.)	Surface	82.5
	Sub-Surface	133
	Pooled	105

Adult Lead Model (ALM) Risk Levels	
Soil Concentration (mg/kg)	Probability of Blood Concentration of 10 ug/dL
2,518 mg/kg	5%
3,216 mg/kg	10%

**Table 7 - Sub-Parcel B2-2
Soil Exposure Point Concentrations**

			EU1 Inside (34.5 ac.)					
			Surface Soil EPCs		Sub-Surface Soil EPCs		Pooled Soil EPCs	
Parameter	Cancer COPC Screening Level (mg/kg)	Non-Cancer COPC Screening Level (mg/kg)	EPC Type EU1 Inside	EPC EU1 Inside (mg/kg)	EPC Type EU1 Inside	EPC EU1 Inside (mg/kg)	EPC Type EU1 Inside	EPC EU1 Inside (mg/kg)
Arsenic	3.00	48.0	95% KM (t) UCL	7.43	95% KM (t) UCL	9.86	95% GROS Adjusted Gamma UCL	9.39
Chromium VI	6.30	350	95% KM (t) UCL	0.57	95% KM (Percentile Bootstrap) UCL	0.60	95% KM (t) UCL	0.52
Cobalt	1,900	35.0	95% KM (t) UCL	8.93	95% Adjusted Gamma UCL	41.0	95% KM (Chebyshev) UCL	28.8
Iron		82,000	95% Student's-t UCL	155,013	95% Adjusted Gamma UCL	115,711	95% Adjusted Gamma UCL	129,568
Manganese		2,600	95% Student's-t UCL	15,985	95% Student's-t UCL	15,893	95% Student's-t UCL	14,367
Vanadium		580	95% Student's-t UCL	573	95% Adjusted Gamma UCL	976	95% Adjusted Gamma UCL	614
Benzo[a]pyrene	2.10	22.0	95% Adjusted Gamma UCL	0.97	95% Adjusted Gamma KM-UCL	1.38	95% KM (Chebyshev) UCL	0.87
Naphthalene	17.0	59.0	95% KM (BCA) UCL	0.08	95% KM (Chebyshev) UCL	0.53	97.5% KM (Chebyshev) UCL	0.35

Bold indicates EPC higher than lowest COPC Screening Level
COPC = Constituent of Potential Concern

**Table 7 - Sub-Parcel B2-2
Soil Exposure Point Concentrations**

			EU2 Outside (63.5 ac.)					
			Surface Soil EPCs		Sub-Surface Soil EPCs		Pooled Soil EPCs	
Parameter	Cancer COPC Screening Level (mg/kg)	Non-Cancer COPC Screening Level (mg/kg)	EPC Type EU2 Outside	EPC EU2 Outside (mg/kg)	EPC Type EU2 Outside	EPC EU2 Outside (mg/kg)	EPC Type EU2 Outside	EPC EU2 Outside (mg/kg)
Arsenic	3.00	48.0	95% GROS Adjusted Gamma UCL	7.64	95% KM (Chebyshev) UCL	10.4	95% KM (Chebyshev) UCL	8.30
Chromium VI	6.30	350	95% KM (t) UCL	1.52	95% KM (BCA) UCL	3.05	95% Adjusted Gamma KM-UCL	2.23
Cobalt	1,900	35.0	95% GROS Adjusted Gamma UCL	7.43	95% KM (BCA) UCL	10.8	95% GROS Adjusted Gamma UCL	8.00
Iron		82,000	95% Student's-t UCL	142,678	95% Chebyshev (Mean, Sd) UCL	131,355	95% Adjusted Gamma UCL	118,476
Manganese		2,600	95% Adjusted Gamma UCL	21,156	97.5% Chebyshev (Mean, Sd) UCL	27,063	95% Adjusted Gamma UCL	16,530
Vanadium		580	95% Chebyshev (Mean, Sd) UCL	1,372	95% Chebyshev (Mean, Sd) UCL	1,516	95% Chebyshev (Mean, Sd) UCL	1,174
Benzo[a]pyrene	2.10	22.0	95% KM (Chebyshev) UCL	0.90	95% KM (Chebyshev) UCL	0.74	95% KM (Chebyshev) UCL	0.69
Naphthalene	17.0	59.0	99% KM (Chebyshev) UCL	17.5	99% KM (Chebyshev) UCL	1.52	97.5% KM (Chebyshev) UCL	6.50

Bold indicates EPC higher than lowest COPC Screening Level
COPC = Constituent of Potential Concern

**Table 8 - Sub-Parcel B2-2
Surface Soils
Composite Worker Risk Ratios**

Parameter		Target Organ		EU1 Inside (34.5 ac.)				EU2 Outside (63.5 ac.)							
				EPC mg/kg		Composite Worker				EPC mg/kg		Composite Worker			
						RSLs		Risk Estimates				RSLs		Risk Estimates	
						Cancer	Non-Cancer	Risk	HQ			Cancer	Non-Cancer	Risk	HQ
Arsenic	Cardiovascular; Dermal	7.43	3.00	480	2.5E-06	0.02	7.64	3.00	480	2.5E-06	0.02				
Chromium VI	Respiratory	0.57	6.30	3,500	9.0E-08	0.0002	1.52	6.30	3,500	2.4E-07	0.0004				
Cobalt	Thyroid	8.93	1,900	350	4.7E-09	0.03	7.43	1,900	350	3.9E-09	0.02				
Iron	Gastrointestinal	155,013		820,000		0.2	142,678		820,000		0.2				
Manganese	Nervous	15,985		26,000		0.6	21,156		26,000		0.8				
Vanadium	Dermal	573		5,800		0.1	1,372		5,800		0.2				
Benzo[a]pyrene	Developmental	0.97	2.10	220	4.6E-07	0.004	0.90	2.10	220	4.3E-07	0.004				
Naphthalene	Nervous; Respiratory	0.08	17.0	590	4.7E-09	0.0001	17.5	17.0	590	1.0E-06	0.03				
					3E-06	↓				4E-06	↓				

RSLs were obtained from the EPA Regional Screening Levels at https://epa-prgs.ornl.gov/cgi-bin/chemicals/csl_search

Total HI	Cardiovascular	0
	Dermal	0
	Respiratory	0
	Thyroid	0
	Gastrointestinal	0
	Nervous	1
	Developmental	0

Total HI	Cardiovascular	0
	Dermal	0
	Respiratory	0
	Thyroid	0
	Gastrointestinal	0
	Nervous	1
	Developmental	0

**Table 9 - Sub-Parcel B2-2
Sub-Surface Soils
Composite Worker Risk Ratios**

Parameter		Target Organ		EU1 Inside (34.5 ac.)				EU2 Outside (63.5 ac.)							
				EPC mg/kg		Composite Worker				EPC mg/kg		Composite Worker			
						RSLs		Risk Estimates				RSLs		Risk Estimates	
						Cancer	Non-Cancer	Risk	HQ			Cancer	Non-Cancer	Risk	HQ
Arsenic	Cardiovascular; Dermal	9.86	3.00	480	3.3E-06	0.02	10.4	3.00	480	3.5E-06	0.02				
Chromium VI	Respiratory	0.60	6.30	3,500	9.5E-08	0.0002	3.05	6.30	3,500	4.8E-07	0.0009				
Cobalt	Thyroid	41.0	1,900	350	2.2E-08	0.1	10.8	1,900	350	5.7E-09	0.03				
Iron	Gastrointestinal	115,711		820,000		0.1	131,355		820,000		0.2				
Manganese	Nervous	15,893		26,000		0.6	27,063		26,000		1				
Vanadium	Dermal	976		5,800		0.2	1,516		5,800		0.3				
Benzo[a]pyrene	Developmental	1.38	2.10	220	6.6E-07	0.006	0.74	2.10	220	3.5E-07	0.003				
Naphthalene	Nervous; Respiratory	0.53	17.0	590	3.1E-08	0.0009	1.52	17.0	590	8.9E-08	0.003				
					4E-06	↓				4E-06	↓				

RSLs were obtained from the EPA Regional Screening Levels at https://epa-prgs.ornl.gov/cgi-bin/chemicals/csl_search

Total HI	Cardiovascular	0
	Dermal	0
	Respiratory	0
	Thyroid	0
	Gastrointestinal	0
	Nervous	1
	Developmental	0

Total HI	Cardiovascular	0
	Dermal	0
	Respiratory	0
	Thyroid	0
	Gastrointestinal	0
	Nervous	1
	Developmental	0

**Table 10 - Sub-Parcel B2-2
Pooled Soils
Composite Worker Risk Ratios**

Parameter		Target Organ		EU1 Inside (34.5 ac.)				EU2 Outside (63.5 ac.)							
				EPC mg/kg		Composite Worker				EPC mg/kg		Composite Worker			
						RSLs		Risk Estimates				RSLs		Risk Estimates	
						Cancer	Non-Cancer	Risk	HQ			Cancer	Non-Cancer	Risk	HQ
Arsenic	Cardiovascular; Dermal	9.39	3.00	480	3.1E-06	0.02	8.30	3.00	480	2.8E-06	0.02				
Chromium VI	Respiratory	0.52	6.30	3,500	8.3E-08	0.0001	2.23	6.30	3,500	3.5E-07	0.0006				
Cobalt	Thyroid	28.8	1,900	350	1.5E-08	0.08	8.00	1,900	350	4.2E-09	0.02				
Iron	Gastrointestinal	129,568		820,000		0.2	118,476		820,000		0.1				
Manganese	Nervous	14,367		26,000		0.6	16,530		26,000		0.6				
Vanadium	Dermal	614		5,800		0.1	1,174		5,800		0.2				
Benzo[a]pyrene	Developmental	0.87	2.10	220	4.1E-07	0.004	0.69	2.10	220	3.3E-07	0.003				
Naphthalene	Nervous; Respiratory	0.35	17.0	590	2.1E-08	0.0006	6.50	17.0	590	3.8E-07	0.01				
					4E-06	↓				4E-06	↓				

RSLs were obtained from the EPA Regional Screening Levels at https://epa-prgs.ornl.gov/cgi-bin/chemicals/csl_search

Total HI	Cardiovascular	0
	Dermal	0
	Respiratory	0
	Thyroid	0
	Gastrointestinal	0
	Nervous	1
	Developmental	0

Total HI	Cardiovascular	0
	Dermal	0
	Respiratory	0
	Thyroid	0
	Gastrointestinal	0
	Nervous	1
	Developmental	0

**Table 11 - Sub-Parcel B2-2
Surface Soils
Construction Worker Risk Ratios**

		95 Day - EU1 Inside (34.5 ac.)					55 Day - EU2 Outside (63.5 ac.)				
		EPC mg/kg	Construction Worker				EPC mg/kg	Construction Worker			
			SSLs		Risk Estimates			SSLs		Risk Estimates	
Parameter	Target Organ		Cancer	Non-Cancer	Risk	HQ		Cancer	Non-Cancer	Risk	HQ
Arsenic	Cardiovascular; Dermal	7.43	39.8	254	1.9E-07	0.03	7.64	68.8	439	1.1E-07	0.02
Chromium VI	Respiratory	0.57	56.7	2,107	1.0E-08	0.0003	1.52	98.9	3,644	1.5E-08	0.0004
Cobalt	Thyroid	8.93	11,986	2,493	7.5E-10	0.004	7.43	27,198	4,392	2.7E-10	0.002
Iron	Gastrointestinal	155,013		633,004		0.2	142,678		1,093,370		0.1
Manganese	Nervous	15,985		10,957		1	21,156		19,591		1
Vanadium	Dermal	573		4,206		0.1	1,372		7,313		0.2
Benzo[a]pyrene	Developmental	0.97	44.8	15.9	2.2E-08	0.06	0.90	76.0	19.7	1.2E-08	0.05
Naphthalene	Nervous; Respiratory	0.08	34.5	50.3	2.3E-09	0.002	17.5	41.6	60.5	4.2E-07	0.3
					2E-07	↓				6E-07	↓

SSLs calculated using equations in the EPA Supplemental Guidance dated 2002

Guidance Equation Input Assumptions:

- 5 cars/day (2 tons/car)
- 5 trucks/day (20 tons/truck)
- 3 meter source depth thickness

Total HI	Cardiovascular	0
	Dermal	0
	Respiratory	0
	Thyroid	0
	Gastrointestinal	0
	Nervous	1
	Developmental	0

Total HI	Cardiovascular	0
	Dermal	0
	Respiratory	0
	Thyroid	0
	Gastrointestinal	0
	Nervous	1
	Developmental	0

**Table 12 - Sub-Parcel B2-2
Sub-Surface Soils
Construction Worker Risk Ratios**

		95 Day - EU1 Inside (34.5 ac.)					55 Day - EU2 Outside (63.5 ac.)				
		EPC mg/kg	Construction Worker				EPC mg/kg	Construction Worker			
			SSLs		Risk Estimates			SSLs		Risk Estimates	
Parameter	Target Organ		Cancer	Non-Cancer	Risk	HQ		Cancer	Non-Cancer	Risk	HQ
Arsenic	Cardiovascular; Dermal	9.86	39.8	254	2.5E-07	0.04	10.4	68.8	439	1.5E-07	0.02
Chromium VI	Respiratory	0.60	56.7	2,107	1.1E-08	0.0003	3.05	98.9	3,644	3.1E-08	0.0008
Cobalt	Thyroid	41.0	11,986	2,493	3.4E-09	0.02	10.8	27,198	4,392	4.0E-10	0.002
Iron	Gastrointestinal	115,711		633,004		0.2	131,355		1,093,370		0.1
Manganese	Nervous	15,893		10,957		1	27,063		19,591		1
Vanadium	Dermal	976		4,206		0.2	1,516		7,313		0.2
Benzo[a]pyrene	Developmental	1.38	44.8	15.9	3.1E-08	0.09	0.74	76.0	19.7	9.7E-09	0.04
Naphthalene	Nervous; Respiratory	0.53	34.5	50.3	1.5E-08	0.01	1.52	41.6	60.5	3.7E-08	0.03
					3E-07	↓				2E-07	↓

SSLs calculated using equations in the EPA Supplemental Guidance dated 2002

Guidance Equation Input Assumptions:

- 5 cars/day (2 tons/car)
- 5 trucks/day (20 tons/truck)
- 3 meter source depth thickness

Total HI	Cardiovascular	0
	Dermal	0
	Respiratory	0
	Thyroid	0
	Gastrointestinal	0
	Nervous	1
	Developmental	0

Total HI	Cardiovascular	0
	Dermal	0
	Respiratory	0
	Thyroid	0
	Gastrointestinal	0
	Nervous	1
	Developmental	0

**Table 13 - Sub-Parcel B2-2
Pooled Soils
Construction Worker Risk Ratios**

		95 Day - EU1 Inside (34.5 ac.)					55 Day - EU2 Outside (63.5 ac.)				
		EPC mg/kg	Construction Worker				EPC mg/kg	Construction Worker			
			SSLs		Risk Estimates			SSLs		Risk Estimates	
Parameter	Target Organ		Cancer	Non-Cancer	Risk	HQ		Cancer	Non-Cancer	Risk	HQ
Arsenic	Cardiovascular; Dermal	9.39	39.8	254	2.4E-07	0.04	8.30	68.8	439	1.2E-07	0.02
Chromium VI	Respiratory	0.52	56.7	2,107	9.2E-09	0.0002	2.23	98.9	3,644	2.3E-08	0.0006
Cobalt	Thyroid	28.8	11,986	2,493	2.4E-09	0.01	8.00	27,198	4,392	2.9E-10	0.002
Iron	Gastrointestinal	129,568		633,004		0.2	118,476		1,093,370		0.1
Manganese	Nervous	14,367		10,957		1	16,530		19,591		0.8
Vanadium	Dermal	614		4,206		0.1	1,174		7,313		0.2
Benzof[a]pyrene	Developmental	0.87	44.8	15.9	1.9E-08	0.05	0.69	76.0	19.7	9.1E-09	0.04
Naphthalene	Nervous; Respiratory	0.35	34.5	50.3	1.0E-08	0.007	6.50	41.6	60.5	1.6E-07	0.1
					3E-07	↓				3E-07	↓

SSLs calculated using equations in the EPA Supplemental Guidance dated 2002

Guidance Equation Input Assumptions:

- 5 cars/day (2 tons/car)
- 5 trucks/day (20 tons/truck)
- 3 meter source depth thickness

Total HI	Cardiovascular	0
	Dermal	0
	Respiratory	0
	Thyroid	0
	Gastrointestinal	0
	Nervous	1
	Developmental	0

Total HI	Cardiovascular	0
	Dermal	0
	Respiratory	0
	Thyroid	0
	Gastrointestinal	0
	Nervous	1
	Developmental	0

"

"

"

"

"

"

"

"

"

APPENDIX A

"

"

"

"

"

"

"

"

"

"

"

"



**TRADEPOINT
ATLANTIC**

1600 Sparrows Point Boulevard
Baltimore, Maryland 21219

September 20, 2018

Maryland Department of Environment
1800 Washington Boulevard
Baltimore MD, 21230

Attention: Ms. Barbara Brown

Subject: Request to Enter Temporary CHS Review
Tradepoint Atlantic Parcel B2-2

Dear Ms. Brown:

The conduct of any environmental assessment and cleanup activities on the Tradepoint Atlantic property, as well as any associated development, is subject to the requirements outlined in the following agreements:

- Administrative Consent Order (ACO) between Tradepoint Atlantic (formerly Sparrows Point Terminal, LLC) and the Maryland Department of the Environment (effective September 12, 2014); and
- Settlement Agreement and Covenant Not to Sue (SA) between Tradepoint Atlantic (formerly Sparrows Point Terminal, LLC) and the United States Environmental Protection Agency (effective November 25, 2014).

On September 11, 2014, Tradepoint Atlantic submitted an application to the Maryland Department of the Environment's (Department) Voluntary Cleanup Program (VCP).

In consultation with the Department, Tradepoint Atlantic affirms that it desires to accelerate the assessment, remediation and redevelopment of certain sub-parcels within the larger site due to current market conditions. To that end, the Department and Tradepoint Atlantic agree that the Controlled Hazardous Substance (CHS) Act (Section 7-222 of the Environment Article) and the CHS Response Plan (COMAR 26.14.02) shall serve as the governing statutory and regulatory authority for completing the development activities on Parcel B2-2 and complement the statutory requirements of the Voluntary Cleanup Program (Section 7-501 of the Environment Article). Upon submission of a Site Response and Development Work Plan and completion of the remedial activities for the sub-parcel, the Department shall issue a "No Further Action" letter upon a recordation of an environmental covenant describing any necessary land use controls for the specific sub-parcel. At such time that all the sub-parcels within the larger parcel have completed remedial activities, Tradepoint Atlantic shall submit to the Department a request for issuing a Certificate of Completion (COC) as well as all pertinent information concerning completion of remedial activities conducted on the parcel. Once the VCP has completed its review of the submitted information it shall issue a COC for the entire parcel described in Tradepoint Atlantic's VCP application.



**TRADEPOINT
ATLANTIC**

1600 Sparrows Point Boulevard
Baltimore, Maryland 21219

Alternatively, Tradepoint Atlantic or other entity may elect to submit an application for a specific sub-parcel and submit it to the VCP for review and acceptance. If the application is received after the cleanup and redevelopment activities described in this work plan are implemented and a No Further Action letter is issued by the Department pursuant to the CHS Act, the VCP shall prepare a No Further Requirements Determination for the sub-parcel.

If Tradepoint Atlantic or other entity has not carried out cleanup and redevelopment activities described in the work plan, the cleanup and redevelopment activities may be conducted under the oversight authority of either the VCP or the CHS Act, so long as those activities comport with this work plan.

Engineering and institutional controls approved as part of this Site Response and Development Work Plan shall be described in documentation submitted to the Department demonstrating that the exposure pathways on the sub-parcel are addressed in a manner that protects public health and the environment. This information shall support Tradepoint Atlantic's request for the issuance of a COC for the larger parcel.

Please do not hesitate to contact Tradepoint Atlantic for further information.

Thank you,

Peter Haid

Senior Director of Environmental
TRADEPOINT ATLANTIC
1600 Sparrows Point Boulevard
Baltimore, Maryland 21219
T 443.649.5055 C 732.841.7935
phaid@tradepointatlantic.com

"

"

"

"

"

"

"

"

"

APPENDIX B

"

"

"

"

"

"

"

"

"

"

"

"

**Sub-Parcel B2-2
Summary of Organics Detected in Soil (NAPL Screening Locations)**

Parameter	Units	PAL	B2-020-SB-1	B2-020-SB-4	B2-021-SB-1	B2-021-SB-4	B2-022-SB-1	B2-022-SB-4	B2-028-SB-1	B2-028-SB-5	B2-049-SB-1	B2-049-SB-4	B2-053-SB-1	B2-053-SB-5.5
Volatile Organic Compounds														
1,2-Dichloroethane	mg/kg	2	N/A	N/A	N/A	0.0048 U	N/A	N/A	0.0044 U	0.0066 U	0.0051 U	0.0044 U	0.0063 U	0.25 U
Acetone	mg/kg	670,000	N/A	N/A	N/A	0.037 J	N/A	N/A	0.0088 U	0.013 U	0.022	0.0074 J	0.013 U	0.5 U
Benzene	mg/kg	5.1	N/A	N/A	N/A	0.0048 U	N/A	N/A	0.0044 U	0.0066 U	0.0051 U	0.0044 U	0.0063 U	0.25 U
Carbon disulfide	mg/kg	3,500	N/A	N/A	N/A	0.0048 U	N/A	N/A	0.0044 UJ	0.0066 UJ	0.0051 UJ	0.0044 UJ	0.0063 UJ	0.25 UJ
Cyclohexane	mg/kg	27,000	N/A	N/A	N/A	0.0096 UJ	N/A	N/A	0.0088 U	0.013 U	0.01 U	0.0088 U	0.013 U	19
Ethylbenzene	mg/kg	25	N/A	N/A	N/A	0.0048 U	N/A	N/A	0.0044 U	0.0066 U	0.0051 U	0.0044 U	0.0063 U	1.8
Isopropylbenzene	mg/kg	9,900	N/A	N/A	N/A	0.0048 U	N/A	N/A	0.0044 U	0.0066 U	0.0051 U	0.0044 U	0.0063 U	2.7
Methyl Acetate	mg/kg	1,200,000	N/A	N/A	N/A	0.048 UJ	N/A	N/A	0.044 UJ	0.066 UJ	0.051 UJ	0.044 UJ	0.063 UJ	2.5 UJ
Methylene Chloride	mg/kg	1,000	N/A	N/A	N/A	0.0048 U	N/A	N/A	0.0044 U	0.0066 U	0.0051 U	0.0044 U	0.0063 U	0.25 U
Toluene	mg/kg	47,000	N/A	N/A	N/A	0.0048 U	N/A	N/A	0.0044 U	0.0066 U	0.0051 U	0.0044 U	0.0063 U	0.19 J
Xylenes	mg/kg	2,800	N/A	N/A	N/A	0.014 U	N/A	N/A	0.013 U	0.02 U	0.015 U	0.013 U	0.019 U	1.4
Semi-Volatile Organic Compounds[^]														
1,1-Biphenyl	mg/kg	200	0.089 U	0.041 J	0.077 U	0.079 U	0.072 U	0.086 U	0.074 U	0.019 J	0.071 U	0.071 U	0.018 J	0.079 U
2,4-Dimethylphenol	mg/kg	16,000	0.089 U	0.072 U	0.077 U	0.079 U	0.072 U	0.086 U	0.074 U	0.075 U	0.071 R	0.071 R	0.076 U	0.057 J
2-Methylnaphthalene	mg/kg	3,000	0.01	0.1	0.031 J	0.007 J	0.0061 J	0.064 J	0.1	0.23	0.01	0.012	0.28	0.7
3&4-Methylphenol(m&p Cresol)	mg/kg	41,000	0.18 U	0.035 J	0.15 U	0.16 U	0.14 U	0.17 U	0.15 U	0.15 U	0.14 R	0.14 R	0.15 U	0.16 U
4-Chloroaniline	mg/kg	11	0.089 U	0.072 U	0.077 U	0.079 U	0.072 U	0.086 U	0.074 U	0.075 U	0.071 U	0.071 U	0.076 U	0.079 U
Acenaphthene	mg/kg	45,000	0.012	0.29	0.07 J	0.01	0.012	0.11	0.075 U	0.077 U	0.0072 U	0.0072 U	0.0092 J	0.0024 J
Acenaphthylene	mg/kg	45,000	0.0023 J	0.079	0.02 J	0.019	0.002 J	0.037 J	0.075 U	0.041 J	0.0072 U	0.0072 U	0.032 J	0.0013 J
Acetophenone	mg/kg	120,000	0.089 U	0.072 U	0.077 U	0.079 U	0.072 U	0.086 U	0.074 U	0.075 U	0.071 U	0.071 U	0.022 J	1.2
Anthracene	mg/kg	230,000	0.011	0.33	0.074 J	0.05	0.011	0.2	0.075 U	0.042 J	0.0009 J	0.0072 U	0.082	0.0031 J
Benz[a]anthracene	mg/kg	21	0.064	1.5	0.34	0.22	0.071	0.61	0.016 J	0.24	0.0039 J	0.0016 J	0.44	0.013
Benzaldehyde	mg/kg	120,000	0.033 J	0.027 J	0.057 J	0.079 U	0.072 U	0.023 J	0.074 R	0.017 J	0.071 R	0.071 R	0.054 J	0.079 U
Benzo[a]pyrene	mg/kg	2.1	0.1	2.4	0.53	0.2	0.11	0.8	0.075 U	0.2	0.0022 J	0.0013 J	0.42	0.012
Benzo[b]fluoranthene	mg/kg	21	0.13	3.2	0.69	0.4	0.18	1	0.026 J	0.48	0.012	0.0038 J	0.97	0.027
Benzo[g,h,i]perylene	mg/kg		0.11	2.4	0.49	0.15	0.1	0.76	0.075 U	0.068 J	0.0081	0.0015 J	0.21	0.0054 J
Benzo[k]fluoranthene	mg/kg	210	0.045	1	0.24	0.32	0.15	0.34	0.017 J	0.33	0.008	0.0015 J	0.77	0.021
bis(2-Chloroethyl)ether	mg/kg	1	0.089 U	0.072 U	0.077 U	0.079 U	0.072 U	0.086 U	0.074 U	0.075 U	0.071 U	0.071 U	0.076 U	0.087
bis(2-Ethylhexyl)phthalate	mg/kg	160	0.089 U	0.13 J	0.038 J	0.079 U	0.024 J	0.037 J	0.074 U	0.075 UJ	0.071 U	0.071 U	0.076 U	0.079 U
Caprolactam	mg/kg	400,000	0.22 U	0.18 U	0.19 U	0.2 U	0.18 U	0.22 U	0.19 U	0.033 J	0.18 U	0.18 U	0.19 U	0.2 U
Carbazole	mg/kg		0.089 U	0.43 J	0.044 J	0.058 J	0.023 J	0.088	0.074 U	0.075 U	0.071 U	0.071 U	0.037 J	0.079 U
Chrysene	mg/kg	2,100	0.064	1.4	0.29	0.22	0.066	0.6	0.012 J	0.14	0.011	0.004 J	0.46	0.013
Dibenz[a,h]anthracene	mg/kg	2.1	0.027	0.54	0.11	0.036	0.029	0.18	0.075 U	0.017 J	0.0072 U	0.0072 U	0.064 J	0.0081 U
Di-n-butylphthalate	mg/kg	82,000	0.074 B	0.083 B	0.046 B	0.04 B	0.048 B	0.035 B	0.074 U	0.075 U	0.071 U	0.071 U	0.076 U	0.079 U
Di-n-octylphthalate	mg/kg	8,200	0.089 U	0.072 UJ	0.077 UJ	0.079 U	0.072 UJ	0.086 UJ	0.074 U	0.075 UJ	0.071 U	0.071 U	0.076 UJ	0.079 UJ
Fluoranthene	mg/kg	30,000	0.089	1.8	0.41	0.43	0.087	0.84	0.017 J	0.27	0.01	0.0098	0.63	0.02
Fluorene	mg/kg	30,000	0.0047 J	0.12	0.034 J	0.013	0.0025 J	0.062 J	0.075 U	0.077 U	0.0072 U	0.0072 U	0.011 J	0.0033 J
Hexachloroethane	mg/kg	8	0.089 U	0.072 U	0.077 U	0.079 U	0.072 U	0.086 U	0.074 U	0.075 U	0.071 U	0.071 U	0.076 U	0.079 U
Indeno[1,2,3-c,d]pyrene	mg/kg	21	0.089	2	0.39	0.13	0.092	0.61	0.075 U	0.068 J	0.0028 J	0.0072 U	0.21	0.0053 J
Isophorone	mg/kg	2,400	0.089 U	0.072 U	0.077 U	0.079 U	0.072 U	0.086 U	0.074 U	0.075 U	0.071 U	0.071 U	0.076 U	0.071 J
Naphthalene	mg/kg	17	0.013	0.14	0.035 J	0.016	0.0073 J	0.073 J	0.075 UJ	0.15 J	0.0072 UJ	0.0037 J	0.22 J	0.076 J
Nitrobenzene	mg/kg	22	0.089 U	0.072 U	0.077 U	0.079 U	0.072 U	0.086 U	0.074 U	0.075 U	0.071 U	0.071 U	0.076 U	0.079 U
Phenanthrene	mg/kg		0.053	1.2	0.22	0.19	0.039	0.68	0.018 J	0.15	0.0062 J	0.01	0.5 J	0.017 J
Phenol	mg/kg	250,000	0.089 U	0.028 J	0.077 U	0.079 U	0.072 U	0.086 U	0.074 U	0.075 U	0.071 R	0.071 R	0.076 U	0.079 U
Pyrene	mg/kg	23,000	0.072	1.6	0.36	0.36	0.078	0.86	0.012 J	0.24	0.0093	0.0076	0.58	0.017
PCBs														
Aroclor 1260	mg/kg	0.99	0.022 U	N/A	0.02 U	N/A	0.018 U	N/A	0.019 U	N/A	0.018 U	N/A	0.019 U	N/A
PCBs (total)	mg/kg	0.97	0.15 U	N/A	0.14 U	N/A	0.13 U	N/A	0.13 U	N/A	0.13 U	N/A	0.13 U	N/A
TPH/Oil and Grease														
Diesel Range Organics	mg/kg	6,200	16.5 J	80.6 J	41.4 J	12.9 J	14.5 J	143 J	12.4	99.8	30.4	17.4	136 J	201 J
Gasoline Range Organics	mg/kg	6,200	12.2 U	3.6 B	10.7 U	10.5 U	10.7 U	15.4 U	2.7 J	4.7 J	3.1 J	3 J	8.4 J	1,130
Oil and Grease	mg/kg	6,200	356 J-	1,460 J-	526 J-	162 J-	58.9 J-	258 J-	112 J	2,770	182	64.9 J	538	262

Detections in bold

Values in red indicate an exceedance of the Project Action Limit (PAL)

N/A indicates that the parameter was not analyzed for this sample.

[^]PAH compounds were analyzed via SIM

*indicates non-validated data

Locations B5-035-SB and B5-036-SB were not sampled due to shallow refusals.

U: This analyte was not detected in the sample. The numeric value represents the sample quantitation/detection limit.

UJ: This analyte was not detected in the sample. The actual quantitation/detection limit may be higher than reported.

J: The positive result reported for this analyte is a quantitative estimate.

J-: The positive result reported for this analyte is a quantitative estimate but may be biased low.

B: This analyte was not detected substantially above the level of the associated method blank/preparation or field blank.

R: The result for this analyte is unreliable. Additional data is needed to confirm or disprove the presence of this analyte in the sample.

**Sub-Parcel B2-2
Summary of Organics Detected in Soil (NAPL Screening Locations)**

Parameter	Units	PAL	B2-054-SB-1	B2-054-SB-5	B2-055-SB-1	B2-055-SB-6.5	B2-064-SB-1	B2-064-SB-5	B2-065-SB-1*	B2-065-SB-4.5*	B2-069-SB-1	B2-069-SB-4	B5-032-SB-1*	B5-032-SB-5*
Volatile Organic Compounds														
1,2-Dichloroethane	mg/kg	2	0.0017 J	0.0046 U	0.0067 U	0.27 U	N/A	N/A	N/A	N/A	N/A	N/A	0.005 U	0.0057 U
Acetone	mg/kg	670,000	0.015 U	0.024 J	0.013 U	14.6 J	N/A	N/A	N/A	N/A	N/A	N/A	0.089	0.078
Benzene	mg/kg	5.1	0.0073 U	0.0046 U	0.0067 U	0.16 J	N/A	N/A	N/A	N/A	N/A	N/A	0.005 U	0.0057 U
Carbon disulfide	mg/kg	3,500	0.0073 UJ	0.0046 UJ	0.0033 J	0.27 UJ	N/A	N/A	N/A	N/A	N/A	N/A	0.005 U	0.0057 U
Cyclohexane	mg/kg	27,000	0.015 U	0.0092 U	0.013 U	26.9 J	N/A	N/A	N/A	N/A	N/A	N/A	0.0099 U	0.011 U
Ethylbenzene	mg/kg	25	0.0073 U	0.0046 U	0.0067 U	0.39	N/A	N/A	N/A	N/A	N/A	N/A	0.005 U	0.0057 U
Isopropylbenzene	mg/kg	9,900	0.0073 U	0.0046 U	0.0067 U	5.2 J	N/A	N/A	N/A	N/A	N/A	N/A	0.005 U	0.0057 U
Methyl Acetate	mg/kg	1,200,000	0.073 UJ	0.046 UJ	0.067 UJ	2.7 UJ	N/A	N/A	N/A	N/A	N/A	N/A	0.05 U	0.057 U
Methylene Chloride	mg/kg	1,000	0.0073 U	0.0046 U	0.0067 U	0.27 U	N/A	N/A	N/A	N/A	N/A	N/A	0.005 U	0.0057 U
Toluene	mg/kg	47,000	0.0073 U	0.0046 U	0.0067 U	0.27 U	N/A	N/A	N/A	N/A	N/A	N/A	0.005 U	0.0057 U
Xylenes	mg/kg	2,800	0.022 U	0.014 U	0.02 U	0.44 J	N/A	N/A	N/A	N/A	N/A	N/A	0.015 U	0.017 U
Semi-Volatile Organic Compounds[^]														
1,1-Biphenyl	mg/kg	200	0.4 U	0.082 U	1.4 U	0.39 U	0.07 U	0.077 U	0.086 U	0.077 U	0.072 U	0.073 U	7.6 U	7.2 U
2,4-Dimethylphenol	mg/kg	16,000	0.4 U	0.082 U	1.4 U	0.14 J	0.07 R	0.077 R	0.086 U	0.077 U	0.072 R	0.073 R	7.6 U	7.2 U
2-Methylnaphthalene	mg/kg	3,000	0.052 J	0.0082 U	0.042 J	1.8	0.0012 J	0.042	0.0072 J	0.011	0.0056 J	0.0085	0.11	0.054
3&4-Methylphenol(m&p Cresol)	mg/kg	41,000	0.79 U	0.16 U	2.8 U	0.77 U	0.14 R	0.15 R	0.17 U	0.15 U	0.14 R	0.15 R	15.1 U	2.4 J
4-Chloroaniline	mg/kg	11	0.4 U	0.082 U	1.4 U	0.12 J	0.07 U	0.077 U	0.086 U	0.077 U	0.072 U	0.073 U	7.6 U	7.2 U
Acenaphthene	mg/kg	45,000	0.043 J	0.0082 UJ	0.0079 J	0.077 J	0.0071 U	0.011	0.00074 J	0.00078 J	0.0008 J	0.0016 J	0.077	0.0023 J
Acenaphthylene	mg/kg	45,000	0.069 J	0.0082 UJ	0.59 J	0.032 J	0.0006 J	0.59	0.0016 J	0.0053 J	0.0012 J	0.025	0.0096	0.0057 J
Acetophenone	mg/kg	120,000	0.4 U	0.082 U	1.4 U	0.39 U	0.07 U	0.077 U	0.086 U	0.077 U	0.072 U	0.073 U	7.6 U	7.2 U
Anthracene	mg/kg	230,000	0.22	0.0082 U	0.21	0.19	0.00066 J	0.58	0.0053 J	0.0027 J	0.0019 J	0.036	0.16	0.0084
Benz[a]anthracene	mg/kg	21	1.1	0.0082 U	1.6	0.29	0.0039 J	3	0.018	0.012	0.0057 J	0.1	0.62	0.026
Benzaldehyde	mg/kg	120,000	0.4 U	0.082 U	1.4 U	0.28 J	0.07 R	0.077 R	0.086 U	0.077 U	0.072 R	0.073 R	7.6 U	7.2 U
Benzo[a]pyrene	mg/kg	2.1	1.1	0.0082 U	2.8	0.24	0.0024 J	2	0.019	0.012	0.0031 J	0.11	0.76	0.05
Benzo[b]fluoranthene	mg/kg	21	2.4	0.0082 U	5.5	0.53	0.0048 J	5.1	0.053	0.034	0.014	0.3	2.7	0.24
Benzo[g,h,i]perylene	mg/kg		0.56	0.0082 U	1.6	0.095	0.0012 J	0.49	0.019	0.01	0.0036 J	0.036	0.019	0.019
Benzo[k]fluoranthene	mg/kg	210	1.9	0.0082 U	4.4	0.42	0.0017 J	1.9	0.042	0.027	0.01	0.085	2.7	0.24
bis(2-Chloroethyl)ether	mg/kg	1	0.4 U	0.082 U	1.4 U	0.39 U	0.07 U	0.077 U	0.086 U	0.077 U	0.072 U	0.073 U	7.6 U	7.2 U
bis(2-Ethylhexyl)phthalate	mg/kg	160	0.4 U	0.082 U	1.4 U	0.39 U	0.07 U	0.077 U	0.086 U	0.077 U	0.072 U	0.073 U	7.6 U	7.2 U
Caprolactam	mg/kg	400,000	1 U	0.2 U	3.5 U	0.97 U	0.18 U	0.19 U	0.21 U	0.19 U	0.18 U	0.18 U	18.9 U	18.1 U
Carbazole	mg/kg		0.17 J	0.082 U	1.4 U	0.39 U	0.07 U	0.029 J	0.086 U	0.077 U	0.072 U	0.073 U	7.6 U	7.2 U
Chrysene	mg/kg	2,100	1	0.0082 U	1.6	0.23	0.0024 J	2	0.027	0.016	0.011	0.13	0.87	0.064
Dibenz[a,h]anthracene	mg/kg	2.1	0.18	0.0082 U	0.44	0.03 J	0.0071 U	0.28	0.0049 J	0.0034 J	0.0072 U	0.015	0.1	0.0073 U
Di-n-butylphthalate	mg/kg	82,000	0.4 U	0.082 U	1.4 U	0.39 U	0.07 U	0.077 U	0.024 J	0.02 J	0.072 U	0.073 U	7.6 U	7.2 U
Di-n-octylphthalate	mg/kg	8,200	0.4 UJ	0.082 UJ	1.4 U	0.39 UJ	0.051 J	0.077 U	0.086 U	0.077 U	0.072 U	0.073 U	7.6 U	7.2 U
Fluoranthene	mg/kg	30,000	2	0.0015 J	2	0.72	0.0054 J	3.2	0.029	0.025	0.017	0.13	1.5	0.04
Fluorene	mg/kg	30,000	0.033 J	0.0082 UJ	0.016 J	0.13 J	0.0071 U	0.025	0.0012 J	0.0013 J	0.00057 J	0.0021 J	0.064	0.0018 J
Hexachloroethane	mg/kg	8	0.4 U	0.082 U	1.4 U	3.7	0.07 U	0.077 U	0.086 U	0.077 U	0.072 U	0.073 U	7.6 U	7.2 U
Indeno[1,2,3-c,d]pyrene	mg/kg	21	0.54	0.0082 U	1.6	0.1	0.0071 U	0.66	0.015	0.0088	0.0019 J	0.04	0.23	0.015
Isophorone	mg/kg	2,400	0.4 U	0.082 U	1.4 U	0.19 J	0.07 U	0.077 U	0.086 U	0.077 U	0.072 U	0.073 U	7.6 U	7.2 U
Naphthalene	mg/kg	17	0.098 J	0.0082 UJ	0.13 J	0.16 J	0.0071 UJ	0.042 J	0.012	0.046	0.0032 J	0.0087 J	0.32	0.044
Nitrobenzene	mg/kg	22	0.4 U	0.082 U	1.4 U	0.3 J	0.07 U	0.077 U	0.086 U	0.077 U	0.072 U	0.073 U	7.6 U	7.2 U
Phenanthrene	mg/kg		0.76 J	0.0082 UJ	0.24 J	0.58 J	0.0031 J	0.42	0.025	0.018	0.025	0.039	0.82	0.064
Phenol	mg/kg	250,000	0.4 U	0.082 U	1.4 U	0.39 U	0.07 R	0.077 R	0.086 U	0.077 U	0.072 R	0.073 R	7.6 U	8.9
Pyrene	mg/kg	23,000	1.7	0.0014 J	2.7	0.62	0.0046 J	3.2	0.027	0.021	0.017	0.16	1.2	0.035
PCBs														
Aroclor 1260	mg/kg	0.99	0.02 U	N/A	0.018 U	N/A	0.018 U	N/A	0.062	N/A	0.018 U	N/A	0.019 U	N/A
PCBs (total)	mg/kg	0.97	0.14 U	N/A	0.12 U	N/A	0.16 U	N/A	0.062 J	N/A	0.16 U	N/A	0.13 U	N/A
TPH/Oil and Grease														
Diesel Range Organics	mg/kg	6,200	55.9 J	15.1 J	121 J	817 J	7.7 J	41.7 J	49.7	38.8	14.8 J	15.1 J	300	133
Gasoline Range Organics	mg/kg	6,200	16	355	8.6 B	1,270	9.2 U	3 J	12.7 U	8.1 U	8.8 U	9.9 U	10.3 U	11.4 U
Oil and Grease	mg/kg	6,200	672	312	455	348	64.3 J-	251 J-	118 J	275	200 J-	129 J-	N/A	N/A

Detections in bold

Values in red indicate an exceedance of the Project Action Limit (PAL)

N/A indicates that the parameter was not analyzed for this sample.

[^]PAH compounds were analyzed via SIM

*indicates non-validated data

Locations B5-035-SB and B5-036-SB were not sampled due to shallow refusals.

U: This analyte was not detected in the sample. The numeric value represents the sample quantitation/detection limit.

UJ: This analyte was not detected in the sample. The actual quantitation/detection limit may be higher than reported.

J: The positive result reported for this analyte is a quantitative estimate.

J-: The positive result reported for this analyte is a quantitative estimate but may be biased low.

B: This analyte was not detected substantially above the level of the associated method blank/preparation or field blank.

R: The result for this analyte is unreliable. Additional data is needed to confirm or disprove the presence of this analyte in the sample.

**Sub-Parcel B2-2
Summary of Organics Detected in Soil (NAPL Screening Locations)**

Parameter	Units	PAL	B5-035-SB	B5-036-SB	B5-037-SB-1*	B5-037-SB-5*	B5-038-SB-1*	B5-038-SB-5*	B5-086-SB-1*	B5-087-SB-1*	B5-087-SB-5*	B5-096-SB-1*	B5-096-SB-5*	B5-097-SB-1*	B5-097-SB-4*
Volatile Organic Compounds															
1,2-Dichloroethane	mg/kg	2	N/A	N/A	0.0046 U	0.0047 U	0.0062 U	0.0052 U	0.0055 U	0.0042 U	0.0056 U	0.0048 U	0.0081 U	0.0046 U	0.0075 U
Acetone	mg/kg	670,000	N/A	N/A	0.05	0.0094 U	0.012 U	0.01 U	0.011 U	0.0085 U	0.011 U	0.0096 U	0.15	0.092	0.015 U
Benzene	mg/kg	5.1	N/A	N/A	0.0046 U	0.0047 U	0.0062 U	0.0071	0.0047 J	0.0073	0.011	0.0048 U	0.0081 U	0.0028 J	0.0075 U
Carbon disulfide	mg/kg	3,500	N/A	N/A	0.0046 U	0.0047 U	0.0062 U	0.0052 U	0.0055 U	0.0042 U	0.0056 U	0.0048 U	0.0081 U	0.0046 U	0.0075 U
Cyclohexane	mg/kg	27,000	N/A	N/A	0.0092 U	0.0094 U	0.012 U	0.01 U	0.011 U	0.0085 U	0.011 U	0.0096 U	0.016 U	0.0091 U	0.015 U
Ethylbenzene	mg/kg	25	N/A	N/A	0.0046 U	0.0047 U	0.0062 U	0.0052 U	0.0055 U	0.0042 U	0.0056 U	0.0048 U	0.0081 U	0.0046 U	0.0075 U
Isopropylbenzene	mg/kg	9,900	N/A	N/A	0.0046 U	0.0047 U	0.0062 U	0.0052 U	0.0055 U	0.0042 U	0.0056 U	0.0048 U	0.0081 U	0.0046 U	0.0075 U
Methyl Acetate	mg/kg	1,200,000	N/A	N/A	0.046 U	0.047 U	0.062 U	0.052 U	0.055 U	0.042 U	0.056 U	0.02 J	0.081 U	0.046 U	0.075 U
Methylene Chloride	mg/kg	1,000	N/A	N/A	0.0046 U	0.0047 U	0.017	0.0052 U	0.0055 U	0.0042 U	0.0056 U	0.0048 U	0.0081 U	0.0046 U	0.0075 U
Toluene	mg/kg	47,000	N/A	N/A	0.0046 U	0.0047 U	0.0062 U	0.0076	0.0022 J	0.0046	0.0056 U	0.0048 U	0.0081 U	0.0026 J	0.0075 U
Xylenes	mg/kg	2,800	N/A	N/A	0.014 U	0.014 U	0.018 U	0.016 U	0.017 U	0.013 U	0.017 U	0.014 U	0.024 U	0.014 U	0.022 U
Semi-Volatile Organic Compounds[^]															
1,1-Biphenyl	mg/kg	200	N/A	N/A	7 U	7.8 U	7.5 U	7.9 U	7.3 U	7.1 U	7.4 U	7.4 U	7.3 U	7.3 U	7.5 U
2,4-Dimethylphenol	mg/kg	16,000	N/A	N/A	7 U	7.8 U	7.5 U	7.9 U	7.3 U	7.1 U	7.4 U	7.4 U	7.3 U	7.3 U	7.5 U
2-Methylnaphthalene	mg/kg	3,000	N/A	N/A	0.14 U	0.011	0.15 U	0.88	0.0039 J	0.0097	0.0074 U	0.024	0.14 U	0.14 J	0.17
3&4-Methylphenol(m&p Cresol)	mg/kg	41,000	N/A	N/A	14 U	15.6 U	15 U	15.8 U	14.7 U	14.2 U	14.7 U	14.8 U	14.7 U	14.5 U	15 U
4-Chloroaniline	mg/kg	11	N/A	N/A	7 U	7.8 U	7.5 U	7.9 U	7.3 U	7.1 U	7.4 U	7.4 U	7.3 U	7.3 U	7.5 U
Acenaphthene	mg/kg	45,000	N/A	N/A	0.14 U	0.008 U	0.038 J	0.041 J	0.0031 J	0.0029 J	0.0074 U	0.0064 J	0.14 U	0.14 U	0.15 U
Acenaphthylene	mg/kg	45,000	N/A	N/A	0.061 J	0.002 J	0.22	0.25	0.00082 J	0.00098 J	0.0074 U	0.014	0.14 U	0.026 J	0.028 J
Acetophenone	mg/kg	120,000	N/A	N/A	7 U	7.8 U	7.5 U	7.9 U	7.3 U	7.1 U	7.4 U	7.4 U	7.3 U	7.3 U	7.5 U
Anthracene	mg/kg	230,000	N/A	N/A	0.19	0.0048 J	0.068 J	0.11 J	0.0083	0.006 J	0.0074 U	0.034	0.14 U	0.041 J	0.028 J
Benz[a]anthracene	mg/kg	21	N/A	N/A	0.54	0.026	0.61	0.18	0.15	0.059	0.0074 U	0.1	0.36 U	0.11 J	0.15 U
Benzaldehyde	mg/kg	120,000	N/A	N/A	7 U	7.8 U	7.5 U	7.9 U	7.3 U	7.1 U	7.4 U	7.4 U	7.3 U	7.3 U	7.5 U
Benzo[a]pyrene	mg/kg	2.1	N/A	N/A	0.47	0.025	1.1	0.19	0.24	0.098	0.0074 U	0.073	0.037 J	0.29	0.21
Benzo[b]fluoranthene	mg/kg	21	N/A	N/A	1.2	0.054	1.3	0.4	0.64	0.27	0.0074 U	0.18	0.095 J	0.28	0.18
Benzo[g,h,i]perylene	mg/kg		N/A	N/A	0.37	0.023	1.2	0.21	0.13	0.056	0.0074 U	0.038	0.19 J	0.7	0.92
Benzo[k]fluoranthene	mg/kg	210	N/A	N/A	1.1	0.052	0.6	0.4	0.53	0.27	0.0074 U	0.074	0.36 U	0.1 J	0.076 J
bis(2-Chloroethyl)ether	mg/kg	1	N/A	N/A	7 U	7.8 U	7.5 U	7.9 U	7.3 U	7.1 U	7.4 U	7.4 U	7.3 U	7.3 U	7.5 U
bis(2-Ethylhexyl)phthalate	mg/kg	160	N/A	N/A	7 U	7.8 U	7.5 U	7.9 U	7.3 U	7.1 U	7.4 U	7.4 U	7.3 U	7.3 U	7.5 U
Caprolactam	mg/kg	400,000	N/A	N/A	17.5 U	19.5 U	18.8 U	19.8 U	18.3 U	17.8 U	18.4 U	18.6 U	18.3 U	18.1 U	18.7 U
Carbazole	mg/kg		N/A	N/A	7 U	7.8 U	7.5 U	7.9 U	7.3 U	7.1 U	7.4 U	7.4 U	7.3 U	7.3 U	7.5 U
Chrysene	mg/kg	2,100	N/A	N/A	0.69	0.029	0.64	0.18	0.24	0.11	0.0074 U	0.13	0.69	0.24	1.5
Dibenz[a,h]anthracene	mg/kg	2.1	N/A	N/A	0.091 J	0.0059 J	0.23	0.16 U	0.055	0.015	0.0074 U	0.016	0.36 U	0.077 J	0.15 J
Di-n-butylphthalate	mg/kg	82,000	N/A	N/A	7 U	7.8 U	7.5 U	7.9 U	7.3 U	7.1 U	7.4 U	7.4 U	7.3 U	7.3 U	7.5 U
Di-n-octylphthalate	mg/kg	8,200	N/A	N/A	7 U	7.8 U	7.5 U	7.9 U	7.3 U	7.1 U	7.4 U	7.4 U	7.3 U	7.3 U	7.5 U
Fluoranthene	mg/kg	30,000	N/A	N/A	0.73	0.037	0.51	0.18	0.24	0.097	0.0074 U	0.18	0.035 J	0.14 J	0.055 J
Fluorene	mg/kg	30,000	N/A	N/A	0.14 U	0.008 U	0.014 J	0.17	0.002 J	0.0024 J	0.0074 U	0.0076	0.019 J	0.022 J	0.02 J
Hexachloroethane	mg/kg	8	N/A	N/A	7 U	7.8 U	7.5 U	7.9 U	7.3 U	7.1 U	7.4 U	7.4 U	7.3 U	7.3 U	7.5 U
Indeno[1,2,3-c,d]pyrene	mg/kg	21	N/A	N/A	0.27	0.016	0.76	0.17	0.13	0.035	0.0074 U	0.039	0.36 U	0.11 J	0.034 J
Isophorone	mg/kg	2,400	N/A	N/A	7 U	7.8 U	7.5 U	7.9 U	7.3 U	7.1 U	7.4 U	7.4 U	7.3 U	7.3 U	7.5 U
Naphthalene	mg/kg	17	N/A	N/A	0.12 J	0.1	0.33	13.1	0.014	0.016	0.0074 U	0.034	0.072 B	0.12 B	0.13 B
Nitrobenzene	mg/kg	22	N/A	N/A	7 U	7.8 U	7.5 U	7.9 U	7.3 U	7.1 U	7.4 U	7.4 U	7.3 U	7.3 U	7.5 U
Phenanthrene	mg/kg		N/A	N/A	0.083 J	0.024	0.17	0.36	0.056	0.038	0.0074 U	0.077	0.037 J	0.12 J	0.068 J
Phenol	mg/kg	250,000	N/A	N/A	7 U	7.8 U	7.5 U	7.9 U	7.3 U	7.1 U	7.4 U	7.4 U	7.3 U	7.3 U	7.5 U
Pyrene	mg/kg	23,000	N/A	N/A	0.96	0.034	0.54	0.17	0.26	0.098	0.0074 U	0.28	0.12 J	0.18	0.15 J
PCBs															
Aroclor 1260	mg/kg	0.99	N/A	N/A	0.18 U	N/A	0.19 U	N/A	0.018 U	0.018 U	N/A	0.2	N/A	0.046 J	N/A
PCBs (total)	mg/kg	0.97	N/A	N/A	1.2 U	N/A	1.3 U	N/A	0.13 U	0.12 U	N/A	0.2	N/A	2.5 U	N/A
TPH/Oil and Grease															
Diesel Range Organics	mg/kg	6,200	N/A	N/A	158	22.5	153	222	29.8	35.6	7.3 U	58.5	2,100	172	1,540
Gasoline Range Organics	mg/kg	6,200	N/A	N/A	11.9 U	12.1 U	5 U	12.2 U	9.6 J	9.5 U	11 U	9.8 U	21.3 U	12.1 U	16.4 U
Oil and Grease	mg/kg	6,200	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A

Detections in bold

Values in red indicate an exceedance of the Project Action Limit (PAL)

N/A indicates that the parameter was not analyzed for this sample.

[^]PAH compounds were analyzed via SIM

*indicates non-validated data

Locations B5-035-SB and B5-036-SB were not sampled due to shallow refusals.

U: This analyte was not detected in the sample. The numeric value represents the sample quantitation/detection limit.

UJ: This analyte was not detected in the sample. The actual quantitation/detection limit may be higher than reported.

J: The positive result reported for this analyte is a quantitative estimate.

J-: The positive result reported for this analyte is a quantitative estimate but may be biased low.

B: This analyte was not detected substantially above the level of the associated method blank/preparation or field blank.

R: The result for this analyte is unreliable. Additional data is needed to confirm or disprove the presence of this analyte in the sample.

Sub-Parcel B2-2
Summary of Inorganics Detected in Soil (NAPL Screening Locations)

Parameter	Units	PAL	B2-020-SB-1	B2-020-SB-4	B2-021-SB-1	B2-021-SB-4	B2-022-SB-1	B2-022-SB-4	B2-028-SB-1
Metals									
Aluminum	mg/kg	1,100,000	13,300	11,500	10,800	16,700	13,800	26,200	19,500
Arsenic	mg/kg	3	4.4 J	10.2 J	7.4 J	4.9 J	4.1 J	6.1 J	2.1
Barium	mg/kg	220,000	51.5	201	87.3	89	69.5	153	114
Beryllium	mg/kg	2,300	0.4 B	0.89	0.7 B	0.74 B	0.66	1.1	1.1
Cadmium	mg/kg	980	1.6 U	0.49 J	1 J	1.3 U	0.99 U	1.4 U	1.3 U
Chromium	mg/kg	120,000	28.9	1,600	126	33.1	34.5	1,170	897 J
Chromium VI	mg/kg	6.3	0.61 B	0.64 B	0.54 B	0.64 B	0.45 B	0.59 B	2.6 J-
Cobalt	mg/kg	350	3.8 J	42.6	10.3	8.1	4.7	26.4	2.5 J
Copper	mg/kg	47,000	15.7	204	64.2	17.6	21.2	135	23.9 J
Iron	mg/kg	820,000	18,700	140,000	50,900	21,200	19,000	89,100	164,000 J
Lead	mg/kg	800	18.2	259	146	72.4	40	112	6.6 J
Manganese	mg/kg	26,000	155	14,800	2,190	281	307	9,480	23,400
Mercury	mg/kg	350	0.02 J	0.059 J	0.068 J	0.29	0.038 J	0.023 J	0.093 U
Nickel	mg/kg	22,000	10.7 J	244 J	31.7 J	17.2 J	11.1 J	145 J	17.9 J
Selenium	mg/kg	5,800	4.1 U	3.2 U	4.4 U	3.4 U	2.6 U	3.7 U	3.4 U
Silver	mg/kg	5,800	2.3 J	15.3 J	4.3 J	3.5 J	1.1 J	14 J	23.5
Vanadium	mg/kg	5,800	34.3	368	129	36.5	40.2	152	493
Zinc	mg/kg	350,000	59.6	204	368	107	107	99.5	100 J
Other									
Cyanide	mg/kg	150	1.1 U	0.77 J	0.39 J	1.1 U	0.56 J	0.78 J	0.14 J-

Detections in bold

Values in red indicate an exceedance of the Project Action Limit (PAL)

N/A indicates that the parameter was not analyzed for this sample

*indicates non-validated data

Locations B5-035-SB and B5-036-SB were not sampled due to shallow refusals.

U: This analyte was not detected in the sample. The numeric value represents the sample quantitation/detection limit.

UJ: This analyte was not detected in the sample. The actual quantitation/detection limit may be higher than reported.

J: The positive result reported for this analyte is a quantitative estimate.

J+: The positive result reported for this analyte is a quantitative estimate but may be biased high.

J-: The positive result reported for this analyte is a quantitative estimate but may be biased low.

B: This analyte was not detected substantially above the level of the associated method blank/preparation or field blank.

Sub-Parcel B2-2
Summary of Inorganics Detected in Soil (NAPL Screening Locations)

Parameter	Units	PAL	B2-028-SB-5	B2-028-SB-10	B2-049-SB-1	B2-049-SB-4	B2-049-SB-10	B2-053-SB-1	B2-053-SB-5.5
Metals									
Aluminum	mg/kg	1,100,000	61,100	N/A	24,200	13,200	N/A	14,800	23,100
Arsenic	mg/kg	3	3.4	19.1 J	2.8	5	13.8 J	8	3.2
Barium	mg/kg	220,000	933	N/A	184	36.3	N/A	145 J	63 J
Beryllium	mg/kg	2,300	5.2	N/A	2.6	0.87 U	N/A	0.81 J	0.5 J
Cadmium	mg/kg	980	0.58 J	N/A	0.38 J	0.48 J	N/A	1.3 U	1.4 U
Chromium	mg/kg	120,000	30.8 J	30.4	680 J	1,390 J	N/A	288	24.8
Chromium VI	mg/kg	6.3	0.72 B	0.91 B	2.2 J-	8.5 J-	1 B	0.57 B	0.88 B
Cobalt	mg/kg	350	3 J	N/A	2 J	1.4 J	N/A	15.3	2.7 J
Copper	mg/kg	47,000	13.8 J	N/A	23.3 J	15.7 J	N/A	43.6 J	11.9 J
Iron	mg/kg	820,000	14,400 J	N/A	129,000 J	207,000 J	N/A	26,300	15,500
Lead	mg/kg	800	35.2 J	N/A	3.5 J	2.2 UJ	N/A	135	12.4
Manganese	mg/kg	26,000	8,400	272 J	16,500	33,900	N/A	4,350 J	76.8 J
Mercury	mg/kg	350	0.045 J	N/A	0.097 U	0.096 U	N/A	0.036 J	0.036 J
Nickel	mg/kg	22,000	9.5 J	N/A	14.2 J	19.2 J	N/A	121	10.6
Selenium	mg/kg	5,800	3.6 U	N/A	3.2 U	3.5 U	N/A	1.7 B	3.6 U
Silver	mg/kg	5,800	22.8	N/A	16.6	25.1	N/A	5.6	2.1 J
Vanadium	mg/kg	5,800	75.4	N/A	416	563	N/A	27.8	29.3
Zinc	mg/kg	350,000	70.3 J	N/A	48 J	13.7 J	N/A	152	18.6
Other									
Cyanide	mg/kg	150	0.48 J-	N/A	0.11 J-	0.089 J-	N/A	1.3 J+	1.1 U

Detections in bold

Values in red indicate an exceedance of the Project Action Limit (PAL)

N/A indicates that the parameter was not analyzed for this sample

*indicates non-validated data

Locations B5-035-SB and B5-036-SB were not sampled due to shallow refusals.

U: This analyte was not detected in the sample. The numeric value represents the sample quantitation/detection limit.

UJ: This analyte was not detected in the sample. The actual quantitation/detection limit may be higher than reported.

J: The positive result reported for this analyte is a quantitative estimate.

J+: The positive result reported for this analyte is a quantitative estimate but may be biased high.

J-: The positive result reported for this analyte is a quantitative estimate but may be biased low.

B: This analyte was not detected substantially above the level of the associated method blank/preparation or field blank.

Sub-Parcel B2-2
Summary of Inorganics Detected in Soil (NAPL Screening Locations)

Parameter	Units	PAL	B2-054-SB-1	B2-054-SB-5	B2-055-SB-1	B2-055-SB-6.5	B2-064-SB-1	B2-064-SB-5	B2-065-SB-1*
Metals									
Aluminum	mg/kg	1,100,000	44,500	15,100	49,000	14,600	17,300	7,860	10,600
Arsenic	mg/kg	3	2.6	3.4	2.2 J	2.4 U	2.1 U	5.8	2.6 U
Barium	mg/kg	220,000	259 J	37.6 J	408 J	62.7 J	193	75.3	56.2
Beryllium	mg/kg	2,300	2.8	0.5 J	8	0.76 J	1.9	0.47 J	0.31 J
Cadmium	mg/kg	980	1.4 U	1.6 U	1.4 U	1.5 U	1.3 U	1.4 U	1.5 U
Chromium	mg/kg	120,000	6.3	23.1	53.7	15.9	875	775	695
Chromium VI	mg/kg	6.3	0.65 B	0.44 B	0.49 B	0.54 B	2.5	1.2 U	12.5
Cobalt	mg/kg	350	0.79 J	4.3 J	0.86 J	4 J	0.93 J	6.8	0.86 J
Copper	mg/kg	47,000	37 J	9.2 J	7.4 J	5.6 J	19 J	43 J	21.4
Iron	mg/kg	820,000	6,960	23,600	10,700	8,800	141,000 J	149,000 J	83,200
Lead	mg/kg	800	5.4	8.6	22.4	8.9	7.4	48.2	29.1
Manganese	mg/kg	26,000	1,010 J	101 J	3,970 J	217 J	21,100	15,400	14,400
Mercury	mg/kg	350	0.019 J	0.019 J	0.11 U	0.025 J	0.099 U	0.019 J	0.06 J
Nickel	mg/kg	22,000	1.8 J	12.5	4.1 J	8.9 J	10.8 J	26.9 J	7.5 J
Selenium	mg/kg	5,800	6.2	2.7 B	3.2 B	3.9 U	3.4 U	3.6 U	4.1 U
Silver	mg/kg	5,800	11.9	3.7	9.4	1.7 J	2.5 J	1.7 J	3.1 U
Vanadium	mg/kg	5,800	7.3	32.3	20.9	17.8	405	335	594
Zinc	mg/kg	350,000	15.3	32.5	53.9	24.3	35.9	140	257
Other									
Cyanide	mg/kg	150	3.1 J+	1.3 U	1.7 J+	0.13 J+	0.32 J	0.29 J	0.36 J

Detections in bold

Values in red indicate an exceedance of the Project Action Limit (PAL)

N/A indicates that the parameter was not analyzed for this sample

*indicates non-validated data

Locations B5-035-SB and B5-036-SB were not sampled due to shallow refusals.

U: This analyte was not detected in the sample. The numeric value represents the sample quantitation/detection limit.

UJ: This analyte was not detected in the sample. The actual quantitation/detection limit may be higher than reported.

J: The positive result reported for this analyte is a quantitative estimate.

J+: The positive result reported for this analyte is a quantitative estimate but may be biased high.

J-: The positive result reported for this analyte is a quantitative estimate but may be biased low.

B: This analyte was not detected substantially above the level of the associated method blank/preparation or field blank.

Sub-Parcel B2-2
Summary of Inorganics Detected in Soil (NAPL Screening Locations)

Parameter	Units	PAL	B2-065-SB-4.5*	B2-069-SB-1	B2-069-SB-4	B5-032-SB-1*	B5-032-SB-5*	B5-035-SB [#]	B5-036-SB [#]
Metals									
Aluminum	mg/kg	1,100,000	38,800	8,060	16,300	9,830	30,800	N/A	N/A
Arsenic	mg/kg	3	2.2 J	2.1 U	2.6	11.7	4.4	N/A	N/A
Barium	mg/kg	220,000	1,700	45.8	126	118	227	N/A	N/A
Beryllium	mg/kg	2,300	2.9	0.15 J	1.9	0.9 J	5.1	N/A	N/A
Cadmium	mg/kg	980	1.4 U	1.3 U	1.3 U	1.9	1.3	N/A	N/A
Chromium	mg/kg	120,000	35	1,290	1,050	204	98.4	N/A	N/A
Chromium VI	mg/kg	6.3	1.1 U	7.4	0.7 J	1.1 U	0.27 J	N/A	N/A
Cobalt	mg/kg	350	1.2 J	1.2 J	2.2 J	15.4	2.9 J	N/A	N/A
Copper	mg/kg	47,000	10.2	17.1 J	27.3 J	88.5	19.6	N/A	N/A
Iron	mg/kg	820,000	8,940	174,000 J	138,000 J	232,000	23,500	N/A	N/A
Lead	mg/kg	800	8	7.5	11	189	95.6	N/A	N/A
Manganese	mg/kg	26,000	5,910	31,300	23,800	2,730	4,350	N/A	N/A
Mercury	mg/kg	350	0.12 U	0.11 U	0.11 U	0.074 J	0.11 U	N/A	N/A
Nickel	mg/kg	22,000	1.9 J	17.1 J	22.6 J	162	17.8	N/A	N/A
Selenium	mg/kg	5,800	3.6 U	3.4 U	3.5 U	4.2 U	2.3 J	N/A	N/A
Silver	mg/kg	5,800	2.7 U	3.9	2.7	2.6 J	2.2 U	N/A	N/A
Vanadium	mg/kg	5,800	212	537	554	54.6	77.2	N/A	N/A
Zinc	mg/kg	350,000	31.3	42.5	47.4	1,100	941	N/A	N/A
Other									
Cyanide	mg/kg	150	1.1 J	0.19 J	0.18 J	43.3	9.1	N/A	N/A

Detections in bold

Values in red indicate an exceedance of the Project Action Limit (PAL)

N/A indicates that the parameter was not analyzed for this sample

*indicates non-validated data

[#] Locations B5-035-SB and B5-036-SB were not sampled due to shallow refusals.

U: This analyte was not detected in the sample. The numeric value represents the sample quantitation/detection limit.

UJ: This analyte was not detected in the sample. The actual quantitation/detection limit may be higher than reported.

J: The positive result reported for this analyte is a quantitative estimate.

J+: The positive result reported for this analyte is a quantitative estimate but may be biased high.

J-: The positive result reported for this analyte is a quantitative estimate but may be biased low.

B: This analyte was not detected substantially above the level of the associated method blank/preparation or field blank.

Sub-Parcel B2-2
Summary of Inorganics Detected in Soil (NAPL Screening Locations)

Parameter	Units	PAL	B5-037-SB-1*	B5-037-SB-5*	B5-038-SB-1*	B5-038-SB-5*	B5-038-SB-10*	B5-086-SB-1*	B5-087-SB-1*
Metals									
Aluminum	mg/kg	1,100,000	22,900	4,020	39,000	8,560	N/A	29,900	31,800
Arsenic	mg/kg	3	2.1 U	2 U	2 U	2 U	N/A	3.6	2.4
Barium	mg/kg	220,000	605	92.7	404	114	N/A	242	336
Beryllium	mg/kg	2,300	3.4	0.79 U	6.2	0.71 J	N/A	3.7	5.5
Cadmium	mg/kg	980	0.31 J	0.46 J	0.36 J	0.47 B	N/A	0.34 J	0.31 J
Chromium	mg/kg	120,000	38.5	1,100	93.6	1,300	N/A	74	36.4
Chromium VI	mg/kg	6.3	0.17 J	0.19 J	0.22 J	0.28 J	N/A	1.1 U	1.1 U
Cobalt	mg/kg	350	1.2 J	4 U	2 J	0.88 J	N/A	4.7 J	1.4 J
Copper	mg/kg	47,000	6.7	15.9	6.1	35.4	N/A	44.9	13.7
Iron	mg/kg	820,000	26,300	208,000	21,000	175,000	N/A	99,900	49,900
Lead	mg/kg	800	5.9	2 U	12.6	25.1	N/A	2.6 U	5
Manganese	mg/kg	26,000	2,130	35,300	2,930	21,600	N/A	2,260	2,870
Mercury	mg/kg	350	0.11 U	0.12 U	0.1 U	0.42	N/A	0.003 J	0.1 U
Nickel	mg/kg	22,000	5.5 J	9.6	4.3 J	20.2	N/A	38.7	11.7
Selenium	mg/kg	5,800	3.4 U	3.2 U	2.7 J	3.2 U	N/A	4.1 U	3 U
Silver	mg/kg	5,800	2.5 U	1.4 J	2.5 U	2.4 U	N/A	3.1 U	2.2 U
Vanadium	mg/kg	5,800	31	1,870	59.8	1,470	N/A	29.9	22.8
Zinc	mg/kg	350,000	32.9	164	90	136	N/A	112	78.4
Other									
Cyanide	mg/kg	150	1.5 J	71.3	12.9	296	4.8	34.3	17.3

Detections in bold

Values in red indicate an exceedance of the Project Action Limit (PAL)

N/A indicates that the parameter was not analyzed for this sample

*indicates non-validated data

Locations B5-035-SB and B5-036-SB were not sampled due to shallow refusals.

U: This analyte was not detected in the sample. The numeric value represents the sample quantitation/detection limit.

UJ: This analyte was not detected in the sample. The actual quantitation/detection limit may be higher than reported.

J: The positive result reported for this analyte is a quantitative estimate.

J+: The positive result reported for this analyte is a quantitative estimate but may be biased high.

J-: The positive result reported for this analyte is a quantitative estimate but may be biased low.

B: This analyte was not detected substantially above the level of the associated method blank/preparation or field blank.

Sub-Parcel B2-2
Summary of Inorganics Detected in Soil (NAPL Screening Locations)

Parameter	Units	PAL	B5-087-SB-5*	B5-096-SB-1*	B5-096-SB-5*	B5-097-SB-1*	B5-097-SB-4*
Metals							
Aluminum	mg/kg	1,100,000	38,500	15,800	18,200	28,400	27,700
Arsenic	mg/kg	3	1.8 J	5.3	13.4	11.2	7
Barium	mg/kg	220,000	354	133	422	259	620
Beryllium	mg/kg	2,300	6.1	0.85 J	2.6	4.3	3.9
Cadmium	mg/kg	980	0.2 J	4.7	9.2	4.1	2.6
Chromium	mg/kg	120,000	32	217	124	112	32.4
Chromium VI	mg/kg	6.3	0.4 J	0.45 J	2.1	0.17 J	2.5
Cobalt	mg/kg	350	1.6 J	7	11.4	9.4	4.8
Copper	mg/kg	47,000	8.4	85.8	109	64.8	55.4
Iron	mg/kg	820,000	45,900	82,200	86,900	73,000	31,000
Lead	mg/kg	800	1.9 U	176	475	256	128
Manganese	mg/kg	26,000	3,500	6,070	4,220	4,010	3,510
Mercury	mg/kg	350	0.1 U	0.064 J	0.0036 J	0.022 J	0.11 U
Nickel	mg/kg	22,000	13.6	54.2	36.8	23.7	7.7 J
Selenium	mg/kg	5,800	1.8 J	3.8 U	3.2 U	2 J	2.4 J
Silver	mg/kg	5,800	2.3 U	1.9 J	1.8 J	0.66 J	2.5 U
Vanadium	mg/kg	5,800	13.8	93.6	118	120	52.9
Zinc	mg/kg	350,000	2.7 B	3,500	2,880	1,520	801
Other							
Cyanide	mg/kg	150	24.5	0.46 J	0.057 J	1.2	0.077 J

Detections in bold

Values in red indicate an exceedance of the Project Action Limit (PAL)

N/A indicates that the parameter was not analyzed for this sample

*indicates non-validated data

Locations B5-035-SB and B5-036-SB were not sampled due to shallow refusals.

U: This analyte was not detected in the sample. The numeric value represents the sample quantitation/detection limit.

UJ: This analyte was not detected in the sample. The actual quantitation/detection limit may be higher than reported.

J: The positive result reported for this analyte is a quantitative estimate.

J+: The positive result reported for this analyte is a quantitative estimate but may be biased high.

J-: The positive result reported for this analyte is a quantitative estimate but may be biased low.

B: This analyte was not detected substantially above the level of the associated method blank/preparation or field blank.

APPENDIX C



ARM Group Inc.
Earth Resource Engineers
and Consultants

Client : EnviroAnalytics Group
 ARM Project No. : 150300M-6-3
 Project Description : Sparrows Point - Parcel B2
 Site Location : Sparrows Point, MD
 ARM Representative : L. Perrin
 Checked by : M. Replogle, E.I.T.
 Drilling Company : Allied Drilling Co.
 Driller : Rick Miller
 Drilling Equipment : Geoprobe 7822DT

Soil Boring Installation Date : 05/31/2017
 Piezometer Installation Date : 11/03/2017
 Casing/Riser/Screen Type : PVC
 Borehole Diameter : 2.25"
 Riser/Screen Diameter : 1"
 Northing (US ft) : 566,214.08
 Easting (US ft) : 1,460,099.15
 0-Hr DTW : 5.99' TOC
 48-Hr DTW : 5.69' TOC
 No LNAPL or DNAPL detected at 0 or 48 hours

Boring ID: B2-024-SB/PZ

(page 1 of 1)

Depth (ft.)	% Recovery	PID Reading (PPM)	Sample No/Interval	DESCRIPTION	USCS	REMARKS
0	-	-	B2-024-SB-1	(0-0.2') ASPHALT, hard, black, dry, no plasticity, no cohesion	NA	Piezometer installed after receipt of soil boring analytical results Wet at 3.8' bgs
	-	-		(0.2-2.5') Non-native GRAVELLY SAND, brown, dry, no plasticity, no cohesion	SW/GW	
76	4.3			(2.5-3.4') SLAG, SAND and GRAVEL-sized, medium dense to dense, light gray and gray, dry, no plasticity, no cohesion	SW/GW	
	2.6			(3.4-3.8') SANDY SILT with some GRAVEL, soft to firm, brown and strong brown, moist, low plasticity, cohesive	ML	
5	0.2			(3.8-7') SANDY GRAVEL, medium dense, reddish yellow and strong brown, wet, no plasticity, no cohesion	GW/SW	
	-			(7-7.2') CLAY, soft, red, moist, medium plasticity, cohesive	CL	
80	-			(7.2-8.1') SILTY SAND, very fine to medium grained, medium dense, dark brownish gray, wet, no plasticity, no cohesion	SM	
	-			(8.1-10') GRAVEL with SILT, medium dense, dark brownish gray with trace reddish yellow and pale brown, wet, no plasticity, no cohesion	GW-GM	
10	-			Piezometer installation later date: (10-15') No Recovery		
15	-			End of boring		

Boring terminated at 15' bgs due to water and piezo installation.

TOC: Top of PVC casing
 DTW: Depth to water
 bgs: Below ground surface
 AMSL: Above mean sea level

Riser Stickup: 3.63'
 Riser: 0 - 3' bgs
 Screen: 3 - 12' bgs [Slot Size: 0.010"]
 Sand Pack: 2 - 12' bgs [Grain Size: WG #2]
 Bentonite Seal: 0 - 2' bgs [Grain Size: 3/8" chips]



ARM Group Inc.
Earth Resource Engineers
and Consultants

Client : EnviroAnalytics Group
 ARM Project No. : 150300M-6-3
 Project Description : Sparrows Point - Parcel B2
 Site Location : Sparrows Point, MD
 ARM Representative : L. Perrin
 Checked by : M. Replogle, E.I.T.
 Drilling Company : Allied Drilling Co.
 Driller : Rick Miller
 Drilling Equipment : Geoprobe 7822DT

Soil Boring Installation Date : 06/22/2017
 Piezometer Installation Date : 06/22/2017
 Casing/Riser/Screen Type : PVC
 Borehole Diameter : 2.25"
 Riser/Screen Diameter : 1"
 Northing (US ft) : 568,050.85
 Easting (US ft) : 1,460,179.34
 0-Hr DTW : 8.49' TOC
 48-Hr DTW : 8.59' TOC
 No LNAPL or DNAPL detected at 0 or 48 hours

Boring ID: B2-051-SB/PZ

(page 1 of 1)

Depth (ft.)	% Recovery	PID Reading (PPM)	Sample No/Interval	DESCRIPTION	USCS	REMARKS
0	-	-	B2-051-SB-1	(0-5.5') GRAVELLY SAND with SILT and SLAG GRAVEL, medium dense, light gray and brown, dry, non plastic, non cohesive	SW/GW	<p>Bentonite seal 1" PVC Riser Sand Pack 1" PVC Screen</p>
0.4	90	0.4				
0.4		0.0				
0.0		0.0				
0.0		0.0	B2-051-SB-5			
0.0		0.0		(5.5-8') SANDY GRAVEL with SLAG and BRICK, medium dense, dark brown, with trace yellow, wet, non plastic, non cohesive	SW/GW	
0.0	90	0.0				
0.0		0.0		(8-12') SLAG with CEMENT, medium dense, light gray and white, wet, non plastic, non cohesive	GW/GM	
0.0		0.0				
0.0		0.0				
10	66	-		(12-13) SILT, soft, dark gray, very moist, low plasticity, cohesive	ML	
15				End of boring		Wet at 6' bgs Trace to light tar with solvent odor from 6-6.2' bgs

Boring terminated at 13' bgs due to water and piezometer installation.
 TOC: Top of PVC casing
 DTW: Depth to water
 bgs: Below ground surface
 AMSL: Above mean sea level

Riser Stickup: 2.60'
 Riser: 0-3' bgs
 Screen: 3-13' bgs [Slot Size: 0.010"]
 Sand Pack: 2-13' bgs [Grain Size: WG #2]
 Bentonite Seal: 0 - 2' bgs [Grain Size: granular (30-50 mesh)]




Client : EnviroAnalytics Group
 ARM Project No. : 150300M-6-3
 Project Description : Sparrows Point - Parcel B2
 Site Location : Sparrows Point, MD
 ARM Representative : L. Perrin
 Checked by : M. Replogle, E.I.T.
 Drilling Company : Allied Drilling Co.
 Driller : Rick Miller
 Drilling Equipment : Geoprobe 7822DT

Soil Boring Installation Date : 06/27/2017
 Piezometer Installation Date : 06/27/2017
 Casing/Riser/Screen Type : PVC
 Borehole Diameter : 2.25"
 Riser/Screen Diameter : 1"
 Northing (US ft) : 566,428.98
 Easting (US ft) : 1,460,658.92
 0-Hr DTW : 9.67' TOC
 48-Hr DTW : 6.90' TOC
 No LNAPL or DNAPL detected at 0 or 48 hours

Boring ID: B2-053-SB/PZ

(page 1 of 1)

Depth (ft.)	% Recovery	PID Reading (PPM)	Sample No/Interval	DESCRIPTION	USCS	REMARKS
0	-	-	B2-053-SB-1	(0-1.5') GRAVELLY SAND, loose, yellow, dry, non plastic, non cohesive	SW/GW	Light organic matter
42.6	-	-		(1.5-5.5') SILT and CLAYEY SILT, soft, gray, moist, low plasticity, cohesive	ML	
80	8.7	150.3				Fuel type odor, light from 3-5.5' bgs, moderate from 5.5-6.2' bgs
154.4	-	-	B2-053-SB-5.5			
5	241.8	876.6		(5.5-6.2') SAND with SILT, medium dense to dense, gray, wet, non plastic, non cohesive	SW/SM	Wet at 5.5' bgs
100	1111	1168		(6.2-13') CLAY, very firm, yellowish brown, reddish yellow and light grayish brown, moist, low plasticity, cohesive	CL	
100	-	-				
15	-	-		End of boring		

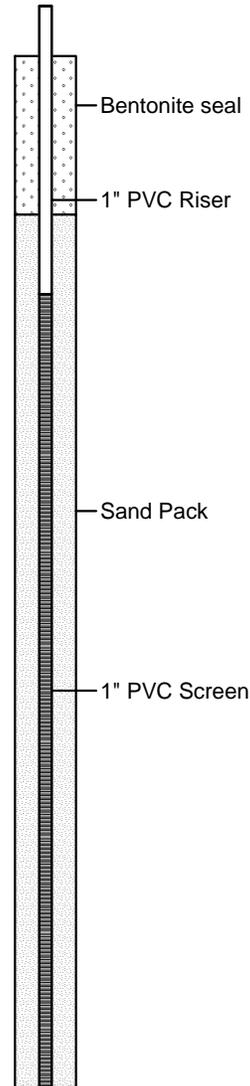

Boring terminated at 13' bgs due to water and piezometer installation.

TOC: Top of PVC casing
 DTW: Depth to water
 bgs: Below ground surface
 AMSL: Above mean sea level

Riser Stickup: 3.30'
 Riser: 0 - 3' bgs
 Screen: 3 - 13' bgs [Slot Size: 0.010"]
 Sand Pack: 2 - 13' bgs [Grain Size: WG #2]
 Bentonite Seal: 0 - 2' bgs [Grain Size: 3/8" chips]




Client : EnviroAnalytics Group
 ARM Project No. : 150300M-6-3
 Project Description : Sparrows Point - Parcel B2
 Site Location : Sparrows Point, MD
 ARM Representative : L. Perrin
 Checked by : M. Replogle, E.I.T.
 Drilling Company : Allied Drilling Co.
 Driller : Rick Miller
 Drilling Equipment : Geoprobe 7822DT

Soil Boring Installation Date : 06/27/2017
 Piezometer Installation Date : 06/27/2017
 Casing/Riser/Screen Type : PVC
 Borehole Diameter : 2.25"
 Riser/Screen Diameter : 1"
 Northing (US ft) : 566,459.61
 Easting (US ft) : 1,460,618.17
 0-Hr DTW : 7.13' TOC
 48-Hr DTW : 7.20' TOC
 No LNAPL or DNAPL detected at 0 or 48 hours

Boring ID: B2-055-SB/PZ

(page 1 of 1)

Depth (ft.)	% Recovery	PID Reading (PPM)	Sample No/Interval	DESCRIPTION	USCS	REMARKS
0	-	-	B2-055-SB-1	(0-0.7') ORGANIC SILT, soft, browning, dry, non plastic, non cohesive	OL	Heavy organic matter
20.5	-	-		(0.7-2.5') GRAVELLY SAND, medium dense, light brown, dry, non plastic, non cohesive	SW/GW	
74	44.5	-		(2.5-3.5') GRAVELLY SAND, medium dense, brown and dark brown, dry, non plastic, non cohesive	SW/GW	Very strong fuel type odor from 3.5-7.2' bgs
187.8	-	-		(3.4-5.7') SILTY CLAY, firm to soft, gray to brownish gray, low plasticity, cohesive	CL	
5	101.0	-				Wet at 6.5' bgs
13.9	-	-	B2-055-SB-6.5	(5.7-7.2') SILTY SAND grading to SAND, very firm, moist then wet at 6.5', non plastic, non cohesive	SM-SW	
96	648.5	-		(7.2-10') CLAY, hard, yellowish brown with yellowish red, dry to moist, low plasticity, cohesive	CL	
158.4	-	-				
82.1	-	-				
10	-	-		(10-14') No Recovery		
0	-	-				
-	-	-				
-	-	-				
15	-	-		End of boring		

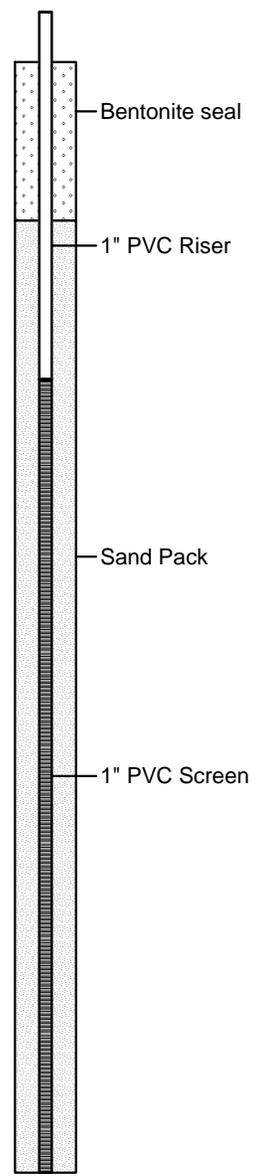

Boring terminated at 14' bgs due to water and piezometer installation.
 TOC: Top of PVC casing
 DTW: Depth to water
 bgs: Below ground surface
 AMSL: Above mean sea level

Riser Stickup: 3.55'
 Riser: 0 - 4' bgs
 Screen: 4 - 14' bgs [Slot Size: 0.010"]
 Sand Pack: 2 - 14' bgs [Grain Size: WG #2]
 Bentonite Seal: 0 - 2' bgs [Grain Size: 3/8" chips]

06-28-2018 P:\EnviroAnalytics Group\150300M EAG_Sparrows Point Area B\Documents\Parcel B2\BOR_PZ_logs\bor\B2-055-SB-PZ.bor



Client : EnviroAnalytics Group
 ARM Project No. : 150300M-3-3
 Project Description : Sparrows Point - Parcel B5
 Site Location : Sparrows Point, MD
 ARM Representative : L. Perrin
 Checked by : M. Replogle, E.I.T.
 Drilling Company : Green Services, Inc
 Driller : Kevin Pumphrey
 Drilling Equipment : Geoprobe 7822DT

Soil Boring Installation Date : 01/13/2016
 Piezometer Installation Date : 04/27/2017
 Casing/Riser/Screen Type : PVC
 Borehole Diameter : 2.25"
 Riser/Screen Diameter : 1"
 Northing (US ft) : 564,799.5701
 Easting (US ft) : 1,459,395.964
 0-Hr DTW : 7.02' TOC
 48-Hr DTW : 7.00' TOC
 No LNAPL or DNAPL detected at 0 or 48 hours

Boring ID: B5-097-SB/PZ

(page 1 of 1)

Depth (ft.)	% Recovery	PID Reading (PPM)	Sample No/Interval	DESCRIPTION	USCS	REMARKS
0	-	-	B5-097-SB-1	(0-4') SLAG, GRAVEL-sized with medium SAND, loose, gray, dry, no plasticity, no cohesion	GP	<p>Piezometer installed after receipt of soil boring analytical results</p> <p>Wet at 4' bgs 1-2 inch thick tar-like/sticky substance at 4.5' bgs</p>
60	2.7	-				
	3.3	-	B5-097-SB-4			
5	-	-		(4-5') SLAG, GRAVEL-sized, loose, dark brown, wet, sticky black substance with odor	GP	
	-	-		(5-6') SAND, light gray, wet, no plasticity, cohesive	SW	
	-	-		(6-7') SANDY CLAY, firm, very pale brown, medium plasticity, cohesive	CL	
100	-	-		(7-10') SANDY CLAY, with trace GRAVEL, light gray, wet, high plasticity, cohesive	CH	
	-	-				
10	-	-		Piezometer installation later date: (10-14') SLAG, GRAVEL-sized, very loose, brown (10-12'), dark gray (12-14'), wet, no plasticity, no cohesion	GP	
	-	-				
	-	-				
15	-	-		Piezometer installation later date: (14-15') CLAY, soft, brown, moist, high plasticity, cohesive	CL	
				End of boring		

Boring terminated at 15' bgs due to water and piezo installation.

TOC: Top of PVC casing
 DTW: Depth to water
 bgs: Below ground surface
 AMSL: Above mean sea level

Riser Stickup: 3.40'
 Riser: 0 - 5' bgs
 Screen: 5 - 15' bgs [Slot Size: 0.010"]
 Sand Pack: 3 - 15' bgs [Grain Size: WG #2]
 Bentonite Seal: 0 - 2' bgs [Grain Size: granular (30-50 mesh)]

APPENDIX D

**Construction Worker Soil Screening Levels
Maximum Allowable Work Day Exposure
Calculation Spreadsheet - Sub-Parcel B2-2**

Description	Variable	Value
Days worked per week	DW	5
Exposure duration (yr)	ED	1
Hours worked per day	ET	8
A/constant (unitless) - particulate emission factor	Aconst	12.9351
B/constant (unitless) - particulate emission factor	Bconst	5.7383
C/constant (unitless) - particulate emission factor	Cconst	71.7711
Dispersion correction factor (unitless)	FD	0.185
Days per year with at least .01" precipitation	P	130
Target hazard quotient (unitless)	THQ	1
Body weight (kg)	BW	80
Averaging time - noncancer (yr)	ATnc	1
Soil ingestion rate (mg/d)	IR	330
Skin-soil adherence factor (mg/cm ²)	AF	0.3
Skin surface exposed (cm ²)	SA	3300
Event frequency (ev/day)	EV	1
Target cancer risk (unitless)	TR	01E-06
Averaging time - cancer (yr)	ATc	70
A/constant (unitless) - volatilization	Aconstv	2.4538
B/constant (unitless) - volatilization	Bconstv	17.566
C/constant (unitless) - volatilization	Cconstv	189.0426
Dry soil bulk density (kg/L)	Pb	1.5
Average source depth (m)	ds	3
Soil particle density (g/cm ³)	Ps	2.65
Total soil porosity	Lpore/Lsoil	0.43
Air-filled soil porosity	Lair/Lsoil	0.28

**Construction Worker Soil Screening Levels
Maximum Allowable Work Day Exposure
Calculation Spreadsheet - Sub-Parcel B2-2**

Area of site (ac)	Ac	34.5
Overall duration of construction (wk/yr)	EW	19
Exposure frequency (day/yr)	EF	95
Cars per day	Ca	5
Tons per car	CaT	2
Trucks per day	Tru	5
Tons per truck	TrT	20
Mean vehicle weight (tons)	w	11
Derivation of dispersion factor - particulate emission factor (g/m ² -s per kg/m ³)	Q/Csr	13.8
Overall duration of construction (hr)	tc	3,192
Overall duration of traffic (s)	Tt	2,736,000
Surface area (m ²)	AR	139,617
Length (m)	LR	374
Distance traveled (km)	ΣVKT	355
Particulate emission factor (m ³ /kg)	PEFsc	133,695,692
Derivation of dispersion factor - volatilization (g/m ² -s per kg/m ³)	Q/Csa	6.95
Total time of construction (s)	Tcv	2,736,000

→ EU1

Input
Calculation

Chemical	RfD & RfC Sources	[^] Ingestion SF (mg/kg-day) ⁻¹	[^] Inhalation Unit Risk (ug/m ³) ⁻¹	[^] Subchronic RfD (mg/kg-day)	[^] Subchronic RfC (mg/m ³)	[^] GIABS	Dermally Adjusted RfD (mg/kg-day)	[^] ABS	[^] RBA	*Dia	*Diw	*Henry's Law Constant (unitless)	*Kd	*Koc	DA	Volatilization Factor - Unlimited Reservoir (m ³ /kg)	Carcinogenic Ingestion/ Dermal SL (SLing/der)	Carcinogenic Inhalation SL (SLinh)	Carcinogenic SL (mg/kg)	Non-Carcinogenic Ingestion/ Dermal SL (SLing/der)	Non-Carcinogenic Inhalation SL (SLinh)	Non-Carcinogenic SL (mg/kg)
Arsenic, Inorganic	I/C	1.50E+00	4.30E-03	3.00E-04	1.50E-05	1	3.00E-04	0.03	0.6			-	2.90E+01				39.9	25,086	39.8	256	23,115	254
Chromium(VI)	A/C/I	5.00E-01	8.40E-02	5.00E-03	3.00E-04	0.025	1.25E-04	0.01	1			-	1.90E+01				59.3	1,284	56.7	2,117	462,306	2,107
Cobalt	P	-	9.00E-03	3.00E-03	2.00E-05	1	3.00E-03	0.01	1			-	4.50E+01					11,986	11,986	2,713	30,820	2,493
Iron	P	-	-	7.00E-01	-	1	7.00E-01	0.01	1			-	2.50E+01							633,004		633,004
Manganese (Non-diet)	I	-	-	2.40E-02	5.00E-05	0.04	9.60E-04	0.01	1			-	6.50E+01							12,774	77,051	10,957
Vanadium and Compounds	A	-	-	1.00E-02	1.00E-04	0.026	2.60E-04	0.01	1			-	1.00E+03							4,324	154,102	4,206
Benzo[a]pyrene	I	1.00E+00	6.00E-04	3.00E-04	2.00E-06	1	3.00E-04	0.13	1	4.80E-02	5.60E-06	1.87E-05	3.54E+03	5.90E+05	2.37E-11	7.54E+5	46.9	1,008	44.8	201	17.3	15.9
Naphthalene	C/I/A	-	3.40E-05	6.00E-01	3.00E-03	1	6.00E-01	0.13	1	6.00E-02	8.40E-06	1.80E-02	9.00E+00	1.50E+03	6.35E-06	1.46E+3		34.5	34.5	402,052	50.3	50.3

*chemical specific parameters found in Chemical Specific Parameters Spreadsheet at <https://www.epa.gov/risk/regional-screening-levels-rsls>

[^]chemical specific parameters found in Unpaved Road Traffic calculator at https://epa-prgs.ornl.gov/cgi-bin/chemicals/csl_search

I: chemical specific parameters found in the IRIS at <https://www.epa.gov/iris>

C: chemical specific parameters found in Cal EPA at <https://www.dtsc.ca.gov/AssessingRisk>

A: chemical specific parameters found in Agency for Toxic Substances and Disease Registry Minimal Risk Levels (MRLs) at https://www.atsdr.cdc.gov/mrls/pdfs/atsdr_mrls.pdf

P: chemical specific parameters found in the Database of EPA PPRTVs at <https://hhpprtv.ornl.gov/quickview/pprtv.php>

**Construction Worker Soil Screening Levels
Maximum Allowable Work Day Exposure
Calculation Spreadsheet - Sub-Parcel B2-2**

Area of site (ac)	Ac	63.5
Overall duration of construction (wk/yr)	EW	11
Exposure frequency (day/yr)	EF	55
Cars per day	Ca	5
Tons per car	CaT	2
Trucks per day	Tru	5
Tons per truck	TrT	20
Mean vehicle weight (tons)	w	11
Derivation of dispersion factor - particulate emission factor (g/m2-s per kg/m3)	Q/Csr	13.4
Overall duration of construction (hr)	tc	1,848
Overall duration of traffic (s)	Tt	1,584,000
Surface area (m2)	AR	256,976
Length (m)	LR	507
Distance traveled (km)	ΣVKT	279
Particulate emission factor (m3/kg)	PEFsc	175,639,933
Derivation of dispersion factor - volatilization (g/m2-s per kg/m3)	Q/Csa	6.36
Total time of construction (s)	Tcv	1,584,000

→ EU2

Input
Calculation

Chemical	RfD & RfC Sources	[^] Ingestion SF (mg/kg-day) ⁻¹	[^] Inhalation Unit Risk (ug/m ³) ⁻¹	[^] Subchronic RfD (mg/kg-day)	[^] Subchronic RfC (mg/m ³)	[^] GIABS	Dermally Adjusted RfD (mg/kg-day)	[^] ABS	[^] RBA	*Dia	*Diw	*Henry's Law Constant (unitless)	*Kd	*Koc	DA	Volatilization Factor - Unlimited Reservoir (m ³ /kg)	Carcinogenic Ingestion/ Dermal SL (SLing/der)	Carcinogenic Inhalation SL (SLinh)	Carcinogenic SL (mg/kg)	Non-Carcinogenic Ingestion/ Dermal SL (SLing/der)	Non-Carcinogenic Inhalation SL (SLinh)	Non-Carcinogenic SL (mg/kg)
Arsenic, Inorganic	I/C	1.50E+00	4.30E-03	3.00E-04	1.50E-05	1	3.00E-04	0.03	0.6			-	2.90E+01				68.9	56,925	68.8	443	52,452	439
Chromium(VI)	A/C/I	5.00E-01	8.40E-02	5.00E-03	3.00E-04	0.025	1.25E-04	0.01	1			-	1.90E+01				102	2,914	98.9	3,656	1,049,049	3,644
Cobalt	P	-	9.00E-03	3.00E-03	2.00E-05	1	3.00E-03	0.01	1			-	4.50E+01					27,198	27,198	4,686	69,937	4,392
Iron	P	-	-	7.00E-01	-	1	7.00E-01	0.01	1			-	2.50E+01							1,093,370		1,093,370
Manganese (Non-diet)	I	-	-	2.40E-02	5.00E-05	0.04	9.60E-04	0.01	1			-	6.50E+01							22,064	174,842	19,591
Vanadium and Compounds	A	-	-	1.00E-02	1.00E-04	0.026	2.60E-04	0.01	1			-	1.00E+03							7,470	349,683	7,313
Benzo[a]pyrene	I	1.00E+00	6.00E-04	3.00E-04	2.00E-06	1	3.00E-04	0.13	1	4.80E-02	5.60E-06	1.87E-05	3.54E+03	5.90E+05	2.37E-11	5.25E+5	81.0	1,216	76.0	347	20.8	19.7
Naphthalene	C/I/A	-	3.40E-05	6.00E-01	3.00E-03	1	6.00E-01	0.13	1	6.00E-02	8.40E-06	1.80E-02	9.00E+00	1.50E+03	6.35E-06	1.01E+3		41.6	41.6	694,453	60.6	60.5

*chemical specific parameters found in Chemical Specific Parameters Spreadsheet at <https://www.epa.gov/risk/regional-screening-levels-rsls>

[^]chemical specific parameters found in Unpaved Road Traffic calculator at https://epa-prgs.ornl.gov/cgi-bin/chemicals/csl_search

I: chemical specific parameters found in the IRIS at <https://www.epa.gov/iris>

C: chemical specific parameters found in Cal EPA at <https://www.dtsc.ca.gov/AssessingRisk>

A: chemical specific parameters found in Agency for Toxic Substances and Disease Registry Minimal Risk Levels (MRLs) at https://www.atsdr.cdc.gov/mrls/pdfs/atsdr_mrls.pdf

P: chemical specific parameters found in the Database of EPA PPRTVs at <https://hhpprtv.ornl.gov/quickview/pprtv.php>

APPENDIX E

Sparrows Point Development - PPE Standard

Operational Procedure, Revision 3

Planning, Tracking/Supervision, Enforcement, and Documentation

Planning

- Response and Development Work Plan (RDWP) for each individual redevelopment sub-parcel identifies and documents site conditions.
- RDWP is reviewed and approved by regulators.
- Contractor HASP to address site-specific conditions and PPE requirements:
 - Contractor H&S professional to sign-off on PPE requirements for site workers;
 - Job Safety Analysis (JSA) to be performed for ground intrusive work.
- Project Environmental Professional (EP) assigned to each construction project – monitors project during environmentally sensitive project phases and is available to construction contractor on an as needed basis. EP responsibilities include the following:
 - Dust monitoring
 - Routine ground intrusive breathing space air monitoring
 - Soil tracking
 - Water handling oversight
 - Ground intrusive work observation
 - Notification for unexpected conditions
- Pre-construction meeting identifies EP roles and responsibilities and reviews site conditions.
- Contractor to perform job-site HazCom. HazCom to be addressed in Contractor HASP and include:
 - PPE requirements,
 - Exposure time limits,
 - Identification of chemicals of concern and potential effects of over-exposure (adverse reactions),
 - Methods and routes of potential exposure.
- All personnel that will be performing ground intrusive work within impacted soils shall sign-off on HazCom.
- If, based on a thorough review of Site conditions, it is expected that construction workers will have the potential to encounter materials considered hazardous waste under RCRA or DOT regulations, HAZWOPER-trained personnel will be utilized.

Tracking/Supervision

- Contractor to record any day that there is ground intrusive work and confirm that proper PPE is being worn.
- EP will note ground intrusive work on daily work sheets and perform at least one spot check per day.
- EP will log on daily work sheets PPE compliance for all intrusive work areas at least once per day.

- EP to take example photos of Exclusion Zones/Contamination Reduction Zones periodically.

Work Zones Delineation

- Exclusion Zone – The Exclusion Zones will include the areas proposed for excavation or with active trenches, excavations, or ground intrusive work, at a minimum. Personnel working within the exclusion zone will be required to wear Modified Level D PPE as described in this SOP. EP to take example photos of Exclusion Zones/Contamination Reduction Zones periodically. The Exclusion Zones will be identified each work day.
- Contamination Reduction Zone – This work zone is located outside of the exclusion zone, but inside of the limits of development (LOD). The Contamination Reduction Zone will be located adjacent to the Exclusion Zone, and all personal decontamination including removal of all disposable PPE/removal of soil from boots will be completed in the Contamination Reduction Zone.

Documentation

- Contractor HASP and HazCom.
- Contractor ground intrusive tracking record.
- HASP and HazCom sign-in sheets.
- EP pre-con memos.
- EP daily work sheets.
- Records documenting intrusive work and proper PPE use to be provided in completion report.

Enforcement

- Non-compliance of PPE requirements will result in disciplinary action up to and including prohibition from working on Sparrows Point.

Unknown and/or Unexpected Conditions

If unknown and/or unexpected conditions are encountered during the project that the EP determines to have a reasonable potential to significantly impact construction worker health and safety, the following will be initiated:

1. Job stoppage,
2. TPA and MDE notification,
3. Re-assessment of conditions.

Work will not continue until EP has cleared the area. If hazardous waste is identified, a HAZWOPER contractor will be brought in to address. The approved contingency plan will be implemented, where appropriate.



Modified Level D PPE

Modified Level D PPE will include, at a minimum, overalls such as polyethylene-coated Tyvek or clean washable cloth overalls, latex (or similar) disposable gloves (when working in wet/chemical surroundings) or work gloves, steel-toe/steel-shank high ankle work boots with taped chemical-protective over-boots (as necessary), dust mask, hard hat, safety glasses with

side shields, and hearing protection (as necessary). If chemical-protective over-boots create increased slip/trip/fall hazardous, then standard leather or rubber work boots could be used, but visible soils from the sides and bottoms of the boots must be removed upon exiting the Exclusion Zone.

SP Development PPE Procedure 4-3-19

APPENDIX F

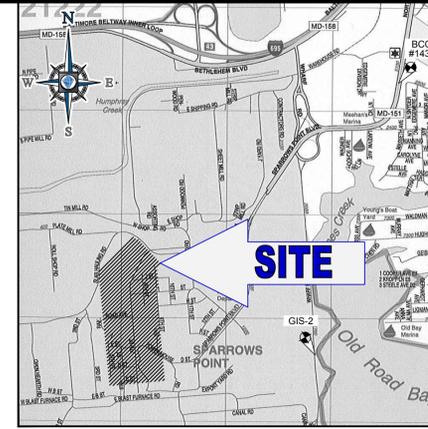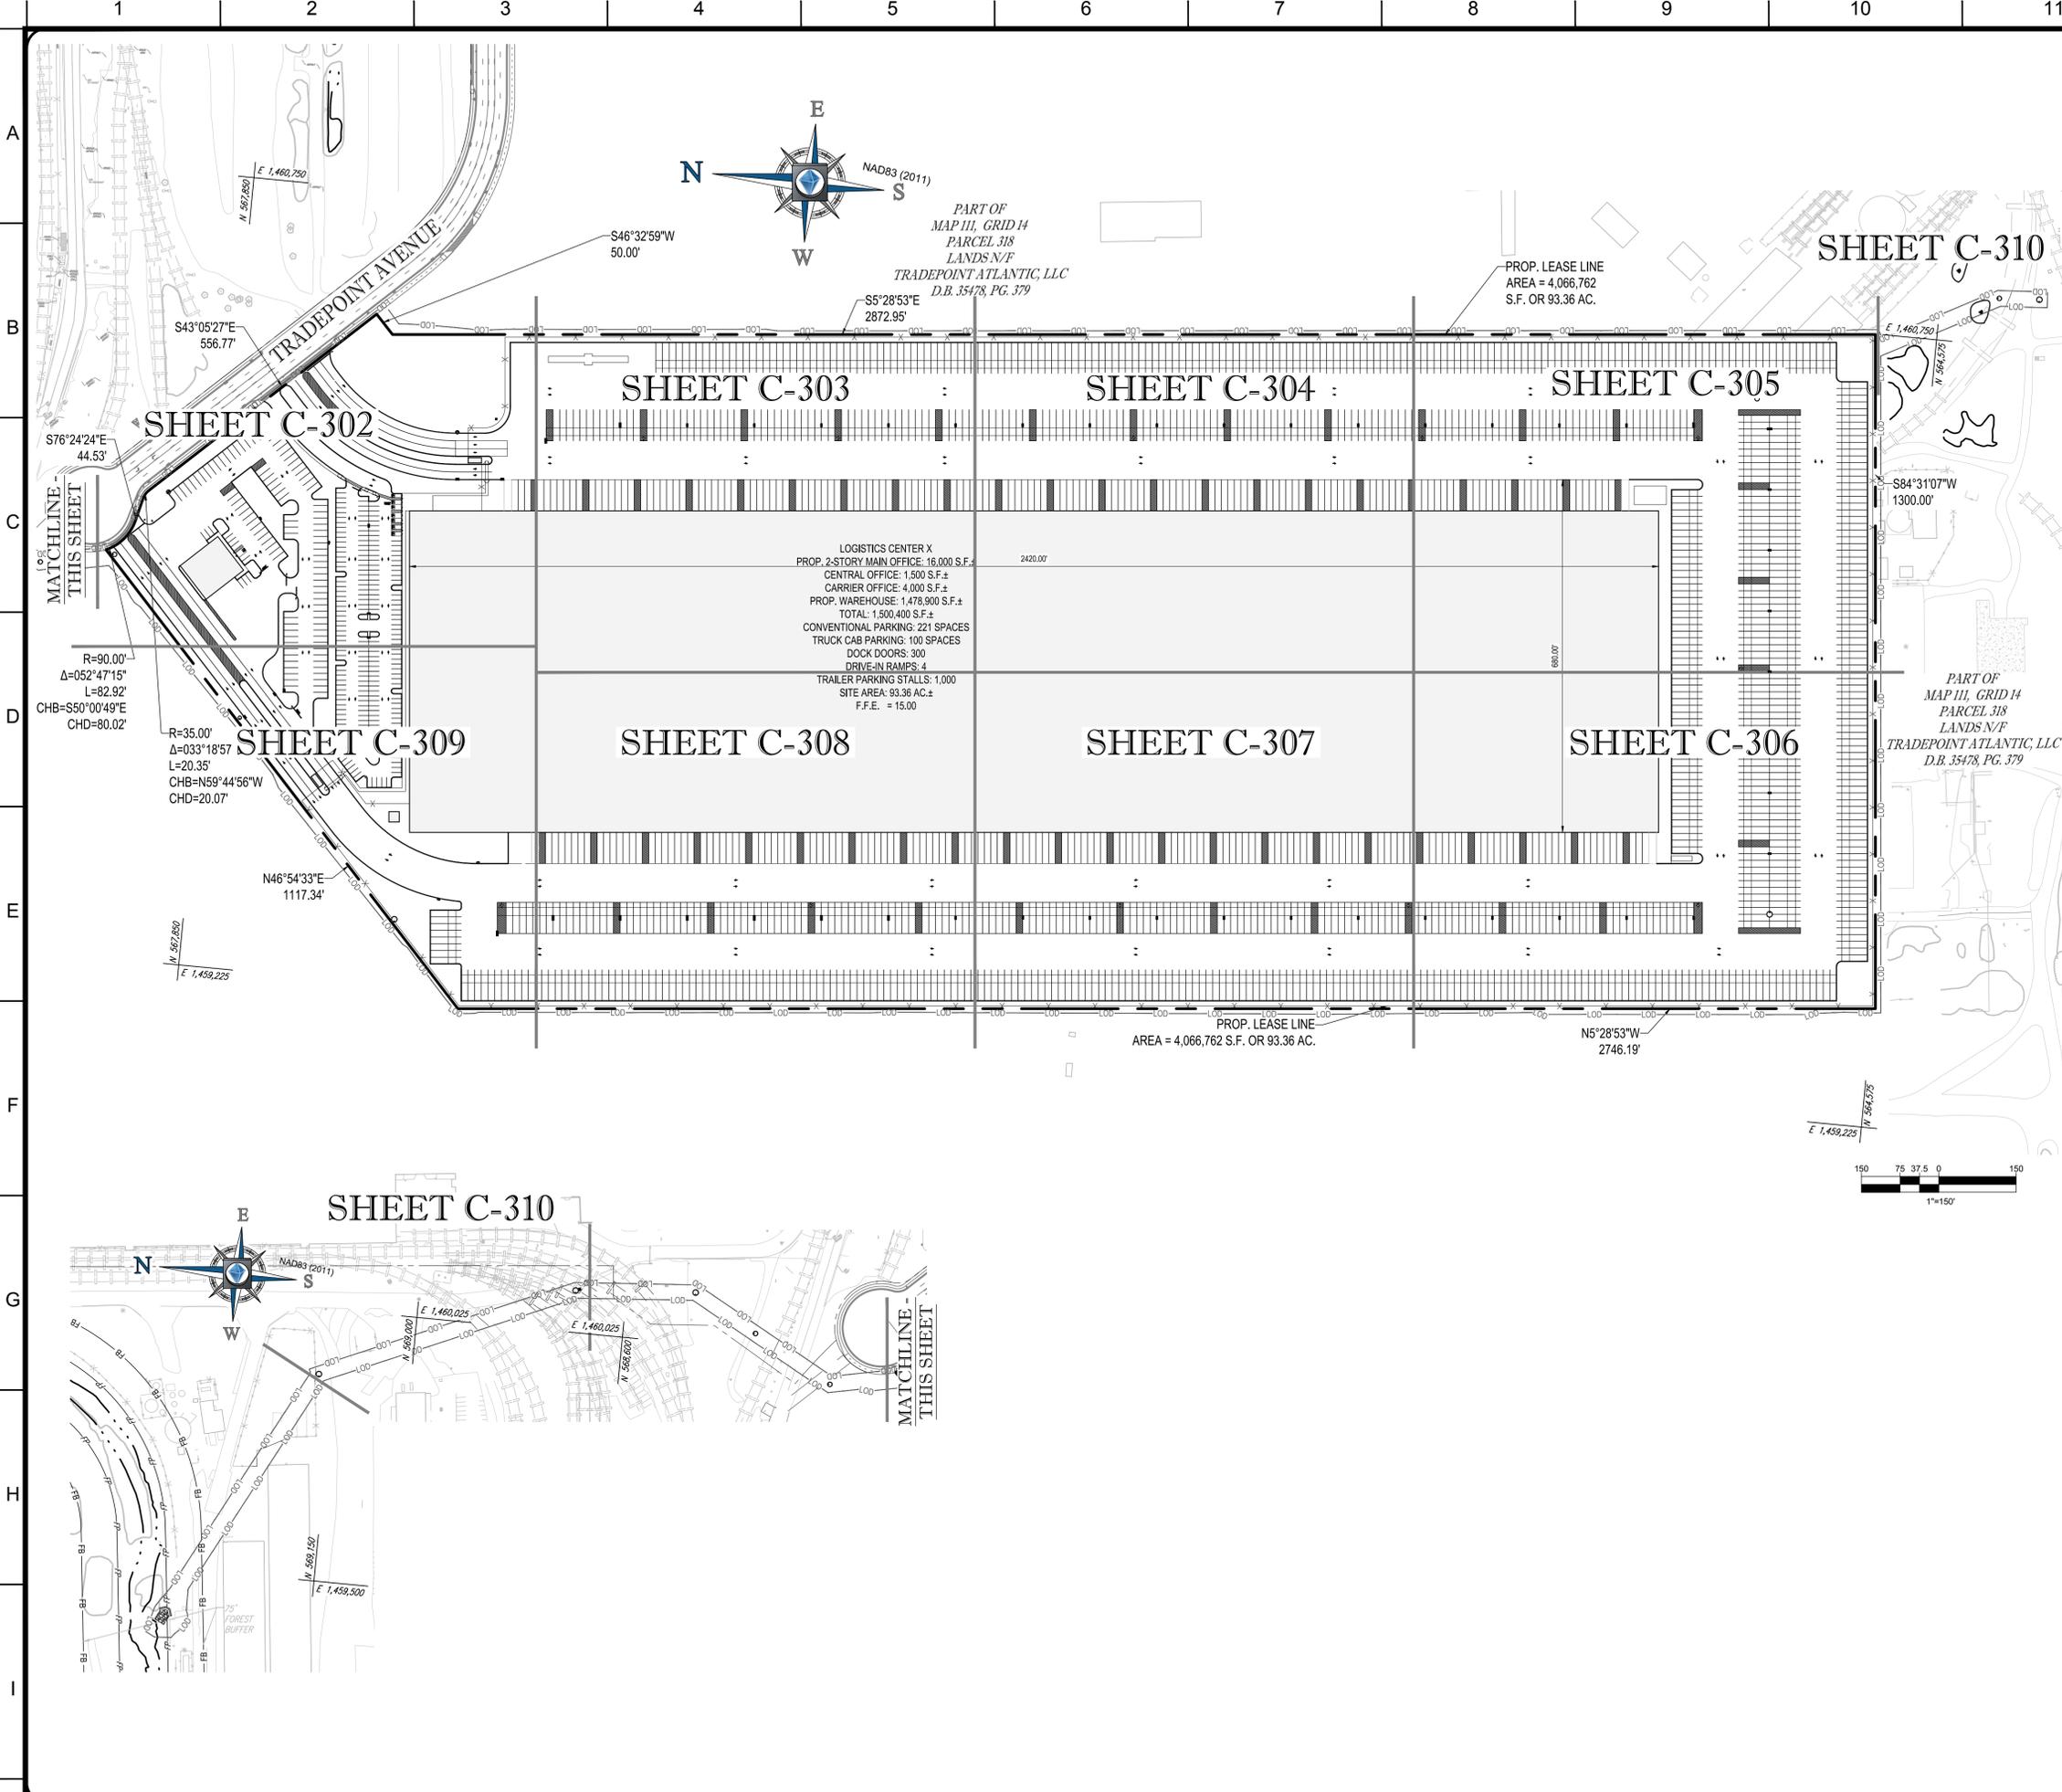

LOCATION MAP
 COPYRIGHT ADC THE MAP PEOPLE
 PERMIT USE NO. 20802453-5
 SCALE: 1"=2000'

BENCHMARK INFORMATION
 ELEVATIONS ARE BASED ON NAVD 88. COORDINATES AND MERIDIAN ARE BASED ON THE MARYLAND COORDINATE SYSTEM (MCS) PER THE FOLLOWING MONUMENTS.

- BCO# 1433 (CAPPED REBAR)
 N 571.883.79, E 1,468,230.89, ELEV. 16.59
 IN MEDIAN OF NORTH POINT BLVD SOUTH OF NORTH SNYDER AVE.
- GIS #2 (BRASS DISK)
 N 565,182.39, E. 1,464,480.72, ELEV. 9.95
 EAST SIDE OF WHARF ROAD 420'S NORTH OF LIGHT TOWER

BOHLER ENGINEERING
 SITE CIVIL AND CONSULTING ENGINEERING
 LAND SURVEYING
 PROGRAM MANAGEMENT
 LANDSCAPE ARCHITECTURE
 SUSTAINABLE DESIGN
 TRANSPORTATION SERVICES

REVISIONS			
REV	DATE	COMMENT	BY

811
 KNOW WHAT'S BELOW
 ALWAYS CALL 811
 BEFORE YOU DIG
 It's fast. It's free. It's the law.

NOT APPROVED FOR CONSTRUCTION

PROJECT No.:	MD16209614
DRAWN BY:	DSH
CHECKED BY:	MJG
DATE:	8/31/18
SCALE:	AS NOTED
CAD I.D.:	SSD

PROJECT: **PROJECT SLATE (F.K.A. LOGISTICS CENTER X)**

FOR
TRADEPOINT ATLANTIC
 PHASE II PLANS
 LOCATION OF SITE
 LOGISTICS X WAREHOUSE
 TRADEPOINT AVENUE
 TAX MAP 111, PARCEL 318
 BALTIMORE, MD 21219
 BALTIMORE COUNTY


BOHLER ENGINEERING
 901 DULANEY VALLEY ROAD, SUITE 801
 TOWSON, MARYLAND 21204
 Phone: (410) 821-7900
 Fax: (410) 821-7987
 MD@BohlerEng.com

ANDREW G. STINE
 PROFESSIONAL ENGINEER
 MARYLAND LICENSE NO. 3180

SHEET TITLE:
OVERALL SITE PLAN
 SHEET NUMBER:
C-301

ELEVATIONS BASED ON NAVD 88. COORDINATES AND MERIDIAN ARE BASED ON THE MARYLAND COORDINATE SYSTEM (MCS) PER MONUMENTS BCO #1433 AND GIS 2

PROFESSIONAL CERTIFICATION
 I, ANDREW G. STINE, HEREBY CERTIFY THAT THESE DOCUMENTS WERE PREPARED OR APPROVED BY ME, AND THAT I AM A DULY LICENSED PROFESSIONAL ENGINEER UNDER THE LAWS OF THE STATE OF MARYLAND, LICENSE NO. 37887, EXPIRATION DATE: 7/12/19

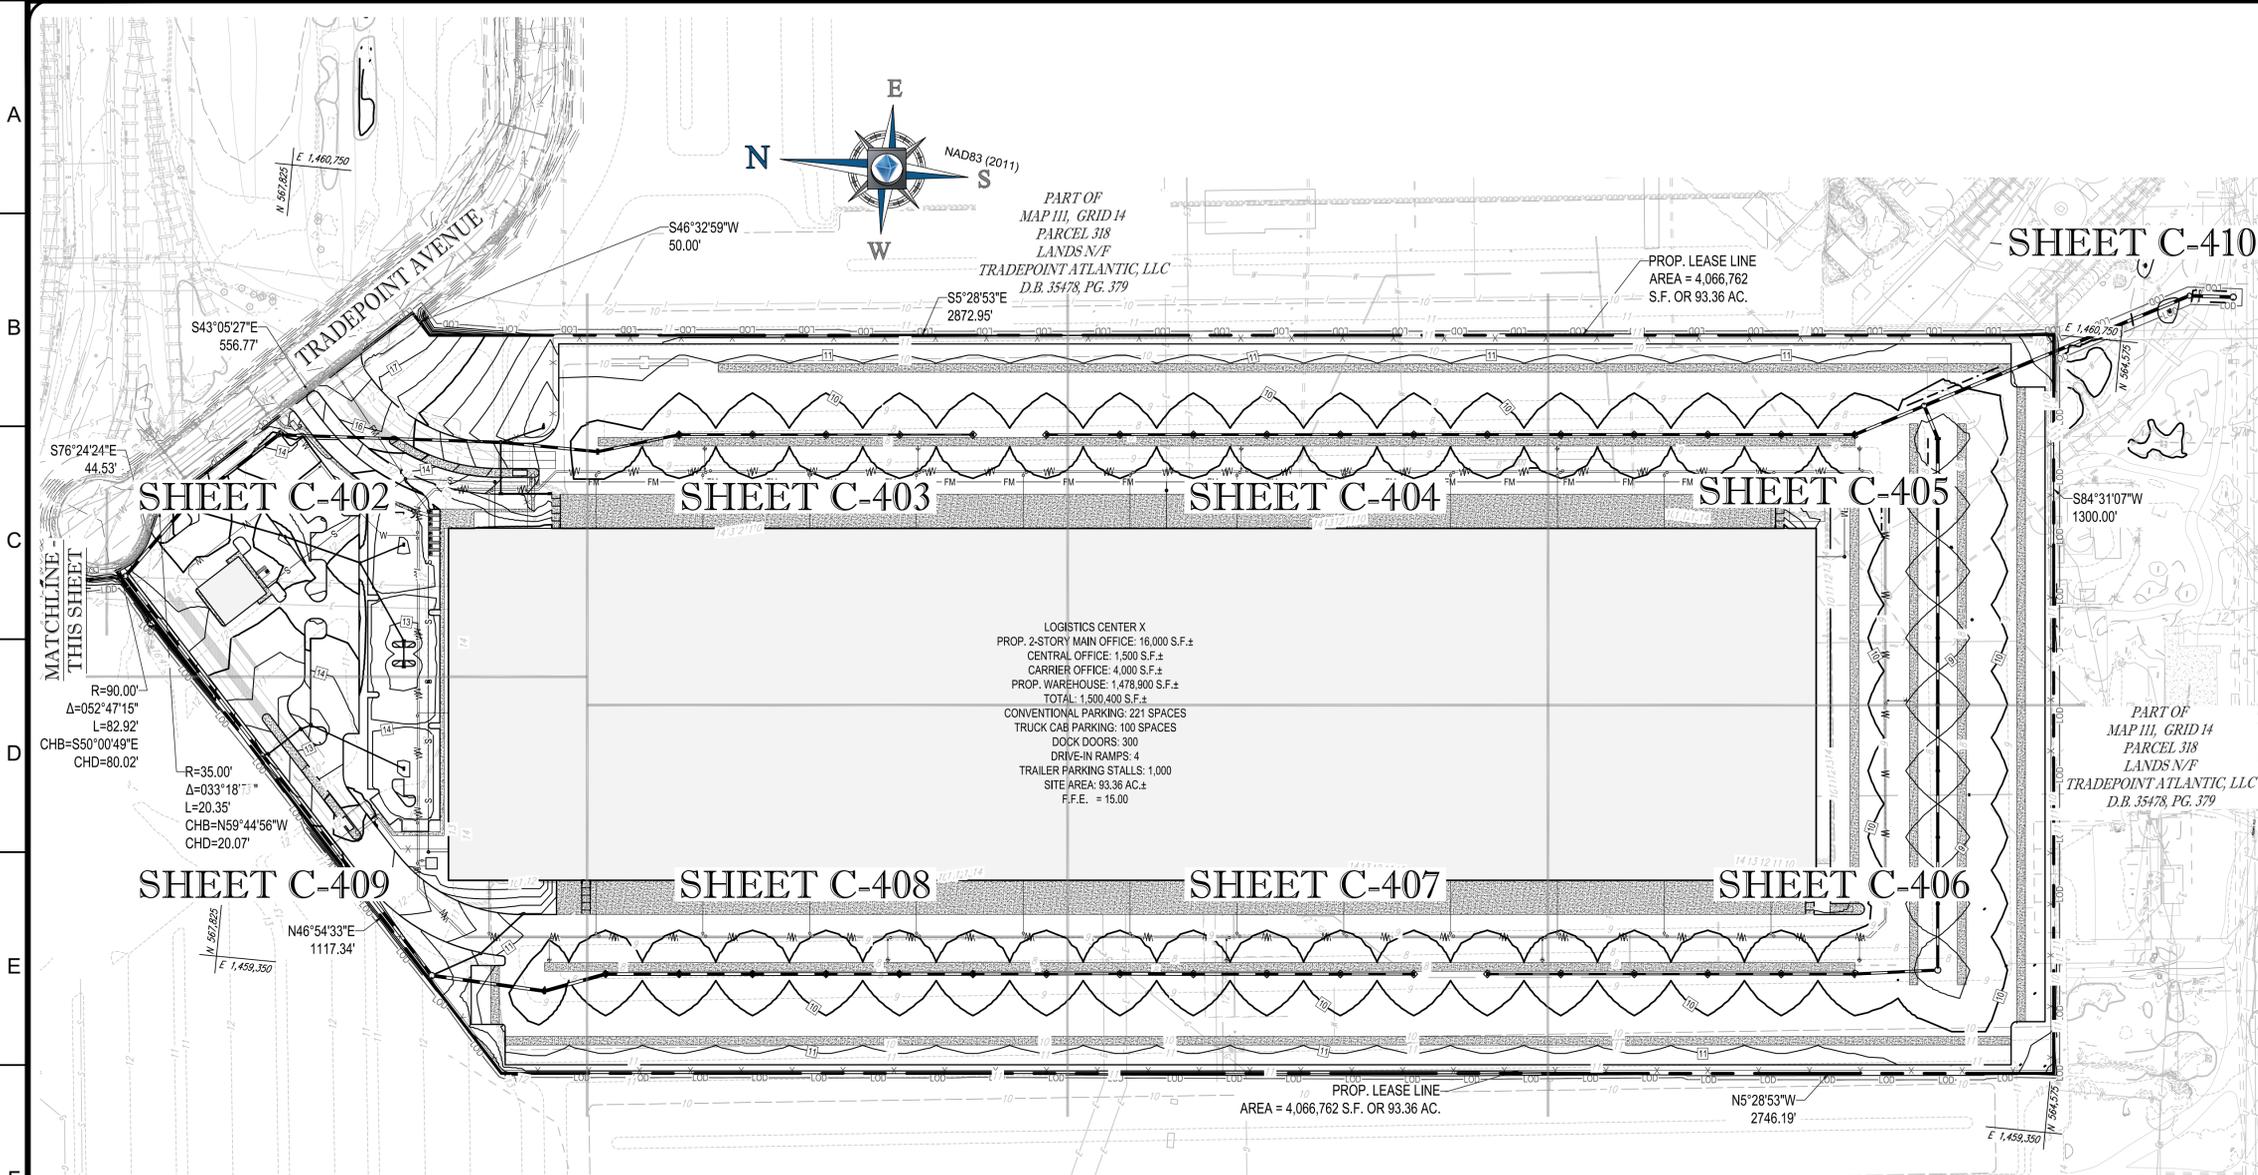

PART OF MAP III, GRID 14 PARCEL 318 LANDS N/F TRADEPOINT ATLANTIC, LLC D.B. 35178, PG. 379

PROP. LEASE LINE AREA = 4,066,762 S.F. OR 93.36 AC.

SHEET C-410

LOGISTICS CENTER X
PROP. 2-STORY MAIN OFFICE: 16,000 S.F.±
CENTRAL OFFICE: 1,500 S.F.±
CARRIER OFFICE: 4,000 S.F.±
PROP. WAREHOUSE: 1,478,900 S.F.±
TOTAL: 1,500,400 S.F.±
CONVENTIONAL PARKING: 221 SPACES
TRUCK CAB PARKING: 100 SPACES
DOCK DOORS: 300
DRIVE-IN RAMPS: 4
TRAILER PARKING STALLS: 1,000
SITE AREA: 93.36 AC.±
F.F.E. = 15.00


PART OF MAP III, GRID 14 PARCEL 318 LANDS N/F TRADEPOINT ATLANTIC, LLC D.B. 35178, PG. 379

SHEET C-407

SHEET C-410

GENERAL GRADING NOTES

- 1. IT IS THE CONTRACTOR'S RESPONSIBILITY TO REVIEW ALL CONSTRUCTION CONTRACT DOCUMENTS INCLUDING, BUT NOT LIMITED TO, ALL OF THE DRAWINGS AND SPECIFICATIONS ASSOCIATED WITH THE PROJECT WORK SCOPE PRIOR TO THE INITIATION AND COMMENCEMENT OF CONSTRUCTION. SHOULD THE CONTRACTOR FIND A CONFLICT AND/OR DISCREPANCY BETWEEN THE DOCUMENTS RELATIVE TO THE SPECIFICATIONS OR THE RELATIVE OR APPLICABLE CODES, REGULATIONS, LAWS, RULES, STATUTES AND/OR ORDINANCES, IT IS THE CONTRACTOR'S SOLE RESPONSIBILITY TO NOTIFY THE PROJECT ENGINEER OF RECORD. IN WRITING, OF SAID CONFLICT AND/OR DISCREPANCY PRIOR TO THE START OF CONSTRUCTION. CONTRACTOR'S FAILURE TO NOTIFY THE PROJECT ENGINEER SHALL CONSTITUTE CONTRACTOR'S FULL AND COMPLETE ACCEPTANCE OF ALL RESPONSIBILITY TO COMPLETE THE SCOPE OF WORK AS DEFINED BY THE DRAWINGS AND IN FULL COMPLIANCE WITH ALL FEDERAL, STATE AND LOCAL REGULATIONS, LAWS, STATUTES, ORDINANCES AND CODES AND, FURTHER, CONTRACTOR SHALL BE RESPONSIBLE FOR ALL COSTS ASSOCIATED WITH SAME.
- 2. SITE GRADING MUST BE PERFORMED IN ACCORDANCE WITH THESE PLANS AND SPECIFICATIONS AND THE RECOMMENDATIONS SET FORTH IN THE GEOTECHNICAL REPORT REFERENCED IN THIS PLAN SET. THE CONTRACTOR IS RESPONSIBLE FOR REMOVING AND REPLACING UNSUITABLE MATERIALS WITH SUITABLE MATERIALS AS SPECIFIED IN THE GEOTECHNICAL REPORT. ALL EXCAVATED OR FILLED AREAS MUST BE COMPACTED AS OUTLINED IN THE GEOTECHNICAL REPORT. MOISTURE CONTENT AT TIME OF PLACEMENT MUST BE SUBMITTED IN A COMPACTION REPORT PREPARED BY A QUALIFIED GEOTECHNICAL ENGINEER, REGISTERED WITH THE STATE WHERE THE WORK IS PERFORMED, VERIFYING THAT ALL FILLED AREAS AND SUBGRADE AREAS WITHIN THE BUILDING PAD AREA AND AREAS TO BE PAVED HAVE BEEN COMPACTED IN ACCORDANCE WITH THESE PLANS, SPECIFICATIONS AND THE RECOMMENDATIONS SET FORTH IN THE GEOTECHNICAL REPORT AND ALL APPLICABLE REQUIREMENTS, RULES, STATUTES, LAWS, ORDINANCES AND CODES. SUBBASE MATERIAL FOR SIDEWALKS, CURBS, OR ASPHALT MUST BE FREE OF ORGANICS AND OTHER UNSUITABLE MATERIALS. SHOULD SUBBASE BE DETERMINED UNSUITABLE BY OWNER/DEVELOPER, OR OWNER/DEVELOPER'S REPRESENTATIVE, SUBBASE IS TO BE REMOVED AND FILLED WITH APPROVED FILL MATERIAL, COMPACTED AS DIRECTED BY THE GEOTECHNICAL REPORT. EARTHWORK ACTIVITIES INCLUDING, BUT NOT LIMITED TO, EXCAVATION, BACKFILL, AND COMPACTING MUST COMPLY WITH THE RECOMMENDATIONS IN THE GEOTECHNICAL REPORT AND ALL APPLICABLE REQUIREMENTS, RULES, STATUTES, LAWS, ORDINANCES AND CODES. EARTHWORK ACTIVITIES MUST COMPLY WITH THE STANDARD STATE DOT SPECIFICATIONS FOR ROADWAY CONSTRUCTION (LATEST EDITION AND ANY AMENDMENTS OR REVISIONS THERETO).
- 3. THE CONTRACTOR MUST COMPLY, TO THE FULLEST EXTENT, WITH THE LATEST OSHA STANDARDS AND REGULATIONS, AND/OR ANY OTHER AGENCY WITH JURISDICTION FOR EXCAVATION AND TRENCHING PROCEDURES. THE CONTRACTOR IS RESPONSIBLE FOR DETERMINING THE "MEANS AND METHODS" REQUIRED TO MEET THE INTENT AND PERFORMANCE CRITERIA OF OSHA, AS WELL AS ANY OTHER ENTITY THAT HAS JURISDICTION FOR EXCAVATION AND/OR TRENCHING PROCEDURES AND CONSULTANT SHALL HAVE NO RESPONSIBILITY FOR OR AS RELATED TO EXCAVATION AND TRENCHING PROCEDURES.
- 4. PAVEMENT MUST BE SAW CUT IN STRAIGHT LINES, AND EXCEPT FOR EDGE OF BUTT JOINTS, MUST EXTEND TO THE FULL DEPTH OF THE EXISTING PAVEMENT. ALL DEBRIS FROM REMOVAL OPERATIONS MUST BE REMOVED FROM THE SITE AT THE TIME OF EXCAVATION. STOCKING OF DEBRIS WILL NOT BE PERMITTED.
- 5. THE TOPS OF EXISTING MANHOLES, INLET STRUCTURES, AND SANITARY CLEANOUT TOPS MUST BE ADJUSTED, AS NECESSARY, TO MATCH PROPOSED GRADES IN ACCORDANCE WITH ALL APPLICABLE STANDARDS, REQUIREMENTS, RULES, STATUTES, LAWS, ORDINANCES AND CODES.
- 6. THE CONTRACTOR IS FULLY RESPONSIBLE FOR VERIFICATION OF EXISTING TOPOGRAPHIC INFORMATION AND UTILITY INVERT ELEVATIONS PRIOR TO COMMENCING ANY CONSTRUCTION. CONTRACTOR MUST CONFIRM AND ENSURE 0.75% MINIMUM SLOPE AGAINST ALL ISLANDS, GUTTERS, AND CURBS; 1.0% ON ALL CONCRETE SURFACES; AND 1.0% MINIMUM ON ASPHALT (EXCEPT WHERE ADA REQUIREMENTS LIMIT GRADES), TO PREVENT PONDING. CONTRACTOR MUST IMMEDIATELY NOTIFY, IN WRITING TO THE ENGINEER, ANY DISCREPANCIES THAT MAY OR COULD AFFECT THE PUBLIC SAFETY, HEALTH OR GENERAL WELFARE, OR PROJECT COST. CONTRACTOR PROCEEDS WITH CONSTRUCTION WITHOUT PROVIDING PROPER NOTIFICATION, MUST BE AT THE CONTRACTOR'S OWN RISK AND, FURTHER, CONTRACTOR SHALL INDEMNIFY, DEFEND AND HOLD HARMLESS THE DESIGN ENGINEER FOR ANY DAMAGES, COSTS, INJURIES, ATTORNEY'S FEES AND THE LIKE WHICH RESULT FROM SAME.
- 7. PROPOSED TOP OF CURB ELEVATIONS ARE GENERALLY 6" ABOVE EXISTING LOCAL ASPHALT GRADE UNLESS OTHERWISE NOTED. FIELD ADJUST TO CREATE A MINIMUM OF 0.75% GUTTER GRADE ALONG CURB FACE. IT IS CONTRACTOR'S OBLIGATION TO ENSURE THAT DESIGN ENGINEER APPROVES FINAL CURBING CUT SHEETS PRIOR TO INSTALLATION OF SAME.
- 8. REFER TO SITE PLAN FOR ADDITIONAL NOTES.
- 9. IN THE EVENT OF DISCREPANCIES AND/OR CONFLICTS BETWEEN PLANS OR RELATIVE TO OTHER PLANS, THE SITE PLAN WILL TAKE PRECEDENCE AND CONTROL. CONTRACTOR MUST IMMEDIATELY NOTIFY THE DESIGN ENGINEER, IN WRITING, OF ANY DISCREPANCIES AND/OR CONFLICTS.
- 10. CONTRACTOR IS REQUIRED TO SECURE ALL NECESSARY AND/OR REQUIRED PERMITS AND APPROVALS FOR ALL OFF SITE MATERIAL SOURCES AND DISPOSAL FACILITIES. CONTRACTOR MUST SUPPLY A COPY OF APPROVALS TO ENGINEER AND OWNER PRIOR TO INITIATING ANY WORK.
- 11. WHERE RETAINING WALLS (WHETHER OR NOT THEY MEET THE JURISDICTIONAL DEFINITION) ARE IDENTIFIED ON PLANS, ELEVATIONS IDENTIFIED ARE FOR THE EXPOSED PORTION OF THE WALL. WALL FOOTINGS/FOUNDATION ELEVATIONS ARE NOT IDENTIFIED HEREIN AND ARE TO BE DETERMINED BY THE CONTRACTOR BASED ON FINAL STRUCTURAL DESIGN SHOP DRAWINGS PREPARED BY THE APPROPRIATE PROFESSIONAL LICENSED IN THE STATE WHERE THE CONSTRUCTION OCCURS.
- 12. CONSULTANT IS NEITHER LIABLE NOR RESPONSIBLE FOR ANY SUBSURFACE CONDITIONS AND FURTHER, SHALL HAVE NO LIABILITY FOR ANY HAZARDOUS MATERIALS, HAZARDOUS SUBSTANCES, OR POLLUTANTS ON, ABOUT OR UNDER THE PROPERTY.

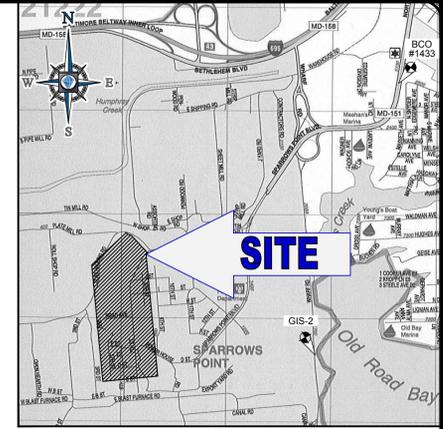

LOCATION MAP

COPYRIGHT ADC THE MAP PEOPLE PERMIT #ISE NO. 2080253-5 SCALE: 1"=2000'

BENCHMARK INFORMATION

ELEVATIONS ARE BASED ON NAVD 88. COORDINATES AND MERIDIAN ARE BASED ON THE MARYLAND COORDINATE SYSTEM (MCS) PER THE FOLLOWING MONUMENTS.
BCO# 1433 (CAPPED REBAR)
N 571,633.79 E 1,468,238.69 ELEV. 16.59
IN MEDIAN OF NORTH POINT BLVD SOUTH OF NORTH SNYDER AVE.
GIS #2 (BRASS DISK)
N 565,182.39 E. 1,464,480.72 ELEV. 9.95
EAST SIDE OF WHARF ROAD 420'S NORTH OF LIGHT TOWER

SITE SPECIFIC GRADING NOTES

- 1. ALL UTILITIES SHOWN ARE PRIVATE.
- 2. THE SUBJECT DEVELOPMENT AREA IS LOCATED IN FLOOD ZONE 'X' (AREAS DETERMINED TO BE OUTSIDE THE CRITICAL AREA) PER MAP ENTITLED "NATIONAL FLOOD INSURANCE PROGRAM, FIRM, FLOOD INSURANCE RATE MAP, BALTIMORE COUNTY, MARYLAND (UNINCORPORATED AREAS) PANEL 555 OF 560" MAP NUMBER 2400105550, MAP REVISED MAY 5, 2014, AND PLAN PREPARED BY PAUL DEV. PLANS REVIEW, DATED SEPTEMBER 21, 2016, PER MAP 0555F, DATED SEPTEMBER 26, 2008.
- 3. ADDITIONAL EXISTING UTILITIES AND SITE FEATURES LOCATED WITHIN THE LIMIT OF DISTURBANCE NOT IDENTIFIED AS "TO BE REMOVED" OR "TO BE RELOCATED" MAY REQUIRE REMOVAL OR RELOCATION AS DIRECTED BY THE GEOTECHNICAL ENGINEER OR TRADEPOINT DEVELOPMENT.
- 4. EXISTING UTILITIES NOTED AS "TO REMAIN" WITHIN THE LIMIT OF DISTURBANCE MUST BE MAINTAINED TO PROVIDE SERVICE FOR THE PROPOSED DEVELOPMENT.
- 5. REFER TO PUBLIC ROAD PLANS FOR GRADING WITHIN TRADEPOINT AVENUE.
- 6. THE ENTIRE SITE AS SHOWN ON THIS PLAN IS LOCATED OUTSIDE THE CRITICAL AREA.
- 7. ALL BUILDING DOWNSPOUTS TO DISCHARGE AT GRADE AND SHEET FLOW TO THE PROPOSED INLETS.

BALTIMORE COUNTY STANDARD GRADING PLAN NOTES

- 1. THE PROPOSED GRADING SHOWN ON THIS PLAN MEETS THE REQUIREMENTS SET FORTH BY BALTIMORE COUNTY DEPARTMENT OF ENVIRONMENTAL PROTECTION AND SUSTAINABILITY AND COMPLIES WITH ARTICLE 33, TITLE 5 OF THE BALTIMORE COUNTY CODE. HOWEVER, DUE TO BUILDING TYPES AND LAYOUT, SOME FIELD ADJUSTMENTS MAY BE REQUIRED. ALL CHANGES MUST COMPLY WITH THE ABOVE MENTIONED REQUIREMENTS.
- 2. ALL SWALES HAVE BEEN DESIGNED BY THE ENGINEER TO CONVEY RUNOFF ACCORDING TO BALTIMORE COUNTY DEPARTMENT OF PUBLIC WORKS DESIGN STANDARDS.
- 3. THERE SHALL BE NO CLEARING, GRADING, CONSTRUCTION OR DISTURBANCE OF VEGETATION IN THE FOREST BUFFER EASEMENT OR OTHER FOREST RETENTION AREAS, EXCEPT AS PERMITTED BY THE BALTIMORE COUNTY DEPARTMENT OF ENVIRONMENTAL PROTECTION AND SUSTAINABILITY.
- 4. STORMWATER MANAGEMENT HAS BEEN ADDRESSED THROUGH A PAYMENT OF A FEE-IN-LIEU TO THE BALTIMORE COUNTY STORMWATER MANAGEMENT FUND FOR 46.89 AC. OF IMPERVIOUS AREA BASED ON AN LOD OF 93.44 ACRES.

LEGEND

EXISTING NOTE	TYPICAL NOTE TEXT	PROPOSED NOTE
---	ONSITE PROPERTY LINE / R.O.W. LINE	---
---	CONTOUR LINE	---
---	SPOT ELEVATIONS	● TC 516.00 ● BC 515.50
---	SANITARY SEWER LINE	---
---	UNDERGROUND WATER LINE	---
---	INDUSTRIAL WATER LINE	---
---	UNDERGROUND ELECTRIC LINE	---
---	UNDERGROUND GAS LINE	---
---	OVERHEAD WIRE	---
---	UNDERGROUND TELEPHONE LINE	---
---	STORM SEWER	---
---	LIMIT OF DISTURBANCE	---
---	SAWCUT	---
---	CONCRETE CURB & GUTTER	---
---	SPILL CURB	---

GRADING 1 OF 10

MARYLAND COORDINATE SYSTEM (MCS)

STORMWATER MANAGEMENT REQUIRED

BALTIMORE COUNTY DEPARTMENT OF ENVIRONMENTAL PROTECTION AND SUSTAINABILITY

APPROVED FOR GRADING

DATE

DEVELOPER

TRADEPOINT DEVELOPMENT, LLC
1600 SPARROWS POINT BLVD
BALTIMORE, MD 21219
CONTACT: JUSTIN DUNN
PHONE: 410-709-1318

ELEVATIONS BASED ON NAVD 88. COORDINATES AND MERIDIAN ARE BASED ON THE MARYLAND COORDINATE SYSTEM (MCS) PER MONUMENTS BCO #1433 AND GIS 2

PROFESSIONAL CERTIFICATION
I, ANDREW G. STINE, HEREBY CERTIFY THAT THESE DOCUMENTS WERE PREPARED OR APPROVED BY ME AND THAT I AM A DULY LICENSED PROFESSIONAL ENGINEER UNDER THE LAWS OF THE STATE OF MARYLAND, LICENSE NO. 37887, EXPIRATION DATE: 7/12/15

OWNER'S/DEVELOPER'S CERTIFICATION - GRADING

I/WE CERTIFY THAT ALL GRADING ON THIS SITE WILL BE DONE IN ACCORDANCE WITH THE CURRENT GRADING REQUIREMENTS AS SET FORTH BY THE BALTIMORE COUNTY DEPARTMENT OF ENVIRONMENTAL PROTECTION AND SUSTAINABILITY AND WITH THE REQUIREMENTS SPECIFIED IN ARTICLE 33, TITLE 5 OF THE BALTIMORE COUNTY CODE.

SIGNATURE OF OWNER/DEVELOPER TITLE DATE
PRINT NAME

LIMIT OF DISTURBANCE: 4,070,046 S.F. OR 93.44 AC.

BOHLER ENGINEERING
SITE CIVIL AND CONSULTING ENGINEERING
LAND SURVEYING
PROGRAM MANAGEMENT
LANDSCAPE ARCHITECTURE
SUSTAINABLE DESIGN
INFRASTRUCTURE
TRANSPORTATION SERVICES
1000 SPARROWS POINT BLVD
BALTIMORE, MD 21219
PHONE: 410-709-1318
WWW.BOHLENGE.COM

REVISIONS

REV	DATE	COMMENT	BY

811
KNOW WHAT'S BELOW
ALWAYS CALL 811
BEFORE YOU DIG
It's fast. It's free. It's the law.

NOT APPROVED FOR CONSTRUCTION

PROJECT No.: MD16209614
DRAWN BY: DSH
CHECKED BY: MJC
DATE: 8/1/18
SCALE: AS NOTED
CAD I.D.: GPD


PROJECT: PROJECT SLATE (F.K.A. LOGISTICS CENTER X)

FOR
TRADEPOINT ATLANTIC
PHASE II PLANS
LOCATION OF SITE
LOGISTICS X WAREHOUSE
TRADEPOINT AVENUE
TAX MAP 111, PARCEL 318
BALTIMORE, MD 21219
BALTIMORE COUNTY


BOHLER ENGINEERING
901 DULANEY VALLEY ROAD, SUITE 801
TOWSON, MARYLAND 21204
Phone: (410) 821-7900
Fax: (410) 821-7987
MD@BohlerEng.com

ANDREW G. STINE
PROFESSIONAL ENGINEER
MARYLAND LICENSE NO. 37887


SHEET TITLE:
OVERALL FINAL GRADING PLAN
SHEET NUMBER:
C-401

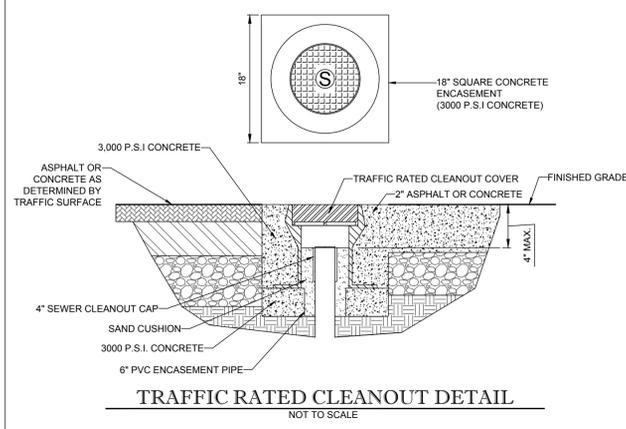

TRAFFIC RATED CLEANOUT DETAIL
NOT TO SCALE



SPILL CURB & GUTTER




COLLECTOR CURB & GUTTER

NOTES:

1. CONCRETE FOR CURBING SHALL HAVE A MINIMUM COMPRESSIVE STRENGTH OF 3000 P.S.I. @ 28 DAYS.
2. CONSTRUCTION STAKING FOR CURB INSTALLATION SHALL BE REFERENCED (CUT OR FILL) TO THE TOP OF CURB.
3. AT CONTRACTOR'S OPTION, THE GUTTER THICKNESS MAY BE INCREASED AT THE EDGE OF PAVEMENT TO MAKE BOTTOM OF GUTTER CONTIGUOUS WITH BOTTOM OF ASPHALT PAVEMENT.
4. CONTRACTION JOINTS SHALL BE PLACED @ 10'-0" O.C. TOOLED 1/4" (±1/16") WIDE, 1" DEEP. EXPANSION JOINTS SHALL BE PLACED @ 40'-0" INTERVALS, MAXIMUM, AND ALL P.C.'S.
5. GUTTER PAN SLOPE TO BE ADJUSTED WITHIN ACCESSIBLE PARKING SPACES TO MATCH SLOPE BETWEEN SPOT ELEVATIONS.


CONCRETE CURB & GUTTER DETAIL
NOT TO SCALE



NOTE:

1. CONTRACTOR TO BLOW OUT DUST FROM DRILLED HOLES PRIOR TO APPLYING GROUT.


CONCRETE DOWELING DETAIL
NOT TO SCALE

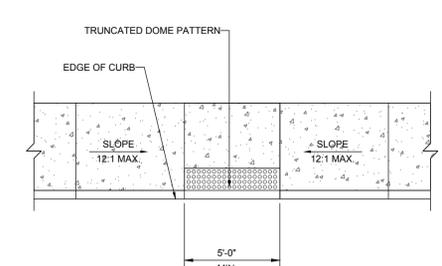

NOTE:

1. ADA ACCESSIBLE RAMP CONSTRUCTION SHALL CONFORM TO CURRENT ADA ACCESSIBLE GUIDELINES.


ADA ACCESSIBLE RAMP DETAIL
NOT TO SCALE

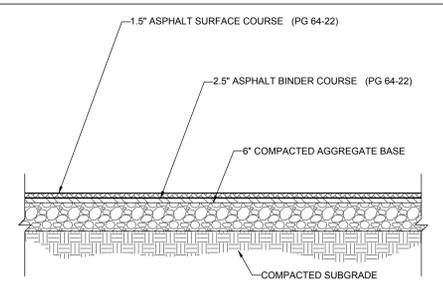


NOTE:

1. SECTION SHOWN WAS PREPARED WITHOUT THE BENEFIT OF A GEOTECHNICAL REPORT. FINAL DESIGN TO BE PROVIDED ONCE FINAL CBR'S ARE AVAILABLE ON COMPACTED SUB-BASE.

STANDARD DUTY ASPHALT PAVEMENT SECTION
NOT TO SCALE

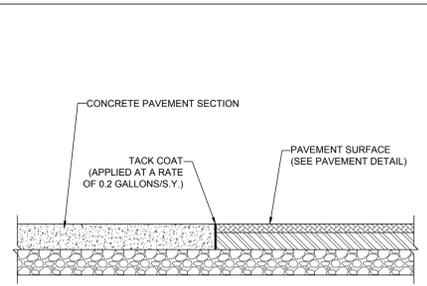


CONCRETE-TO-ASPHALT DETAIL
NOT TO SCALE

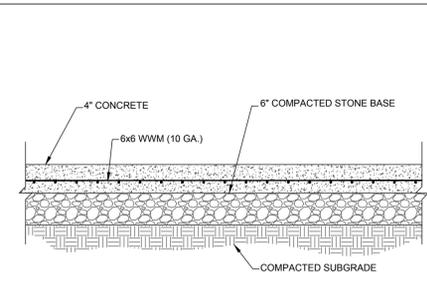

NOTE:

1. SECTION SHOWN WAS PREPARED WITHOUT THE BENEFIT OF A GEOTECHNICAL REPORT. FINAL DESIGN TO BE PROVIDED ONCE FINAL CBR'S ARE AVAILABLE ON COMPACTED SUB-BASE.


STANDARD DUTY CONCRETE SECTION
NOT TO SCALE

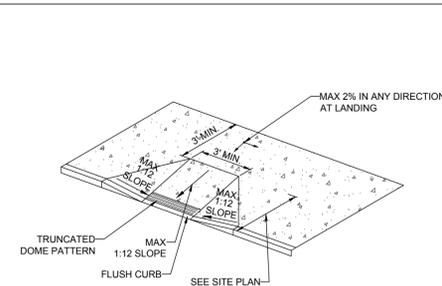


NOTE:

1. ADA ACCESSIBLE RAMP CONSTRUCTION SHALL CONFORM TO CURRENT ADA ACCESSIBLE GUIDELINES.

ADA ACCESSIBLE RAMP DETAIL
NOT TO SCALE

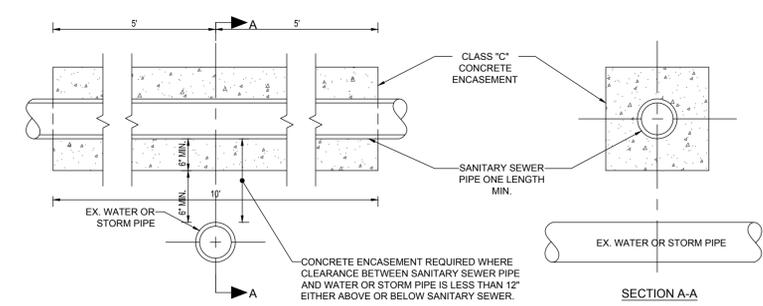


CONCRETE ENCASUREMENT DETAIL
NOT TO SCALE

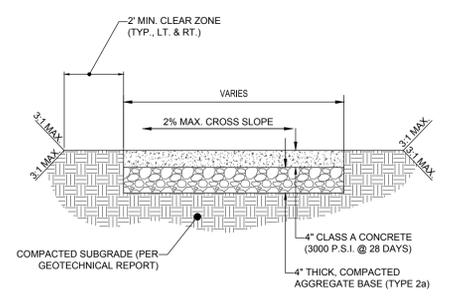

NOTE:

1. EXPANSION JOINTS 1/2" WIDE PREMOLDED BIT. MATERIAL SHALL BE INSTALLED AT 30' INTERVALS. CRACK CONTROL JOINTS TO BE SPACED AT INTERVALS EQUAL TO SIDEWALK WIDTH.


CONCRETE SIDEWALK DETAIL
NOT TO SCALE

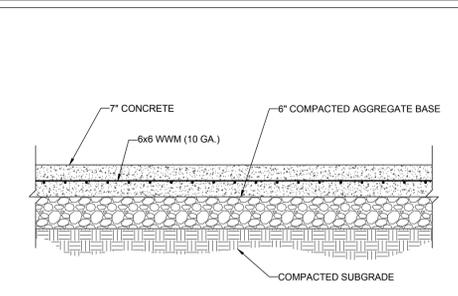

NOTE:

1. SECTION SHOWN WAS PREPARED WITHOUT THE BENEFIT OF A GEOTECHNICAL REPORT. FINAL DESIGN TO BE PROVIDED ONCE FINAL CBR'S ARE AVAILABLE ON COMPACTED SUB-BASE.


HEAVY DUTY CONCRETE SECTION
NOT TO SCALE

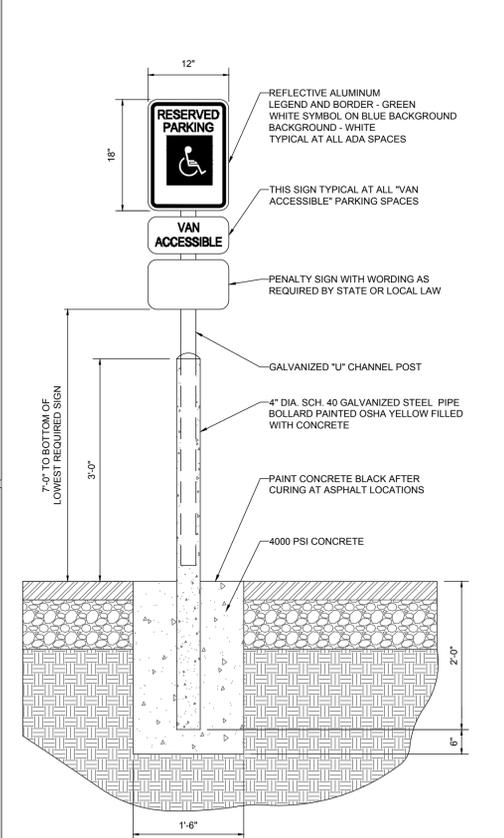

NOTE:

1. ONE AT EACH ADA SPACE. WHERE ADA SPACES FACE EACH OTHER WITHOUT WALKWAY, THERE SHALL BE ONE POST WITH SIGNS MOUNTED BOTH SIDES

BOLLARD MOUNTED ADA PARKING SIGN DETAIL
NOT TO SCALE



NOTE:

1. SECTION SHOWN WAS PREPARED WITHOUT THE BENEFIT OF A GEOTECHNICAL REPORT. FINAL DESIGN TO BE PROVIDED ONCE FINAL CBR'S ARE AVAILABLE ON COMPACTED SUB-BASE.

HEAVY DUTY ASPHALT PAVEMENT SECTION
NOT TO SCALE

BOHLER ENGINEERING
SITE CIVIL AND CONSULTING ENGINEERING
LAND SURVEYING
PROGRAM MANAGEMENT
LANDSCAPE ARCHITECTURE
SUSTAINABLE DESIGN
PERMITTING SERVICES
TRUCKING SERVICES
FROM MOUNTAIN VIEW, COLORADO TO THE PALM BEACHES, FLORIDA. WE CAN TAKE YOU ANYWHERE FROM HERE. WE'VE BEEN THERE SINCE 1988.

REVISIONS

REV	DATE	COMMENT	BY

811
KNOW WHAT'S BELOW
ALWAYS CALL 811
BEFORE YOU DIG
It's fast. It's free. It's the law.

NOT APPROVED FOR CONSTRUCTION

PROJECT No.: MD16206614
DRAWN BY: DSH
CHECKED BY: MJG
DATE: 8/31/18
SCALE: AS NOTED
CAD I.D.: SD0

PROJECT SLATE (F.K.A. LOGISTICS CENTER X)

FOR **TRADEPOINT ATLANTIC**
PHASE II PLANS
LOCATION OF SITE
LOGISTICS X WAREHOUSE
TRADEPOINT AVENUE
TAX MAP 111, PARCEL 318
BALTIMORE, MD 21219
BALTIMORE COUNTY

BOHLER ENGINEERING
901 DULANEY VALLEY ROAD, SUITE 801
TOWSON, MARYLAND 21204
Phone: (410) 821-7900
Fax: (410) 821-7987
MD@BohlerEng.com

ANDREW G. STINE
PROFESSIONAL ENGINEER
MARYLAND LICENSE No. 37887

SHEET TITLE:
C-901 - SITE DETAILS
SHEET NUMBER:
C-901

ELEVATIONS BASED ON NAVD 88. COORDINATES AND MERIDIAN ARE BASED ON THE MARYLAND COORDINATE SYSTEM (MCS) PER MONUMENTS BCO #1433 AND GIS 2

PROFESSIONAL CERTIFICATION
I, ANDREW G. STINE, HEREBY CERTIFY THAT THESE DOCUMENTS WERE PREPARED OR APPROVED BY ME, AND THAT I AM A DULY LICENSED PROFESSIONAL ENGINEER UNDER THE LAWS OF THE STATE OF MARYLAND, LICENSE NO. 37887, EXPIRATION DATE: 7/12/19

120" DIAMETER PRECAST MANHOLE FOR 78" TO 84" PIPES

STANDARD NO. MD 384.11

NOTES:

1. THIS STANDARD IS TO BE USED WITH TYPE A COMBINATION CURB AND GUTTER.
2. CONCRETE SHALL BE CAST IN PLACE.
3. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
4. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
5. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
6. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
7. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
8. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
9. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
10. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.

ITEM	QUANTITY	REMARKS
1. PRECAST CONCRETE	1.00	120" DIA. MANHOLE
2. REINFORCEMENT	1.00	AS SHOWN
3. CURB AND GUTTER	1.00	AS SHOWN

PRECAST CONCRETE TROUGH SLAB

STANDARD NO. MD 374.62

NOTES:

1. THIS STANDARD IS TO BE USED WITH TYPE A COMBINATION CURB AND GUTTER.
2. CONCRETE SHALL BE CAST IN PLACE.
3. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
4. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
5. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
6. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
7. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
8. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
9. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
10. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.

ITEM	QUANTITY	REMARKS
1. PRECAST CONCRETE	1.00	TROUGH SLAB
2. REINFORCEMENT	1.00	AS SHOWN
3. CURB AND GUTTER	1.00	AS SHOWN

PRECAST CONCRETE INLET SLAB FOR SQUARE & RECTANGULAR COG & COG INLETS

STANDARD NO. MD 374.63

NOTES:

1. THIS STANDARD IS TO BE USED WITH TYPE A COMBINATION CURB AND GUTTER.
2. CONCRETE SHALL BE CAST IN PLACE.
3. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
4. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
5. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
6. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
7. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
8. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
9. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
10. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.

ITEM	QUANTITY	REMARKS
1. PRECAST CONCRETE	1.00	INLET SLAB
2. REINFORCEMENT	1.00	AS SHOWN
3. CURB AND GUTTER	1.00	AS SHOWN

PRECAST CONCRETE INLET SLAB FOR CIRCULAR COG & COG INLETS

STANDARD NO. MD 374.64

NOTES:

1. THIS STANDARD IS TO BE USED WITH TYPE A COMBINATION CURB AND GUTTER.
2. CONCRETE SHALL BE CAST IN PLACE.
3. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
4. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
5. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
6. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
7. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
8. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
9. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
10. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.

ITEM	QUANTITY	REMARKS
1. PRECAST CONCRETE	1.00	INLET SLAB
2. REINFORCEMENT	1.00	AS SHOWN
3. CURB AND GUTTER	1.00	AS SHOWN

PRECAST TRIPLE WR INLET (MODIFIED)

STANDARD NO. MD 374.26

NOTES:

1. THIS STANDARD IS TO BE USED WITH TYPE A COMBINATION CURB AND GUTTER.
2. CONCRETE SHALL BE CAST IN PLACE.
3. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
4. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
5. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
6. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
7. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
8. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
9. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
10. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.

ITEM	QUANTITY	REMARKS
1. PRECAST CONCRETE	1.00	TRIPLE WR INLET
2. REINFORCEMENT	1.00	AS SHOWN
3. CURB AND GUTTER	1.00	AS SHOWN

DOUBLE GRATE TANDEM (NO SUPPORT BEAM)

TYPE S INLET

STANDARD NO. D-2.19A

NOTES:

1. SEE STD. DETAIL D-2.20 FOR GENERAL NOTES.
2. INLET MAY BE CONSTRUCTED OF PRECAST OR REINFORCED CONCRETE. TYPE AND DIMENSIONS OF INLET CONNECTION SHALL VARY TO SUIT CONDITIONS. SEE DETAIL D-2.20.
3. PLACE 1/4" EXPANSION MATERIAL OF SAME TYPE APPROVED FOR PAVEMENT AT LOCATIONS SHOWN ON STD. DETAIL D-2.20. USE PARALLEL BARS TO BE USED TO HOLD IN PLACE. SEE DETAIL D-2.20.
4. SUBGRADE FINISH - 1.5" MAX. BELOW TOP OF GRATE.
5. TYPE 'S' INLET - DOUBLE GRATE TANDEM MAY BE USED WITH OR WITHOUT MANHOLE. USE PARALLEL BARS TO BE USED TO HOLD IN PLACE. SEE DETAIL D-2.20.
6. INLET SHALL NOT BE USED IN ROADWAY OR DRIVEWAY UNLESS APPROVED BY THE MANUFACTURER.
7. INLET SHALL NOT BE USED IN ROADWAY OR DRIVEWAY UNLESS APPROVED BY THE MANUFACTURER.
8. INLET SHALL NOT BE USED IN ROADWAY OR DRIVEWAY UNLESS APPROVED BY THE MANUFACTURER.
9. INLET SHALL NOT BE USED IN ROADWAY OR DRIVEWAY UNLESS APPROVED BY THE MANUFACTURER.
10. INLET SHALL NOT BE USED IN ROADWAY OR DRIVEWAY UNLESS APPROVED BY THE MANUFACTURER.

ITEM	QUANTITY	REMARKS
1. PRECAST CONCRETE	1.00	DOUBLE GRATE TANDEM
2. REINFORCEMENT	1.00	AS SHOWN
3. CURB AND GUTTER	1.00	AS SHOWN

SHALLOW PRECAST MANHOLE

STANDARD NO. D-3.02A

NOTES:

1. UNLESS OTHERWISE NOTED, MANHOLE SHOULD BE CAST IN PLACE.
2. ALL CONCRETE SHALL BE 4500 PSI COMPRESSIVE STRENGTH.
3. SHALLOW MANHOLE REINFORCEMENT SHALL BE AS SHOWN.
4. SET SHALLOW MANHOLE IN PLACE ON FINISHED GRADE.
5. PRECAST MANHOLE SHALL BE CAST IN PLACE.
6. MANHOLE SHALL BE CAST IN PLACE.
7. MANHOLE SHALL BE CAST IN PLACE.
8. MANHOLE SHALL BE CAST IN PLACE.
9. MANHOLE SHALL BE CAST IN PLACE.
10. MANHOLE SHALL BE CAST IN PLACE.

ITEM	QUANTITY	REMARKS
1. PRECAST CONCRETE	1.00	SHALLOW MANHOLE
2. REINFORCEMENT	1.00	AS SHOWN
3. CURB AND GUTTER	1.00	AS SHOWN

TYPE S COMBINATION INLET DOUBLE GRATE TANDEM

STANDARD NO. D-2.20

NOTES:

1. SEE STD. DETAIL D-2.20 FOR GENERAL NOTES.
2. INLET MAY BE CONSTRUCTED OF PRECAST OR REINFORCED CONCRETE. TYPE AND DIMENSIONS OF INLET CONNECTION SHALL VARY TO SUIT CONDITIONS. SEE DETAIL D-2.20.
3. PLACE 1/4" EXPANSION MATERIAL OF SAME TYPE APPROVED FOR PAVEMENT AT LOCATIONS SHOWN ON STANDARD DETAIL D-2.20. USE PARALLEL BARS TO BE USED TO HOLD IN PLACE. SEE DETAIL D-2.20.
4. SUBGRADE FINISH - 1.5" MAX. BELOW TOP OF GRATE.
5. TYPE 'S' INLET - DOUBLE GRATE TANDEM MAY BE USED WITH OR WITHOUT MANHOLE. USE PARALLEL BARS TO BE USED TO HOLD IN PLACE. SEE DETAIL D-2.20.
6. INLET SHALL NOT BE USED IN ROADWAY OR DRIVEWAY UNLESS APPROVED BY THE MANUFACTURER.
7. INLET SHALL NOT BE USED IN ROADWAY OR DRIVEWAY UNLESS APPROVED BY THE MANUFACTURER.
8. INLET SHALL NOT BE USED IN ROADWAY OR DRIVEWAY UNLESS APPROVED BY THE MANUFACTURER.
9. INLET SHALL NOT BE USED IN ROADWAY OR DRIVEWAY UNLESS APPROVED BY THE MANUFACTURER.
10. INLET SHALL NOT BE USED IN ROADWAY OR DRIVEWAY UNLESS APPROVED BY THE MANUFACTURER.

ITEM	QUANTITY	REMARKS
1. PRECAST CONCRETE	1.00	DOUBLE GRATE TANDEM
2. REINFORCEMENT	1.00	AS SHOWN
3. CURB AND GUTTER	1.00	AS SHOWN

REPAVING QUANTITIES

SHOWN IN TONS PER LINEAR FOOT

TRENCH WIDTH (W)	GRADED AGGREGATE BASE WIDTH (C)		
	12 INCH GRADED AGGREGATE BASE (TONS / LINEAR FOOT)	2 INCH HOT MIX ASPHALT PAVING (TONS / LINEAR FOOT)	3 INCH HOT MIX ASPHALT PAVING (TONS / LINEAR FOOT)
6"	0.318	0.037	0.075
8"	0.318	0.037	0.075
10"	0.318	0.037	0.075
12"	0.318	0.037	0.075
15" & 16"	0.318	0.037	0.075
18"	0.354	0.044	0.084
20" & 21"	0.354	0.044	0.084
24"	0.390	0.050	0.094
27"	0.393	0.052	0.112
30"	0.393	0.052	0.112
33"	0.399	0.059	0.122
36"	0.399	0.059	0.122
42"	0.471	0.081	0.140
48"	0.508	0.087	0.150
54"	0.580	0.100	0.168
60"	0.616	0.106	0.178
66"	0.653	0.112	0.187
72"	0.725	0.125	0.206
78"	0.798	0.137	0.225
84"	0.834	0.144	0.234
90"	0.870	0.150	0.243
102"	0.943	0.162	0.262
108"	1.015	0.175	0.281

BRACING ADDITIVES

SINGLE TIE	ADD 0.145	ADD 0.225	ADD 0.337
DOUBLE TIE	ADD 0.290	ADD 0.450	ADD 0.675

LANDSCAPE TYPICAL SECTION (LAWN AREA)

NOT TO SCALE

NOTES:

1. MATERIAL - CAST BORN ASTM A-48, CLASS 30.
2. MACHINED ON HORIZONTAL BEARING SURFACE.
3. LOADING - AASHTO H-20.
4. EQUIVALENT DESIGN MAY BE USED WITH APPROVAL OF DEPARTMENT OF PUBLIC WORKS.
5. OPENING AREA - 179 SQUARE INCHES.

HEADWALLS

STANDARD NO. D-1.05

NOTES:

1. THIS STANDARD IS TO BE USED WITH TYPE A COMBINATION CURB AND GUTTER.
2. CONCRETE SHALL BE CAST IN PLACE.
3. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
4. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
5. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
6. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
7. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
8. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
9. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
10. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.

ITEM	QUANTITY	REMARKS
1. PRECAST CONCRETE	1.00	HEADWALL
2. REINFORCEMENT	1.00	AS SHOWN
3. CURB AND GUTTER	1.00	AS SHOWN

DISPOSITION OF BARS DETAIL

STANDARD NO. D-1.05

NOTES:

1. THIS STANDARD IS TO BE USED WITH TYPE A COMBINATION CURB AND GUTTER.
2. CONCRETE SHALL BE CAST IN PLACE.
3. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
4. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
5. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
6. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
7. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
8. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
9. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
10. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.

ITEM	QUANTITY	REMARKS
1. PRECAST CONCRETE	1.00	DISPOSITION OF BARS
2. REINFORCEMENT	1.00	AS SHOWN
3. CURB AND GUTTER	1.00	AS SHOWN

LANDSCAPE TYPICAL SECTION (LAWN AREA)

NOT TO SCALE

NOTES:

1. MATERIAL - CAST BORN ASTM A-48, CLASS 30.
2. MACHINED ON HORIZONTAL BEARING SURFACE.
3. LOADING - AASHTO H-20.
4. EQUIVALENT DESIGN MAY BE USED WITH APPROVAL OF DEPARTMENT OF PUBLIC WORKS.
5. OPENING AREA - 179 SQUARE INCHES.

REPAVING QUANTITIES

SHOWN IN TONS PER LINEAR FOOT

TRENCH WIDTH (W)	GRADED AGGREGATE BASE WIDTH (C)		
	12 INCH GRADED AGGREGATE BASE (TONS / LINEAR FOOT)	2 INCH HOT MIX ASPHALT PAVING (TONS / LINEAR FOOT)	3 INCH HOT MIX ASPHALT PAVING (TONS / LINEAR FOOT)
6"	0.318	0.037	0.075
8"	0.318	0.037	0.075
10"	0.318	0.037	0.075
12"	0.318	0.037	0.075
15" & 16"	0.318	0.037	0.075
18"	0.354	0.044	0.084
20" & 21"	0.354	0.044	0.084
24"	0.390	0.050	0.094
27"	0.393	0.052	0.112
30"	0.393	0.052	0.112
33"	0.399	0.059	0.122
36"	0.399	0.059	0.122
42"	0.471	0.081	0.140
48"	0.508	0.087	0.150
54"	0.580	0.100	0.168
60"	0.616	0.106	0.178
66"	0.653	0.112	0.187
72"	0.725	0.125	0.206
78"	0.798	0.137	0.225
84"	0.834	0.144	0.234
90"	0.870	0.150	0.243
102"	0.943	0.162	0.262
108"	1.015	0.175	0.281

BRACING ADDITIVES

SINGLE TIE	ADD 0.145	ADD 0.225	ADD 0.337
DOUBLE TIE	ADD 0.290	ADD 0.450	ADD 0.675

RADIAL GRATE

FOR USE WITH 24" HEAVY TRAFFIC MANHOLE FRAME

STANDARD NO. D-3.05A

NOTES:

1. MATERIAL - CAST BORN ASTM A-48, CLASS 30.
2. MACHINED ON HORIZONTAL BEARING SURFACE.
3. LOADING - AASHTO H-20.
4. EQUIVALENT DESIGN MAY BE USED WITH APPROVAL OF DEPARTMENT OF PUBLIC WORKS.
5. OPENING AREA - 179 SQUARE INCHES.

HEADWALLS

STANDARD NO. D-1.05

NOTES:

1. THIS STANDARD IS TO BE USED WITH TYPE A COMBINATION CURB AND GUTTER.
2. CONCRETE SHALL BE CAST IN PLACE.
3. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
4. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
5. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
6. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
7. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
8. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
9. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
10. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.

ITEM	QUANTITY	REMARKS
1. PRECAST CONCRETE	1.00	HEADWALL
2. REINFORCEMENT	1.00	AS SHOWN
3. CURB AND GUTTER	1.00	AS SHOWN

DISPOSITION OF BARS DETAIL

STANDARD NO. D-1.05

NOTES:

1. THIS STANDARD IS TO BE USED WITH TYPE A COMBINATION CURB AND GUTTER.
2. CONCRETE SHALL BE CAST IN PLACE.
3. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
4. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
5. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
6. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
7. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
8. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
9. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.
10. CURB AND GUTTER SHALL BE CAST ON FINISHED GRADE.

ITEM	QUANTITY	REMARKS
1. PRECAST CONCRETE	1.00	DISPOSITION OF BARS
2. REINFORCEMENT	1.00	AS SHOWN
3. CURB AND GUTTER	1.00	AS SHOWN

LANDSCAPE TYPICAL SECTION (LAWN AREA)

NOT TO SCALE

NOTES:

1. MATERIAL - CAST BORN ASTM A-48, CLASS 30.
2. MACHINED ON HORIZONTAL BEARING SURFACE.
3. LOADING - AASHTO H-20.
4. EQUIVALENT DESIGN MAY BE USED WITH APPROVAL OF DEPARTMENT OF PUBLIC WORKS.
5. OPENING AREA - 179 SQUARE INCHES.

REPAVING QUANTITIES

SHOWN IN TONS PER LINEAR FOOT

TRENCH WIDTH (W)	GRADED AGGREGATE BASE WIDTH (C)		
	12 INCH GRADED AGGREGATE BASE (TONS / LINEAR FOOT)	2 INCH HOT MIX ASPHALT PAVING (TONS / LINEAR FOOT)	3 INCH HOT MIX ASPHALT PAVING (TONS / LINEAR FOOT)
6"	0.318	0.037	0.075
8"	0.318	0.037	0.075
10"	0.318	0.037	0.075
12"	0.318	0.037	0.075
15" & 16"	0.318	0.037	0.075
18"	0.354	0.044	0.084
20" & 21"	0.354	0.044	0.084
24"	0.390	0.050	0.094
27"	0.393	0.052	0.112
30"	0.393	0.052	0.112
33"	0.399	0.059	0.122
36"	0.399	0.059	0.122
42"	0.471	0.081	0.140
48"	0.508	0.087	0.150
54"	0.580	0.100	0.168
60"	0.616	0.106	0.178
66"	0.653	0.112	0.187
72"	0.725	0.125	0.206
78"	0.798	0.137	0.225
84"	0.834	0.144	0.234
90"	0.870	0.150	0.243
102"	0.943	0.162	0.262
108"	1.015	0.175	0.281

BRACING ADDITIVES

SINGLE TIE	ADD 0.145	ADD 0.225	ADD 0.337
DOUBLE TIE	ADD 0.290	ADD 0.450	ADD 0.675

RADIAL GRATE

FOR USE WITH 24" HEAVY TRAFFIC MANHOLE FRAME

STANDARD NO. D-3.05A

NOTES:

1. MATERIAL - CAST BORN ASTM A-48, CLASS 30.
2. MACHINED ON HORIZONTAL BEARING SURFACE.
3. LOADING - AASHTO H-20.
4. EQUIVALENT DESIGN MAY BE USED WITH APPROVAL OF DEPARTMENT OF PUBLIC WORKS.
5. OPENING AREA - 179 SQUARE INCHES.



BOHLER ENGINEERING

SITE CIVIL AND CONSULTING ENGINEERING


LAND SURVEYING
PROGRAM MANAGEMENT
LANDSCAPE ARCHITECTURE

CRRGF KZ'I "

\\armgroup\el\CopData\Projects\EnviroAnalytics Group\160443M EAG_TPA Redevelopment\Drawg\B6\Production\Figure 6b - Environmental Capping Detail.dwg, Plotted: January 31, 2019

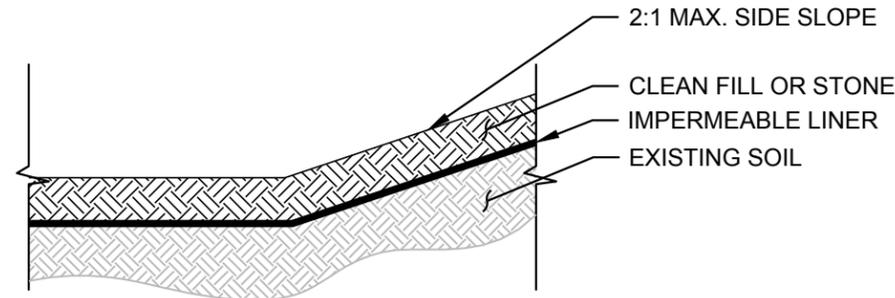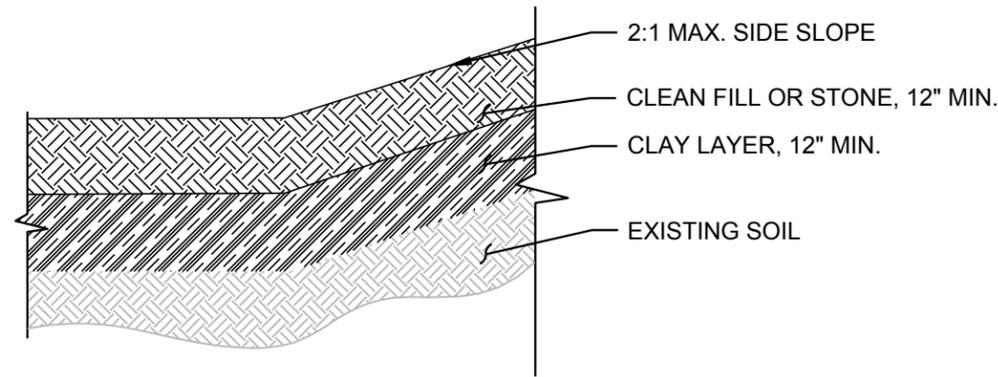


TYPICAL POND SECTIONS
NOT TO SCALE




TYPICAL LANDSCAPE SECTION
NOT TO SCALE

GEOTEXTILE MARKER FABRIC SPECIFICATIONS

THE GEOTEXTILE MARKER FABRIC SHALL BE A NONWOVEN PERVIOUS SHEET OF POLYPROPYLENE MATERIAL. ADD STABILIZERS AND/OR INHIBITORS TO THE BASE MATERIAL, AS NEEDED, TO MAKE THE FILAMENTS RESISTANT TO DETERIORATION BY ULTRAVIALET LIGHT, OXIDATION AND HEAT EXPOSURE. REGRIND MATERIAL, WHICH CONSISTS OF EDGE TRIMMINGS AND OTHER SCRAPS THAT HAVE NEVER REACHED THE CONSUMER, MAY BE USED TO PRODUCE THE GEOTEXTILE. POST-CONSUMER RECYCLED MATERIAL MAY BE USED. GEOTEXTILE SHALL BE FORMED INTO A NETWORK SUCH THAT THE FILAMENTS OR YARNS RETAIN DIMENSIONAL STABILITY RELATIVE TO EACH OTHER, INCLUDING THE EDGES. GEOTEXTILES SHALL MEET THE REQUIREMENTS SPECIFIED IN TABLE 1. WHERE APPLICABLE, TABLE 1 PROPERTY VALUES REPRESENT THE MINIMUM AVERAGE ROLL VALUES IN THE WEAKEST PRINCIPAL DIRECTION. VALUES FOR APPARENT OPENING SIZE (AOS) REPRESENT MAXIMUM AVERAGE ROLL VALUES



TYPICAL PAVING SECTION
NOT TO SCALE

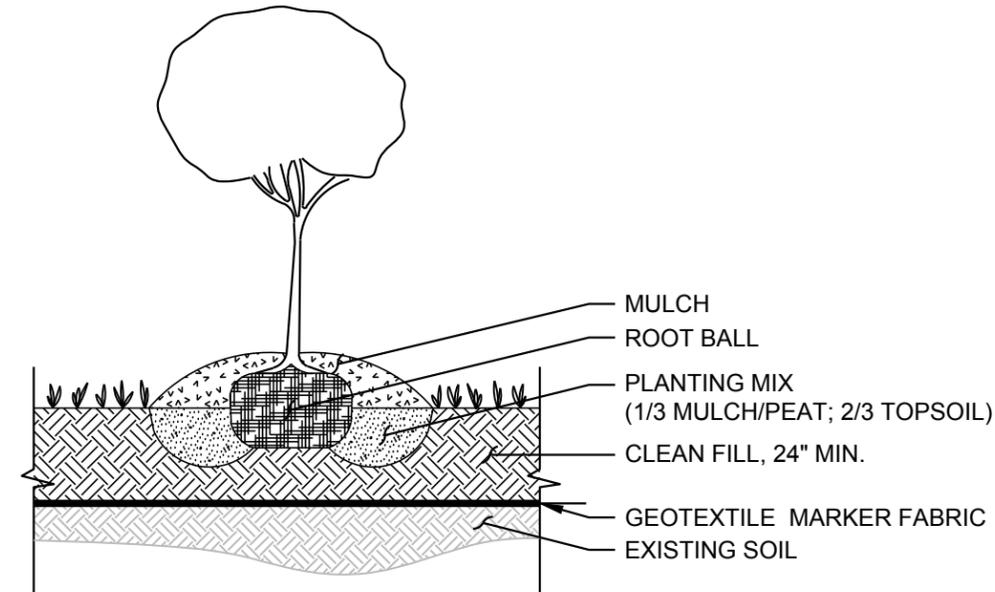

TYPICAL PLANTING SECTION
NOT TO SCALE

TABLE 1		WOVEN SLIT FILM GEOTEXTILE		WOVEN MONOFILAMENT GEOTEXTILE		NONWOVEN GEOTEXTILE	
		MINIMUM AVERAGE ROLL VALUE ¹					
PROPERTY	TEST METHOD	MD	CD	MD	CD	MD	CD
Grab Tensile Strength	ASTM D-4632	200 lb	200 lb	370 lb	250 lb	200 lb	200 lb
Grab Tensile Elongation	ASTM D-4632	15%	10%	15%	15%	50%	50%
Trapezoidal Tear Strength	ASTM D-4533	75 lb	75 lb	100 lb	60 lb	80 lb	80 lb
Puncture Strength	ASTM D-6241	450 lb		900 lb		450 lb	
Apparent Opening Size ²	ASTM D-4751	U.S. Sieve 30 (0.59 mm)		U.S. Sieve 70 (0.21 mm)		U.S. Sieve 70 (0.21 mm)	
Permittivity	ASTM D-4491	0.05 sec ⁻¹		0.28 sec ⁻¹		1.1 sec ⁻¹	
Ultraviolet Resistance Retained at 500 hours	ASTM D-4355	70% strength		70% strength		70% strength	





¹ All numeric values except apparent opening size (AOS) represent minimum average roll values (MARV). MARV is calculated as the typical minus two standard deviations. MD is machine direction; CD is cross direction.

² Values for AOS represent the average maximum opening.

APPENDIX H

GENERAL NOTES:

1. ALL PIPES OR CONDUIT SHALL BE LEAK-PROOF AND WATERTIGHT. ALL JOINTS SHALL BE SEALED OR GASKETED.
2. ALL PIPES SHALL BE PROPERLY PLACED AND BEDDED TO PREVENT MISALIGNMENT OR LEAKAGE. PIPE BEDDING SHALL BE INSTALLED IN SUCH A MANNER AS TO MINIMIZE THE POTENTIAL FOR ACCUMULATION OF WATER AND CONCENTRATED INFILTRATION.
3. MINIMUM COVER ABOVE UTILITY SHALL BE BASED ON SPECIFIC UTILITY REQUIREMENTS.
4. TRENCHES SHALL BE BACKFILLED WITH BEDDING AND MATERIALS APPROVED BY MDE.
5. FOR ANY UTILITY SEGMENT WHICH GOES THROUGH AN AREA WHICH IS DESIGNATED TO RECEIVE A LANDSCAPED CAP, THE UPPER 2 FEET OF BACKFILL MUST MEET THE REQUIREMENTS OF MDE VCP CLEAN FILL FOR INDUSTRIAL LAND USE. IN THIS CASE THE MDE VCP CLEAN FILL WILL BE UNDERLAIN BY A GEOTEXTILE MARKER FABRIC. UTILITY SEGMENTS WHICH GO THROUGH AREAS WHICH DO NOT REQUIRE CAPPING OR ARE DESIGNATED TO RECEIVED A PAVED CAP WILL BE BACKFILLED WITH MATERIALS APPROVED BY MDE FOR THIS USE.

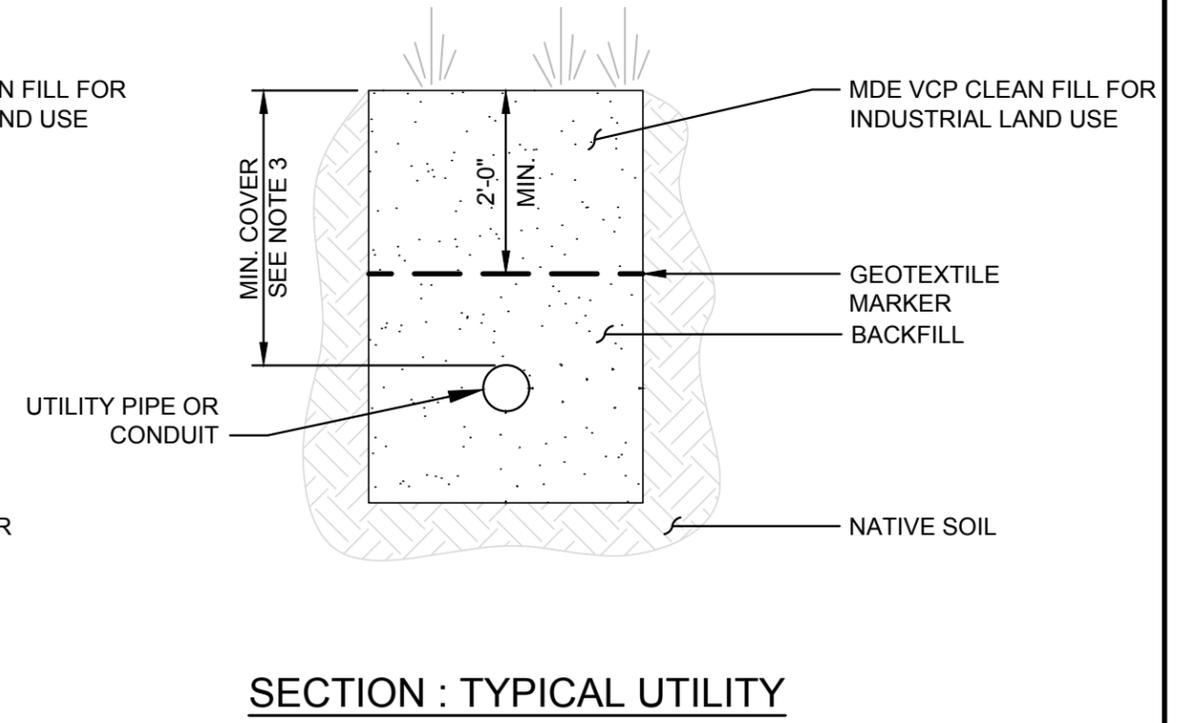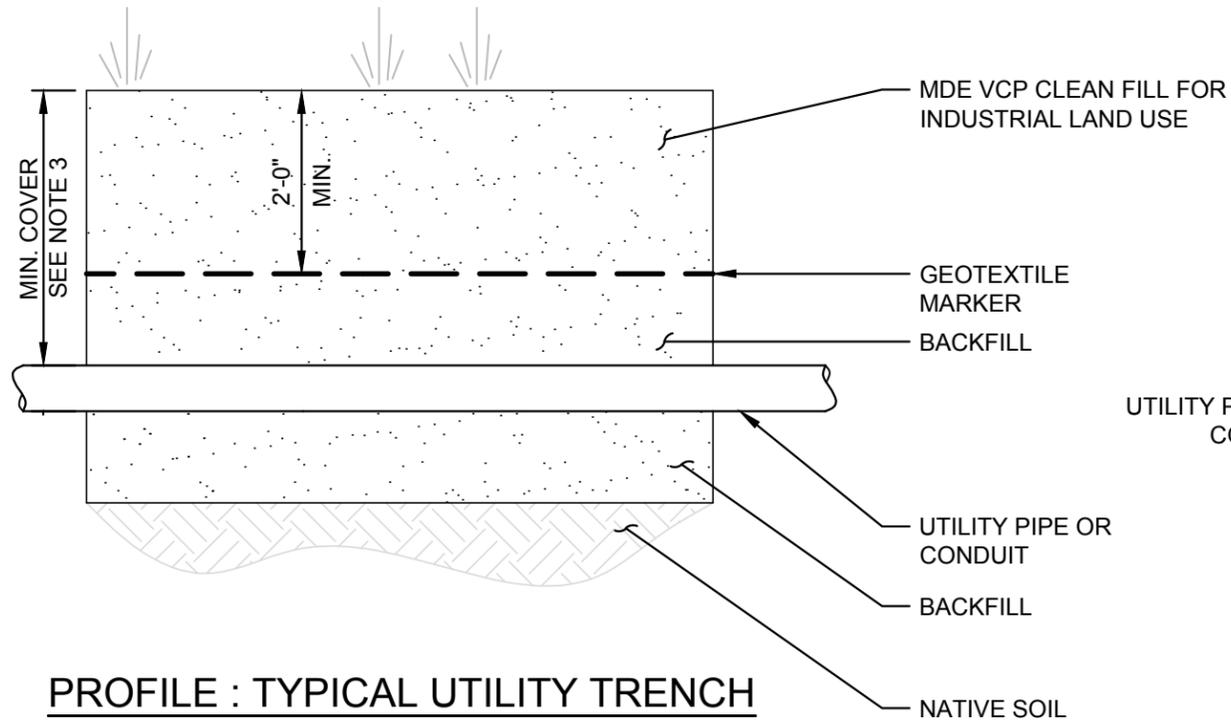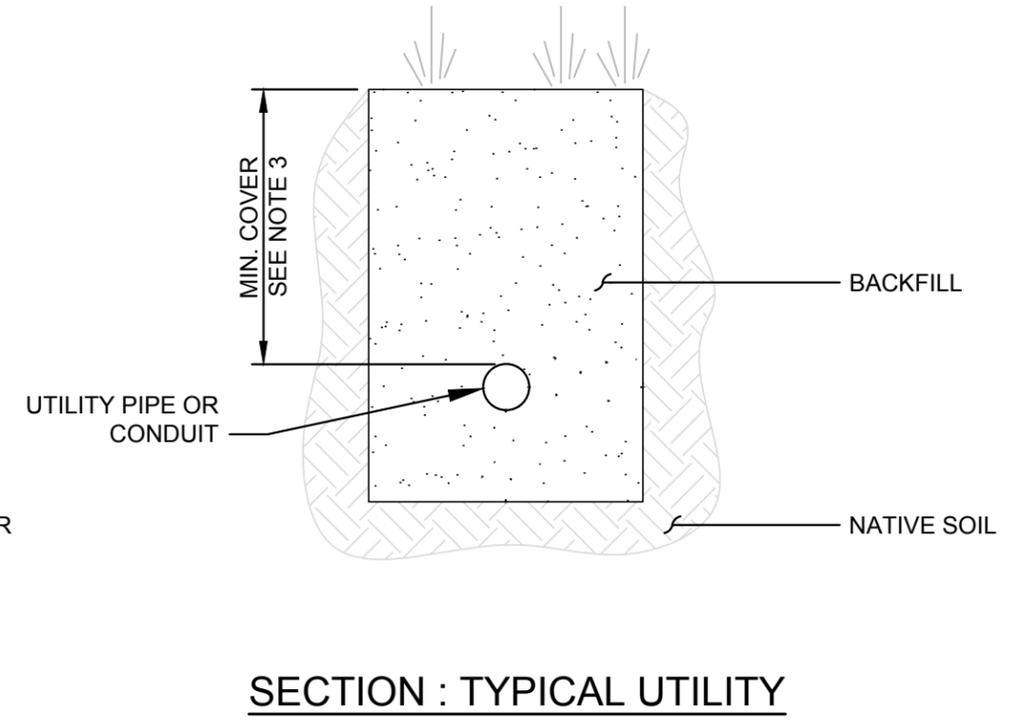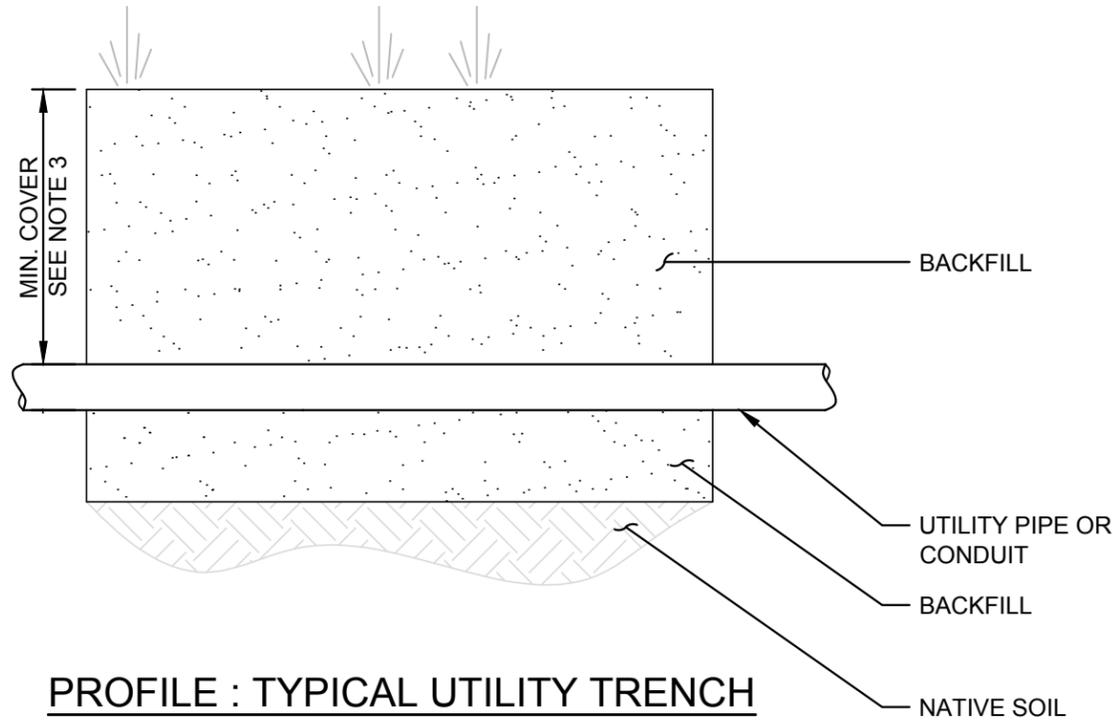

\\armgroup\cd\CompData\Projects\EnviroAnalytics\Group\160443M_EAG_TPA_Redevelopment\Drawings\Reference\Utility_Cross_Section_REV.dwg Plotted: January 11, 2018

APPENDIX I

Utility Excavation NAPL Contingency Plan

Revision 4 – June 19, 2017

Introduction:

Proposed underground utilities and excavations necessary for the redevelopment of the Tradepoint Atlantic property may encounter areas of petroleum and/or Oil & Grease contamination in soil. The assessment of total petroleum hydrocarbons (TPH) diesel range organics (DRO), gasoline range organics (GRO), Oil & Grease, and/or non-aqueous phase liquid (NAPL) completed as part of each Phase II Investigation includes the following:

- Each soil boring with evidence of NAPL (i.e., containing a sheen or free oil in the soil core), whether located near utilities or not, is investigated via the installation of a piezometer to assess mobility to groundwater. If measureable NAPL is present in the initial piezometer, additional soil borings and shallow temporary piezometers are installed surrounding the initial detection to delineate the impacts. Each piezometer installed to delineate the presence or absence of NAPL is checked with an oil-water interface probe immediately after installation, 48 hours after installation, and at least 30 days after installation.
- TPH-DRO/GRO and Oil & Grease data, once received, are assessed in their magnitude and location respective to subsurface utilities, stormwater conveyances, and surface waters.
- Locations that exhibit elevated detections of TPH/Oil & Grease or evidence of NAPL, that are within reasonable proximity (i.e. 25 feet) to subsurface utilities or stormwater conveyances and/or within reasonable proximity (i.e. 100 feet) to surface waters, are identified for further delineation and selective removal (if warranted).

Any NAPL identified in soil borings or piezometers during the Phase II Investigation would be noted on relevant logs and identified in Response and Development Work Plans for construction planning purposes. Despite these planning efforts, unidentified pockets of contamination (including NAPL) may still be encountered during construction. This contingency plan provides the procedures to be utilized during construction work to properly address response and construction techniques if any materials impacted with NAPL are encountered.

Objectives:

The purpose of this plan is to describe procedures to be followed in the event that NAPL is encountered in utility trenches or other excavations during development of the Tradepoint Atlantic property. The specific objectives of this plan and the procedures outlined herein are:

1. To ensure identification and proper management of Oil & Grease and petroleum-contaminated soils.
2. To ensure proper worker protection for working in areas of Oil & Grease and petroleum contamination.
3. To ensure that the installation of new utilities does not create new preferential flow paths for the migration of free-phase hydrocarbons (Oil & Grease, TPH-DRO/GRO, etc.) or soil vapors.

Identification of Oil & Grease and Petroleum Contaminated Soil:

An Environmental Professional (EP) will be on-site to determine if soils show evidence of the presence of Oil & Grease or TPH present as NAPL during installation of utility trenches or other excavation activities completed during development. Oil & Grease or petroleum-contaminated soils can be identified by the presence of free oil, oil staining, a petroleum odor, or any combination of these conditions. Free oil (NAPL) is liquid oil which could potentially be drained or otherwise extracted from the soil, and is the focus of this contingency plan, although severe staining accompanied by odors should be addressed via the same contingency measures provided herein (based on the judgement of the EP). The appearance of oil staining is not always consistent, but varies depending on the nature of the oil, the soil type, and the age of the release. Staining associated with old petroleum contamination often has a greenish hue, but may also be brown or black. The olfactory sense is the most sensitive instrument for identifying petroleum contamination in the field. Therefore, a petroleum odor may be noted although there is no visible sign of oil or staining. In some instances, decaying organic matter can produce an odor similar to petroleum, but this is rare.

If NAPL is encountered during construction, the extent of impacts shall be delineated by excavating trenches or installing four soil borings (two in each direction) perpendicular to the utility alignment or excavation to examine the soil for physical evidence of NAPL. Perpendicular transects will be investigated every 50 feet along the section of the utility trench or excavation where there is physical evidence of NAPL. Each transect will extend to a distance of 10 feet from the edge of the utility trench or excavation. This represents the maximum distance which would require mandatory excavation to mitigate potential migration risks (see below).

NAPL delineation will be guided primarily by screening observations from the perpendicular borings or trenches, and samples will be collected to test for extractable Oil & Grease or petroleum-contaminated soil using the Oil Sticks™ test kit. This test kit provides a determination of whether hydrocarbons are present in soil and extractable (i.e. could mobilize as a NAPL). Oil Sticks™ change from a pale blue to a deep blue color when they come in contact with free product. This instantaneous change in color occurs even when miniscule amounts of product come in contact with the strip. The sensitivity of Oil Sticks™ to determine the presence/absence of oil is reported by the manufacturer to be about 1,000 to 2,000 mg/kg. The

field test is performed by placing approximately 3 tablespoons of soil in a clean sample cup and adding enough water to cover the sample. After stirring the sample and waiting ~1 minute, the Oil Sticks™ test strip should be swished through the water, making sure to touch the strip to the sides of the cup where product may collect at the interface (meniscus) between the cup, water, and air. If the strip turns deep blue, or deep blue spots appear, oil or hydrocarbon is present. However, the MDE has observed that the Oil Sticks™ method may produce inconsistent results. Therefore, documentation of all screening methods is necessary during boring/trenching work. This documentation shall include an accurate record of visual and olfactory screening, along with a narrative with photographs. Field screening will be aided by photoionization detector (PID) results, and Oil Sticks™ samples should be biased to target elevated PID readings, if any. The agencies have requested that all soil samples prepared for the Oil Sticks™ field test be photographed for evidence of sheen/residue on the cup sides. Detailed records are required to be submitted with the project-specific Completion Report.

If petroleum or Oil & Grease impacts are identified in Site soils based on use of the Oil Sticks™ test kit or other field screening methods, disposal requirements will be determined using the quantitative PetroFLAG™ hydrocarbon analysis system or fixed laboratory analysis (see following section). The PetroFLAG™ hydrocarbon analysis system is a broad spectrum field test kit suitable for TPH contamination regardless of the source or state of degradation (Dexsil Corporation). PetroFLAG™ field test kits do not distinguish between aromatic and aliphatic hydrocarbons, but quantify all fuels, oils, and greases as TPH. Dilutions can be used to determine concentrations of TPH/Oil & Grease above the normal calibration range. Dexsil notes that positive results for TPH may occur if naturally occurring waxes and oils, such as vegetable oils, are present in the sample. Additional detail regarding the procedure for the PetroFLAG™ kit is given in **Attachment 1**.

Soil Excavation, Staging, Sampling and Disposal:

The EP will monitor all utility trenching and excavation activities for signs of potential contamination. In particular, soils will be monitored with a hand-held PID for potential VOCs, and will also be visually inspected for the presence of staining, petroleum waste materials, or other indications of NAPL contamination that may be different than what was already characterized. Excavated material that is visibly stained or that exhibits a sustained PID reading of greater than 10 ppm will be segregated and containerized or placed in a stockpile on polyethylene or impervious surface until the material can be analyzed using the PetroFLAG™ test kit to characterize the material for appropriate disposal. If a PetroFLAG™ test kit is not available to the contractor, or if the contractor prefers to use fixed laboratory analysis, samples may be characterized via submittal to a laboratory for TPH/Oil & Grease analysis. However, any excavated material containing NAPL (i.e., containing free oil) cannot be characterized for waste disposal using the PetroFLAG™ test kit and must instead be characterized via fixed laboratory analysis, as described in the final paragraph of this section. In addition, any hydrocarbon contaminated soil discovered during construction activities that was not previously

characterized must also be analyzed for PCBs prior to removal and transport to an appropriate disposal facility. If excavated and stockpiled, such materials will be covered with a plastic tarp so that the entire stockpile is encapsulated, and anchored to prevent the elements from affecting the integrity of the containment. The MDE will be notified if such materials are encountered during utility work.

Soil exhibiting physical evidence of NAPL contamination or elevated TPH/Oil & Grease with detections in the low percentage range, which is located within 10 feet of a proposed new utility or subsurface structure (i.e., foundation, sump, electrical vault, underground tank, etc.), will be excavated and segregated for disposal at the on-site nonhazardous landfill (Greys Landfill) or an off-site facility pending the completion of any required PCB analytical testing. Impacted soil which is located greater than 10 feet away from the proposed utility or subsurface structure may be left in place and undisturbed. The extent of the excavation will be determined in the field following visual/olfactory screening supplemented by the PID and Oil Sticks™ test kit, but soil disposal requirements will be determined with the PetroFLAG™ test kit (since the Oil Sticks™ method is not quantitative) or via fixed laboratory analysis for TPH/Oil & Grease (if preferred by the contractor or if the PetroFLAG™ test kit is unavailable to the contractor).

Any recovered NAPL will be collected for off-site disposal. As required by the appropriate and MDE approved facility, samples impacted by NAPL (i.e., containing free oil) will be collected for profiling/waste characterization and submitted to a fixed laboratory, as mentioned above, for the following analyses: metals, VOCs, TPH-DRO/GRO, and/or additional analysis required by the selected disposal facility. Upon receipt of any additional characterization analytical results, the MDE will be notified of the proposed disposal facility. Non-impacted material with no evidence of NAPL (i.e. soils that may contain measureable concentrations of TPH/Oil & Grease but below percentage levels) may be placed on the Site in areas to be paved or capped as long as all other requirements specified in the Response and Development Work Plan (or similar governing document) are met.

Initial Reporting:

If evidence of NAPL in soil or groundwater is encountered during excavation, it will be reported to the MDE within two hours. Information regarding the location and characteristics of any NAPL contaminated soil will be documented as follows:

- Location (exact stationing);
- Extent of contamination (horizontally and vertically – prepare a sketch including dimensions);
- Relative degree of contamination (i.e. free oil with strong odor vs. staining); and
- Visual documentation (take photographs and complete a photograph log)

Utility Installations in Impacted Areas:

Underground piping or conduits installed through areas of Oil & Grease or petroleum contamination shall be leak proof and water tight. All joints will be adequately sealed or gasketed, and pipes or conduits will be properly bedded and placed to prevent leakage. All trench backfill will meet the MDE definition of clean fill, or otherwise be approved by the MDE. Pipe bedding will be installed to minimize the potential for accumulation of water and concentrated infiltration. This can be achieved by using a relatively small amount of low-permeability pipe bedding; open-graded stone will be avoided or only used in thicknesses of 6 inches or less. Bedding must be properly placed and compacted below the haunches of the pipe. Clay, flowable fill, or concrete plugs will be placed every 100 feet across any permeable bedding to minimize the preferential flow and concentration of water along the bedding of such utilities.

If required, each trench plug will be constructed with a 2-foot-thick clay plug or 1-foot-thick flowable fill or concrete plug, perpendicular to the pipe, which extends at least 1 foot in all directions beyond the permeable pipe bedding. The plug acts as an anti-seep collar, and will extend above the top of the pipe. Installation of each trench plug will follow the completion of the trench excavation, installation of granular pipe bedding (because dense-graded aggregate or soil or other pipe bedding is difficult to properly compact below the haunches of the pipe), and seating of the pipe. The trench plug will then be installed by digging out a 1-foot trench below and around the pipe corridor, and placing clay, flowable fill, or concrete to construct the plug. A specification drawing for installation of the trench plug has been provided as **Figure 1**.

Attachment 1 - PetroFLAG™ Procedure

PetroFLAG™ field test kits use a proprietary turbidimetric reaction to determine the TPH concentration of solvent extracted samples (USEPA). Calibration standards provided with the unit are used to perform a two-point calibration for the PetroFLAG™. A blank and a 1,000 ppm standard are run by the analyzer unit to create an internal calibration curve.

Analysis of a soil sample is performed using three simple steps: extraction, filtration, and analysis. The PetroFLAG™ analysis is performed as follows:

- Place a 10 gram soil sample in a test tube.
- Add extraction solvent to the tube.
- Shake the tube intermittently for four minutes.
- Filter the extract into a vial that contains development solution
- Allow the solution to react for 10 minutes.

The filtration step is important because the PetroFLAG™ analyzer measures the turbidity or "optical density" of the final solution. Approximately 25 samples can be analyzed per hour. The vial of developed solution is placed in the meter, and the instrument produces a quantitative reading that reveals the concentration of hydrocarbons in the soil sample. The PetroFLAG™ method quantifies all fuels, oils, and greases as TPH between 15 and 2000 ppm (Dexsil Corporation). A 10x dilution of the filtered extraction solvent will be completed to allow for quantification of soil concentrations in excess of 10,000 ppm. The specially designed PetroFLAG™ analyzer allows the user to select, in the field, the response factor that is appropriate for the suspected contaminant at each site. Vegetable-based oils have been shown to exhibit a response factor of 18% (EPA Method 9074). Using the selected response factor, the analyzer compensates for the relative response of each analyte and displays the correct concentration in parts per million (ppm).

References:


U.S. Environmental Protection Agency (EPA). Contaminated Site Clean-up Information (Clu-IN): Test Kits. Office of Superfund Remediation and Technology Innovation. <http://www.clu-in.net/characterization/technologies/color.cfm>

Dexsil Corporation. 2016. PetroFLAG Analyzer System (PF-MTR-01). http://www.dexsil.com/products/detail.php?product_id=23


EPA SW-846 Method Number 9074 - Turbidimetric Screening Procedure for Total Recoverable Hydrocarbons in Soil

GENERAL NOTES:

1. ALL PIPES OR CONDUIT PASSING THROUGH AREAS OF PETROLEUM CONTAMINATION SHALL BE LEAK-PROOF AND WATERTIGHT. ALL JOINTS SHALL BE SEALED OR GASKETED.
2. ALL PIPES SHALL BE PROPERLY PLACED AND BEDDED TO PREVENT MISALIGNMENT OR LEAKAGE. PIPE BEDDING SHALL BE INSTALLED IN SUCH A MANNER AS TO MINIMIZE THE POTENTIAL FOR ACCUMULATION OF WATER AND CONCENTRATED INFILTRATION.
3. ANTI-SEEP COLLARS FROM THE PIPE MANUFACTURER, THAT ARE PRODUCED SPECIFICALLY FOR THE PURPOSE OF PREVENTING SEEPAGE AROUND THE PIPE, ARE ACCEPTABLE IF INSTALLED IN STRICT ACCORDANCE WITH THE MANUFACTURER'S RECOMMENDATIONS, AND ONLY WITH PRIOR APPROVAL BY EAG.
4. MINIMUM COVER ABOVE UTILITY SHALL BE BASED ON SPECIFIC UTILITY REQUIREMENTS.
5. TRENCHES SHALL BE BACKFILLED WITH BEDDING AND MATERIALS APPROVED BY MDE.
6. FOR ADDITIONAL REQUIREMENTS, INCLUDING THE USE OF MDE VCP CLEAN FILL FOR INDUSTRIAL LAND USE AND INSTALLATION OF GEOTEXTILE MARKER FABRIC, REFER TO NOTE 5 ON THE TYPICAL UTILITY CROSS SECTIONS.
7. ALL UTILITIES INSTALLED THROUGH AREAS CONTAINING NAPL OR ELEVATED CHEMICAL IMPACTS WITH THE POTENTIAL TO TRANSMIT VAPORS ALONG PREFERENTIAL FLOW PATHWAYS SHALL BE EITHER 1) BACKFILLED WITH LOW PERMEABILITY BACKFILL MATERIAL (LESS THAN OR EQUAL TO THE PERMEABILITY OF THE EXISTING SUBGRADE), OR 2) INSTALLED WITH TRENCH PLUGS ALONG THE ALIGNMENT IN ACCORDANCE WITH THE DETAILS SHOWN ON THIS PLAN AND THE FOLLOWING NOTES:
 - A.) UTILITY TRENCH PLUGS SHALL BE INSTALLED AT 100-FOOT (MAX.) INTERVALS THROUGH ALL AREAS OF NAPL CONTAMINATION.
 - B.) UTILITY TRENCH PLUGS SHALL EXTEND A MINIMUM OF 1-FOOT IN ALL DIRECTIONS BEYOND ANY HIGHER PERMEABILITY BACKFILL MATERIALS (I.E., MATERIALS EXCEEDING THE PERMEABILITY OF THE EXISTING SUBGRADE).

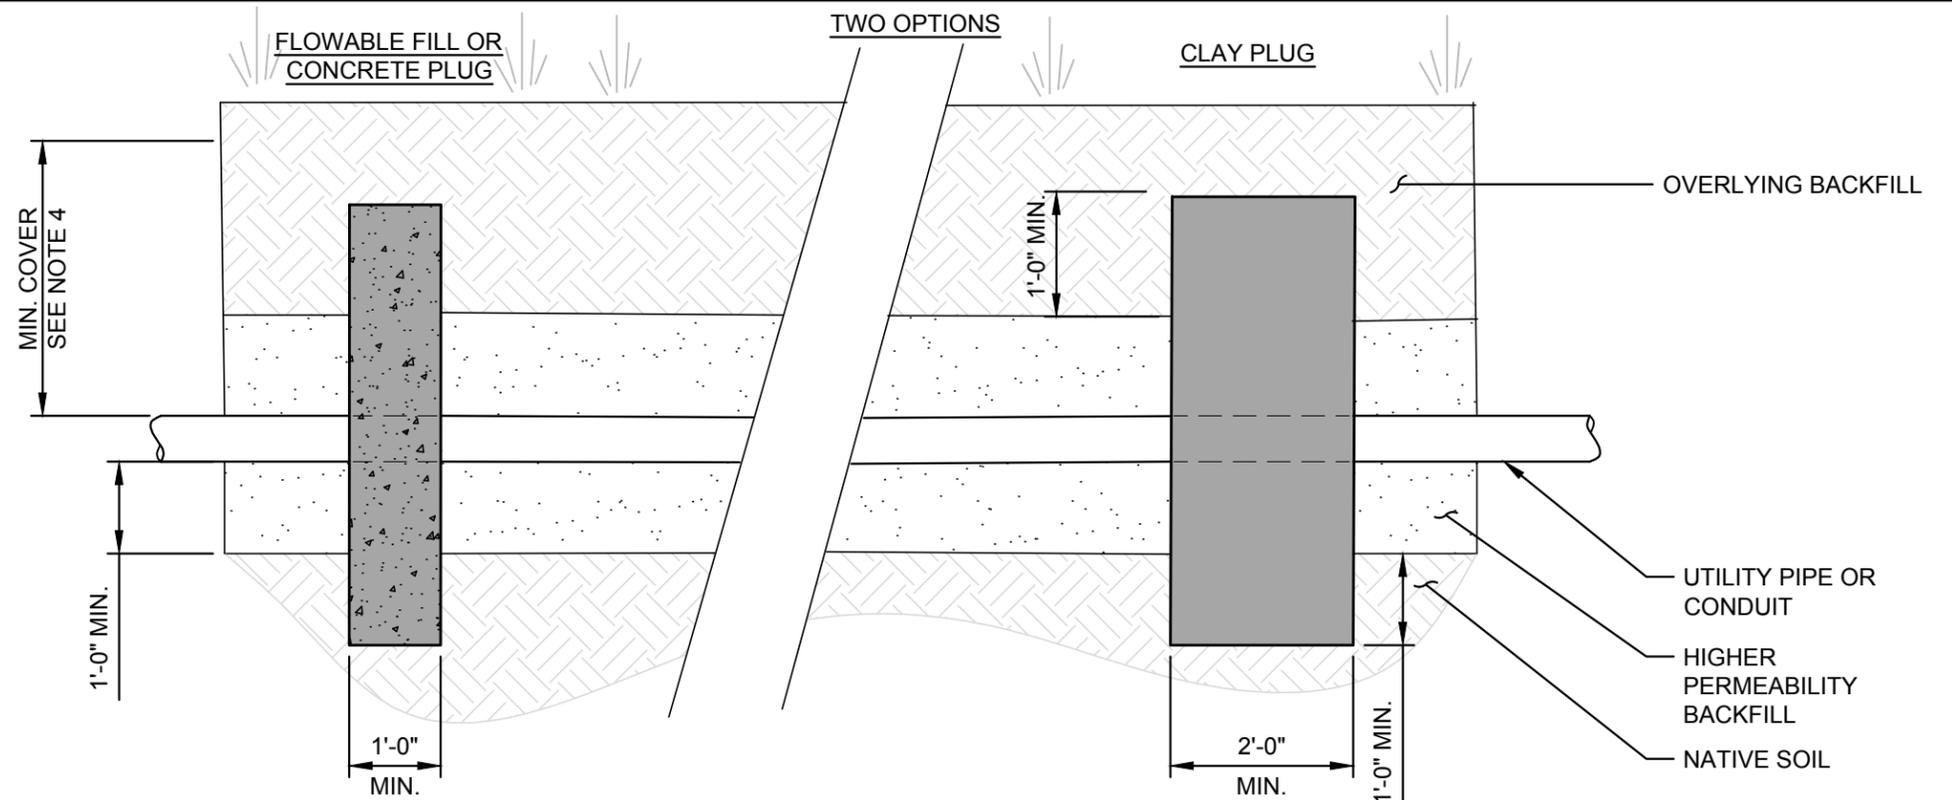

SECTION : TYPICAL UTILITY TRENCH PLUG

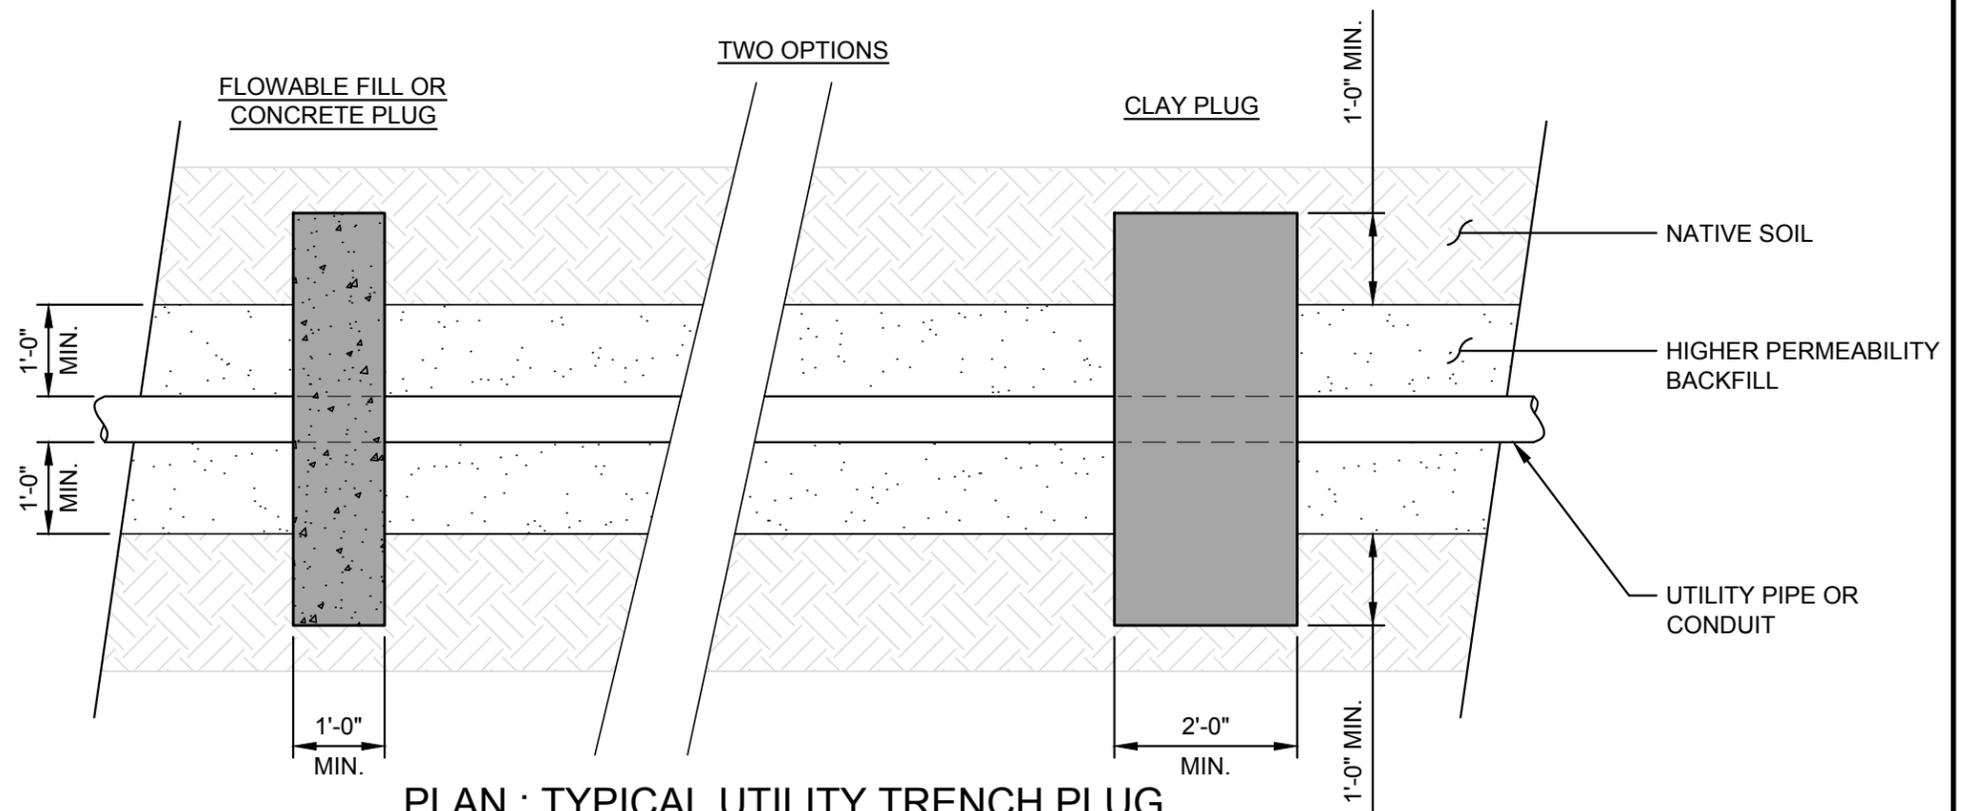

PLAN : TYPICAL UTILITY TRENCH PLUG

This drawing, its contents, and each component of this drawing are the property of and proprietary to ARM Group Inc. and shall not be reproduced or used in any manner except for the purpose identified on the Title Block, and only by or on behalf of this client for the identified project unless otherwise authorized by the express, written consent of ARM Group Inc.

P:\EnviroAnalytics Group\160443M EAG_TPA Redevelopment\Drawings\NAPL_Contingency\SK01_Utility Trench Plug_rev2.dwg Plotted: September 24, 2018

APPENDIX J

HEALTH AND SAFETY PLAN

SPARROWS POINT TERMINAL SPARROWS POINT, MARYLAND

Prepared by:



Environmental Engineers

January 2015

TABLE OF CONTENTS

1.0	Introduction.....	5
1.1	Background.....	5
1.2	Historic Operations.....	5
2.0	Purpose, Scope and Organization.....	6
2.1	Scope.....	6
2.2	Organization of Documents.....	7
2.3	EAG Health and Safety Personnel.....	7
3.0	Hazard Analysis.....	8
3.1	Hazard Analysis.....	8
3.1.1	Chemical Hazards.....	8
3.1.2	Physical Hazards.....	8
3.1.3	Biological Hazards.....	9
4.0	Health Hazard Information.....	9
4.1	Chemical Hazards.....	9
4.2	Physical Hazards.....	14
4.2.1	Heat Stress.....	14
4.2.2	Cold Stress.....	16
4.2.3	Lifting Hazards.....	16
4.2.4	Slips, Trips and Falls.....	17
4.2.5	Buried Hazards.....	17
4.2.6	Electrical Hazards.....	17
4.2.7	Heavy Equipment Operations.....	17
4.2.8	Drilling and Excavation Safety.....	18
4.2.9	Use of Hand Tools and Portable Power Tools.....	21
4.2.10	Noise.....	21
4.2.11	Work Zone Traffic Control.....	21
4.2.12	Work Over Water.....	21
4.2.13	Vehicle Use.....	22
4.3	Biological Hazards.....	22

5.0	Personal Protective Equipment.....	23
5.1	Level D Protection.....	23
5.2	Modified Level D Protection.....	23
5.3	Level C Protection.....	23
5.4	First Aid, Emergency and Safety Equipment.....	24
6.0	Personnel Training and Standard Safety Procedures.....	24
6.1	Onsite Safety, Health and Emergency Response Training.....	24
6.2	Standard Safety Procedures.....	25
6.2.1	General Safety Work Practices.....	25
6.2.2	Hand Safety.....	25
6.2.3	Respiratory Protection.....	26
6.2.4	Personal Hygiene Practices.....	27
6.2.5	Electrical Safety.....	27
6.2.6	Fire Safety.....	27
6.2.7	Illumination.....	27
6.2.8	Sanitation.....	28
7.0	Exposure Monitoring Plan.....	28
7.1	Air Monitoring.....	28
7.1.1	Combustible Gas and Oxygen Deficiency/Excess Monitoring.....	28
7.1.2	Organic Vapor Concentrations.....	29
7.2	Physical Conditions Monitoring.....	30
8.0	Medical Surveillance.....	30
8.1	Medical Surveillance Program.....	30
8.2	Physician Review.....	33
9.0	Site Control Measures and Decontamination.....	31
9.1	Site Control Measures.....	31
9.1.1	Work Zone Delineation.....	31
9.1.2	Communications.....	32
9.1.3	Site Security.....	32

9.2	Decontamination Procedures.....	33
9.2.1	Personal Decontamination.....	33
9.2.2	Equipment Decontamination.....	33
9.2.3	Waste Management.....	34
10.0	Emergency Response and Contingency Procedures.....	34
10.1	Emergency Phone Numbers.....	35
10.2	Injury/Illness Treatment.....	35
10.3	Occupational Health Clinic and Hospital Information.....	36
10.4	Accident and Emergency Medical Response.....	38
10.4.1	Chemical Exposure.....	38
10.4.2	Decontamination During Medical Emergency.....	38
10.4.3	Small or Incipient Fire.....	39
10.4.4	Large Fire or Explosion.....	39
10.4.5	Adverse Weather Conditions.....	39
10.4.6	First Aid for Heat Stress/Cold Stress.....	40
10.4.7	Snake Bites.....	40
10.4.8	Animal Bites.....	40
10.4.9	Insect Bites and Stings.....	41
10.4.10	Poisonous Plants.....	41
10.4.11	Ticks.....	41

ATTACHMENTS

Attachment A – EAG Acknowledgment Form

Attachment B – MSDSs

1.0 INTRODUCTION

1.1 Background

The Sparrows Point Terminal site has historically been a steel making facility. It is located in Baltimore County, Maryland in the southeast corner of the Baltimore metropolitan area (approximately 9 miles from the downtown area), on the Sparrows Point Peninsula in the Chesapeake Bay watershed. The facility occupies the entire peninsula and is bounded to the west by Bear Creek; to the south by Patapsco River; and to the east by Jones Creek, Old Road Bay and residential areas of the City of Edgemere. The facility is bounded to the north by the Sparrows Point Country Club. The site is approximately 3,100 acres in size.

Pennsylvania Steel built the furnace at Sparrows Point in 1887 and the first iron was cast in 1889. Bethlehem Steel Corporation (BSC) purchased the facility in 1916 and enlarged it by building additional and plating facilities. BSC filed for bankruptcy in 2001. A series of entities has owned the site between then and now: the International Steel Group (ISG), Mittal Steel, ISG Sparrows Point, LLC, Severstal Sparrows Holding LLC, which was renamed to Severstal Sparrows Point, LLC, RG Steel Sparrows Point, LLC, and then a joint venture to Sparrows Point LLC (SP) and HRE Sparrows Point LLC. Most recently, in 2014, the property and assets were sold to Sparrows Point Terminal LLC (SPT). Environmental liability was retained by SP and work is currently being conducted by EnviroAnalytics Group, LLC (EAG) on behalf of SP.

- In addition to the current environmental investigation and remediation being conducted onsite by EAG and their consultants, there are other entities conducting work on the facility. Demolition of the remaining structures is currently ongoing at the site, and those contractors are being managed by SPT.
- The purpose of this document is to provide an overall health and safety plan (HASP) for EAG personnel and EAG directed contractors who are engaging in environmental investigation and remediation activities onsite. EAG directed contractors will also be expected to have their own Health and Safety Program, and they may opt to draft their own site specific HASP, provided it meets the requirements in this HASP.

1.2 Historic Operations

Steel manufacturing involves handling vast amounts of raw material including coke, iron ore, limestone and scrap steel, as well as recovering byproducts and managing waste materials. The operations listed below either were or are currently performed at the Sparrows Point Facility.

- Iron and steel production
- Coal chemical recovery system
- Other byproducts recovery systems
- Wastewater treatment systems
- Solid waste management
- Air pollution control

A number of site-specific environmental and hydrogeologic investigations have been prepared for the Sparrows Point facility. For the purposes of this HASP, information was obtained from the “Special Study Area Release Site Characterization” completed in 2001 by CH2MHill, as well as additional documents submitted since that time. There are five separate Special Study Areas as put forth in the Consent Decree:

- Humphrey Impoundment,
- Tin Mill Canal/Finishing Mills Areas,
- Coke Oven Area,
- Coke Point Landfill, and
- Greys Landfill.

Contaminated soils and groundwater may be present at the site. This plan was prepared based on an assessment of hazards expected to be present and a review of data from the previous site investigations and groundwater sampling events.

During the current investigations and remedial efforts, all related work will be performed in accordance with the requirements of this HASP and Occupational Safety and Health Administration (OSHA) regulations as defined in 29 Code of Federal Regulations (CFR) 1910.120 and 1926.65.

2.0 PURPOSE, SCOPE AND ORGANIZATION

This section describes the purpose, scope and organization of this HASP and the health and safety responsibilities of EAG, their employees, and their subcontractors involved in the field investigation and remediation activities at the Sparrows Point facility.

2.1 Scope

Field investigation and remediation activities for this project may include, but are not limited to:

- Groundwater sampling and monitoring,
- Groundwater and remediation well installation,
- Groundwater and remediation well repairs,
- Groundwater and remediation well closure and abandonment,
- Surface water sampling,
- Sediment sampling,
- Soil boring and subsurface soil sampling,
- Soil excavations for remedial purposes,
- Installation and operation of remediation systems for soil, soil vapor, and groundwater,
- Decommissioning and closure of remediation systems,
- Soil excavations for remedial purposes,
- Insitu soil mixing/soil stabilization,
- Exsitu soil mixing/soil stabilization,
- Dredging operations along Tin Mill Canal,
- Insitu chemical and/or biological injections, and
- Recovery of non-aqueous phase liquids (NAPL)

When EAG personnel are providing oversight of subcontractors, they will attend the safety and health briefings held by the contractor. EAG personnel will follow the requirements of this HASP, as well as any potentially more stringent requirements of the contractor’s health and safety plan.

When EAG personnel are conducting tasks on their own, with or without subcontractors, they will follow the requirements of this HASP. EAG contractors, such as drillers, will also be required to follow the requirements of this HASP, as well as any more stringent requirements of the contractor’s health and safety plan.

All EAG field personnel, including subcontractors to EAG, will be required to read and understand this HASP and agree to implement its provisions. All site personnel will sign the Acknowledgement Form included in **Attachment A** stating that they have read, understood, and agree to abide by the guidelines and requirements set forth in this plan.

2.2 Organization of Document

This HASP includes health and safety procedures for all generally anticipated project field activities. This plan also meets the OSHA requirements contained in the CFR, specifically 29 CFR 1910.120 and 29 CFR 1926, by including the following items:

- A description of staff organization, qualifications and responsibilities (Section 2.3),
- Hazard analysis (Section 3.0),
- Health hazard information (Section 4.0),
- Personal protective equipment (PPE), including available first aid, emergency, and safety equipment (Section 5.0),
- Employee and subcontractor training and standard safety procedures (section 6.0),
- Exposure monitoring plan (Section 7.0),
- Medical surveillance (Section 8.0),
- Site control measures and decontamination procedures for personnel and equipment (Section 9.0),
- Emergency response and contingency procedures (section 10.0), and
- Material Safety Data Sheets (MSDSs) for chemicals used on-site (**Attachment B**).

2.3 EAG Health and Safety Personnel

Personnel responsible for implementing this HASP include:

EAG Contacts for Sparrows Point Project Work	
VP Remediation, Russ Becker	(314) 686-5611
Senior Project Manager, James Calenda	(314) 620-3056
Senior Project Engineer, Elizabeth Schlaeger	(314) 307-1732
Josh Burke – Field Operations Manager	(314) 686-5623
Project Field Team Members, Jeff Wilson and Bill Trentzsch	(314) 620-3135, (314) 686-5598

3.0 HAZARD ANALYSIS

This section outlines the potential hazards related to the field activities listed in Section 2.1.

3.1 Hazard Analysis

The field activities planned for this project pose potential health and safety hazards for field team members. This section describes the hazards associated with the above-listed field activities. Detailed chemical, physical, and biological hazards information is provided in Section 4.0 (Health Hazard Information).

Hazards to which employees and subcontractors may be exposed to as a result of the above-listed activities include potential chemical exposures, lacerations, excessive noise, thermal stress, lifting of excessive weight or bulk, hand tools and heavy equipment, drilling and slips, trips and falls.

3.1.1 Chemical Hazards

Potential exposures to chemicals in the soil or groundwater include the possibility of dermal exposure (contact and/or absorption), inhalation of chemical contamination that may be encountered during sampling or during equipment decontamination activities, or ingestion of contaminants if good personal hygiene practices are not followed.

Benzene, naphthalene, and various metals are the major contaminants that have been identified in groundwater during previous investigations at the site. In addition, light NAPL (LNAPL – benzene, in particular) and dense NAPL (DNAPL – naphthalene, in particular) have also been identified or are heavily suspected in various locations in the Coke Oven Area. Dissolved metals the chemicals of concern primarily located in the area of Tin Mill Canal and the Rod and Wire Mill Area. Treatment chemicals, such as sulfuric acid, are currently being used in remediation systems. All appropriate MSDS sheets will be reviewed that apply to the investigation or remedial tasks being conducted. MSDS sheets are located in **Attachment B**. It should be noted that this is a dynamic document: should any additional chemicals be introduced or discovered, the MSDS sheets will be added to **Attachment B**, as necessary.

3.1.2 Physical Hazards

The potential physical hazards associated with field activities include:

- Excessive lifting
- Slips, trips, and falls
- Working at heights
- Exposure to extreme outside temperatures and weather
- Equipment hazards
- Drilling Hazards
- Noise
- Dust and fumes
- Injury from tools, equipment, rotating parts
- Electrical hazards
- Buried and overhead hazards
- Work over water
- Driving to, from, and around the site (including working in trafficked areas)

Additional hazards may be encountered based on the various task at hand. It will be the responsibility of the site manager, with the help of field staff, to identify and address any additional hazards on a “per task or job” basis. A Job Safety Analyses (JSA) may need to be conducted prior to the start of various tasks. Safety meetings will be conducted with all staff in attendance, before the start of any new task or when any significant personnel or other changes (such as a swift change in weather, for example) occur. Updated information relating to physical hazards will be presented during these meetings in an effort to familiarize the crew with potential hazards, discuss new situations, and determine how the associated risks can be reduced. Further, good housekeeping practices will be enforced to preclude other risks resulting from clutter and inattention to detail. In addition, internal field audits will be randomly conducted to ensure adherence to all procedures are being followed.

3.1.3 Biological Hazards

Biological hazards that may be encountered when conducting field activities include the following:

- Poisonous snakes and spiders
- Ticks and tick-borne diseases
- Stinging insects such as chiggers, bees, wasps, etc.
- Various viruses and diseases spread via animal to human contact such as West Nile virus or rabies
- Various viruses and diseases spread via human to human contact such as colds or the flu
- Dermal contact with poison ivy, oak, and/or sumac
- Bloodborne pathogens when administering first aid

First aid kits will be available on-site. It is crucial to note that any site personnel who has significant allergies should communicate that information to the field team they are working with, along with the location of their auto-injector pen (such as an Epi-Pen) for use in case of going into anaphylactic shock from something that would cause such a reaction (like a bee sting, for example). Personnel who suffer from such allergies are responsible for providing their own auto-injector devices as those are typically prescription based as well as specific to their particular allergy.

4.0 HEALTH HAZARD INFORMATION

This section provides chemical hazard information for those potentially hazardous materials expected to be present at the facility. Potential physical and biological hazards are also discussed in this section.

4.1 Chemical Hazards

Exposure to chemicals through inhalation, ingestion, or skin contact may result in health hazards to field workers. Hazards associated with exposure will be evaluated using OSHA Permissible Exposure Limits (PELs) and the American Conference of Governmental Industrial Hygienists (ACGIH) Threshold Limit Values (TLVs). Each of these values are 8-hour, time-weighted averaged (TWAs) above which an employee cannot be exposed. EAG may also use the National Institute of Occupational Safety and Health (NIOSH) Recommended Exposure Limits (RELs) where applicable. Although the OSHA PELs are the only exposure limits enforceable by law, the most stringent of exposure limits will be used as the EAG-enforced exposure criteria during field activities.

The following is a summary of the potential hazards created by the compounds that may be encountered during field activities. Data from sampling of groundwater wells was reviewed to identify potential contaminants at the site. Contaminants of concern may include benzene, toluene, ethylbenzene and xylenes (BTEX), polycyclic aromatic hydrocarbons (PAHs), phenols, metals and water treatment chemicals. Table 4-1 contains chemical information and exposure limits for various chemicals that may be expected to be present in the investigation and remediation efforts. During the recovery of NAPL, the major contaminants of concern are benzene and naphthalene. It is possible that carbon monoxide may also be encountered from the use of various internal combustion engines (vehicular or otherwise); however, it is anticipated that since any such engine will be used outdoors, it is not expected that concentrations of concern will accumulate. With the use of any such engine, the engine should be positioned such that site personnel are upwind of the engine exhaust.

If any chemicals are brought on-site, MSDS must be made available and added to **Attachment B**. Personnel must be trained in the hazards and use of chemicals.

**Table 4-1
Chemical Contaminants of Potential Concern**

Chemical Name Synonyms (trade name)	Exposure Limits	Characteristics	Route of Exposure	Symptoms of Exposure
Benzene	PEL: 1PPM REL: 0.1 CA TLV: 0.5PPM STEL: 1PPM (NIOSH) Skin: YES	Colorless to light-yellow liquid with aromatic odor. LEL: 1.2% UEL: 7.8% VP: 75mm Fl.P: 12°F	INH ABS ING CON	Irritation of eyes, skin, nose, respiratory system, giddiness, headache, nausea, fatigue, anorexia, dermatitis, bone marrow depression
Ethylbenzene	PEL: 100PPM REL: 100PPM TLV: 100PPM STEL: 125PPM IDLH: 800PPM Skin: NO	Colorless liquid with an aromatic odor. LEL: 0.85 UEL: 6.7% IP: 8.76EV VP: 7mm Fl.P: 55°F	INH ING CON	Irritation of eyes, skin, mucous membranes; headache; dermatitis
1,1 dichloroethane	PEL: 100PPM REL: 100PPM TLV: 100PPM STEL: NA IDLH: 3000PPM Skin: NO	Colorless, oily liquid with a chloroform-like odor. LEL: 6.2% UEL: 16% IP: 11.05EV Vp: 64mm Fl.P: 56°F	INH ING CON	Irritation of eyes, CNS depression, liver, kidney, lung damage
Phenol	PEL: 5PPM REL: 5PPM, 15.6PPM (C) TLV: 5PPM STEL: NA IDLH 250PPM Skin: YES	Colorless to light pink crystalline solid with a sweet, acrid odor. LEL: 1.8% UEL: 5.9% IP: 8.12EV Vp: 0.08mm Fl.P: 175°F	INH ING CON ABS	Irritated eyes, nose, throat, anorexia, weakness, muscular ache, pain, dark urine, cyanosis, liver, kidney damage, skin burns, dermatitis, tremor, convulsions, twitch
Naphthalene	PEL: 10PPM REL: 10PPM TLV: 10PPM STEL: 15PPM IDLH: 250PPM Skin: YES	Colorless to brown solid with an odor of mothballs LEL: 0.9% UEL: 5.9% IP: 8.12EV Vp: 0.08mm Fl.P: 174°F	INH ABS ING CON	Irritation of eyes, headache, confusion, excitement, malaise, nausea, vomiting, abdominal pain, irritated bladder, profuse sweating, jaundice, hematuria, renal shutdown, dermatitis, optical neuritis, corneal damage
Toluene	PEL: 200PPM, 300PPM (C) REL: 100PPM TLV: 20PPM STEL: 150PPM IDLH: 500PPM Skin: YES	Colorless liquid with a sweet, pungent benzene-like odor. LEL: 1.1% UEL: 7.1% IP: 8.82EV VP: 21MM Fl.P: 40°F	INH ABS ING CON	Irritation of eyes, nose, fatigue, weakness, confusion, euphoria, dizziness, headache, dilated pupils, lacrimation, nervousness, muscle fatigue, insomnia, dermatitis, liver, kidney damage
Xylenes	PEL: 100PPM REL: 100PPM TLV: 100PPM STEL: 150PPM IDLH: 900PPM Skin: NO	Colorless liquid with an aromatic odor. LEL: 0.9% UEL: 6.7% IP: 8.40EV VP: 5MM Fl.P: 88°F	INH ABS ING CON	Irritated eyes, nose, respiratory system, headache, fatigue, dizziness, confusion, malaise, drowsiness, incoherence, staggering gait, corneal vacuolization, anorexia, nausea, vomiting, abdominal pain, dermatitis

Chemical Name Synonyms (trade name)	Exposure Limits	Characteristics	Route of Exposure	Symptoms of Exposure
Styrene	PEL: 100PPM, 200PPM (C) REL: 50PPM TLV: 20PPM STEL: 40PPM IDLH: 700PPM Skin: NO	Colorless to yellow, oily liquid with a sweet, floral odor. LEL: 0.9% UEL: 6.8% IP: 8.40eV VP: 5MM F.I.P: 88°F	INH ABS ING CON	Irritated eyes, nose, respiratory system, headache, fatigue, dizziness, confusion, malaise, drowsiness, weakness, narcosis, dermatitis
Chlorodiphenyl (54% chlorine) (11097-69-1)	PEL: 0.5mg/m ³ REL: 0.001mg/m ³ TLV: 0.5mg/m ³ STEL: N/A IDLH: 5mg/m ³ (CA) Skin: YES	Colorless to pale yellow viscous liquid with a mild hydrocarbon odor. LEL: NA UEL: NA IP: UNKNOWN VP: 0.00006MM F.I.P: NA	INH ABS ING CON	Irritated eyes, chloracne, liver damage, reproductive effects (carcinogen)
Polynuclear aromatic hydrocarbons (PAHs) (coal tar pitch volatiles) (65996-93-2)	PEL: 0.2mg/m ³ REL: 0.1mg/m ³ TLV: 0.2 mg/m ³ STEL: N/A IDLH: 80mg/m ³ (CA) Skin: NO	The pitch of coal tar is black or dark brown amorphous residue that remains after the redistillation process. LEL: N/A UEL: N/A IP: VARIES VP: VARIES F.I.P: VARIES	INH CON	Direct contact or exposure to vapors may be irritating to the eyes. Direct contact can be highly irritating to the skin and produce dermatitis. Exposure to vapors may cause nausea and vomiting. A potential human carcinogen.
Arsenic (inorganic)	PEL: 0.01mg/m ³ REL: NONE TLV: 0.5 mg/m ³ STEL: N/A IDLH: 5mg/m ³ (CA) Skin: NO	Silver-gray or tin-white brittle odorless solid. Air odor threshold: N/D.	INH ABS CON ING	Symptoms include ulceration of nasal septum, gastrointestinal disturbances, respiratory irritation and peripheral neuropathy. Potential occupational carcinogen.
Barium	PEL: 0.5mg/m ³ REL: 0.5mg/m ³ TLV: 0.5mg/m ³ STEL: N/A IDLH: 50mg/m ³ Skin: NO	White, odorless solid. Air odor threshold: N/D.	INH ING CON	Irritated eyes, skin, upper respiratory system, skin burns, gastroenteritis, muscle spasm, slow pulse, cardiac arrhythmia
Cadmium (elemental)	PEL: 0.005mg/m ³ REL: CA TLV: 0.01mg/m ³ STEL: N/A IDLH: 9mg/m ³ (CA) Skin: NO	Silver-white, blue-tinged lustrous, odorless solid. Air odor threshold: N/D.	INH ING	Symptoms include pulmonary edema, cough, tight chest, head pain, chills, muscle aches, vomiting and diarrhea. Potential occupational carcinogen.
Chromium (Metal)	PEL: 1.0mg/m ³ REL: 0.5mg/m ³ TLV: 0.5mg/m ³ STEL: N/A IDLH: 250mg/m ³ Skin: NO	Blue-white to steel-gray lustrous, brittle, hard odorless solid. Air odor threshold: N/D.	INH ING CON	Symptoms may include irritated eyes and skin, lung fibrosis.
Chromium (Chromium III inorganic compounds)	PEL: 0.5mg/m ³ REL: 0.5mg/m ³ TLV: 0.5mg/m ³ STEL: N/A IDLH: 25mg/m ³ Skin: NO	Varies depending on specific compound.	INH ING CON	Irritation of eyes, sensitivity dermatitis

Chemical Name Synonyms (trade name)	Exposure Limits	Characteristics	Route of Exposure	Symptoms of Exposure
Copper	PEL: 1mg/m ³ REL: 1mg/m ³ TLV: 1mg/m ³ STEL: N/A IDLH: 100mg/m ³ Skin: NO	Reddish, lustrous, malleable, odorless solid	INH ING CON	Irritation of eyes, nose, pharynx, nasal septum perforations, metallic taste, dermatitis
Lead (Elemental & Inorganic as Pb)	PEL: 0.05mg/m ³ RELO.1mg/m ³ TLV: 0.05mg/m ³ STEL: N/A IDLH: 100mg/m ³ Skin: NO	A heavy, ductile soft gray solid. Air odor threshold: N/D.	INH ING CON	Accumulative poison may cause weakness, insomnia, facial pallor, anorexia, malnutrition, constipation, abdominal pain, anemia, gingival lead line, paralysis of wrists and ankles, hypertension and kidney disease.
Nickel	PEL: 1mg/m ³ REL: 0.015mg/m ³ (Ca) TLV: 0.1mg/m ³ STEL: N/A IDLH: 10mg/m ³ Skin: NO	Lustrous, silvery, odorless solid. Air odor threshold: N/A VP: 0mm	INH CON ING	Sensitivity dermatitis, allergic asthma, pneumonitis
Vanadium pentoxide dust	PEL: 0.5mg/m ³ (C) REL: 0.05mg/m ³ (C) TLV: 0.05mg/m ³ STEL: N/A IDLH: 35mg/m ³ Skin: NO	Yellow-orange powder or dark gray, odorless flakes dispersed in air. VP: 0mm	INH ING CON	Irritated eyes, skin, throat, green tongue, metallic taste, eczema, cough, fine rales, wheezing, bronchitis
Zinc oxide	PEL: 5mg/m ³ REL: 5mg/m ³ TLV: 2mg/m ³ STEL: 10mg/m ³ IDLH: 500mg/m ³ Skin: NO	White, lustrous solid	INH	Metal fume fever, chills, muscular ache, nausea, fever, dry throat, cough, weakness, metallic taste, headache, blurred vision, low back pain, vomiting, fatigue, malaise
Sulfuric Acid (water treatment chemical)	PEL: 1mg/m ³ TLV: 0.2mg/m ³ Skin: YES	Oily, colorless to slightly yellow, clear to turbid liquid	IHN ABS ING CON	Can cause irritation or corrosive burns to the upper respiratory system, lung irritation, pulmonary edema, burns to mouth throat and stomach, erode teeth, skin lesions
Antiscale (water treatment chemical)	PEL: 1mg/m ³ TLV: 0.2mg/m ³ Skin: YES	Liquid, colorless, clear	IHN ABS ING CON	May cause severe skin burns and eye damage, can cause cancer, fatal if inhaled, may damage organs through prolonged exposure
Antifoam (water treatment chemical)	N/E	Liquid emulsion, white, opaque	IHN ABS ING CON	May be harmful to skin, if inhaled and if swallowed
Gases				
Carbon Monoxide	PEL: 50PPM REL: 35PPM TLV: 25PPM STEL: 200PPM (C) IDLH: 1200PPM Skin: NO	Colorless, odorless gas LEL: 12.5% UEL: 74% IP: 14.01eV VP: >35atm FI.P: N/A	INH	Headache, rapid breathing, nausea, tiredness, dizziness, confusion

NOTES:

OSHA PEL	Occupational Safety and Health administration Final Rule Limits, Permissible Exposure Limit for an eight-hour, time-weighted average
ACGIH TLV	American Conference of Governmental Industrial Hygienists, Threshold Limit Value for eight-hour, time-weighted average
STEL	Short-term Exposure Limit for a 15-minute, time-weighted average
NIOSH IDLH	National Institute for Occupational Safety and Health, Immediately Dangerous to Life or Health concentration
PPM	Part of vapor or gas per millions parts of air by volume at 25°Celsius and 760mm Hg mg/m ³ (milligram of substance per cubic meter of air)
CA	NIOSH has identified numerous chemicals that it recommends to be treated as potential or confirmed human carcinogens.
(C)	The (ceiling) concentration that should not be exceed during any part of the working exposure.
Skin	Refers to the potential contribution to the overall exposure by the cutaneous (absorption) route, including mucous membranes and eye, either by airborne or more particularly by direct contact with the substance.
UEL	Upper Explosive Limit – the highest concentration of a material in air that produces an explosion in fire or ignites when it contacts an ignition source.
LEL	Lower Explosive Limit – the lowest concentration of the material in air that can be detonated by spark, shock, fire, etc.
INH	Inhalation
ABS	Skin absorption
ING	Ingestion
CON	Skin and/or eye contact

4.2 Physical Hazards

Field employees and subcontractors may be exposed to a number of physical hazards during this project. Physical hazards that may be encountered include the following:

- Heat and cold stress
- Lifting hazards
- Slips, trips and falls
- Working around heavy equipment
- Drilling hazards
- Noise
- Use of hand and power tools
- Buried hazards
- Electrical hazards
- Underground and overhead utilities
- Working over water
- Travel to and from site

4.2.1 Heat Stress

Local weather conditions may produce an environment that will require restricted work schedules in order to protect employees from heat stress. The Project Manager or the Field Lead Team Member will observe workers for any potential symptoms of heat stress. Adaptation of work schedules and training on recognition of heat stress conditions should help prevent heat-related illnesses from occurring. Heat stress controls will be stated at 70°F for personnel in protective clothing and at 90°F for personnel in regular work clothing. Heat stress prevention controls include:

- Allow workers to become acclimatized to heat (three to six days)
- Provide rest breaks in a shaded or air-conditioned break area
- Provide sun screen to prevent sun burn
- Provide drinking water and electrolyte-replenishing fluids
- Keep ice readily available to rapidly cool field team members

The following Heat Stress Index should be used as a guide to evaluate heat stress situations. If the Heat Stress exceeds 105 degrees Fahrenheit, contact the project manager prior to conducting work for detailed guidance.

Heat Stress Index									
Temp. °F	Relative Humidity								
	10%	20%	30%	40%	50%	60%	70%	80%	90%
105	98	104	110	120	132				
102	97	101	108	117	125				
100	95	99	105	110	120	132			
98	93	97	101	106	110	125			
96	91	95	98	104	108	120	128		
94	89	93	95	100	105	111	122		
92	87	90	92	96	100	106	114	122	
90	85	88	90	92	96	100	106	114	122
88	82	86	87	89	93	95	100	106	115
86	80	84	85	87	90	92	96	100	109
84	78	81	83	85	86	89	91	95	99
82	77	79	80	81	84	86	89	91	95
80	75	77	78	79	81	83	85	86	89
78	72	75	77	78	79	80	81	83	85
76	70	72	75	76	77	77	77	78	79
74	68	70	73	74	75	75	75	76	77

NOTES: Add 10° F when protective clothing is being used; Add 10° F when in direct sunlight

HSI Temp	Category	Injury Threat
Above 130° F	Extreme Danger	No work unless emergency exists. Contact Cardno ATC RSC and Corporate Risk Management Department prior to proceeding. Heat cramps or exhaustion likely, heat stroke possible if exposure is prolonged and there is physical activity.
105° to 130° F	Danger	Contact RSC prior to proceeding. Requires strict adherence to ACGIH Heat Stress Guidelines, including use of on-site WBGT equipment. Heat cramps or exhaustion likely, heat stroke possible if exposure is prolonged and there is physical activity.
90° to 105° F	Extreme Caution	Heat cramps or exhaustion likely, heat stroke possible if exposure is prolonged and there is physical activity.
80° to 90° F	Caution	Heat cramps or exhaustion likely, heat stroke possible if exposure is prolonged and there is physical activity.
Below 80° F	Normal Range	Typical conditions for time of year. Little or no danger under normal circumstances. As always, anticipate problems and work safely.

4.2.2 Cold Stress

Frostbite and hypothermia are two types of cold injury that personnel must be protected against during the performance of field duties. The objective is to prevent the deep body temperature from falling below 96.8° F and to prevent cold injury to body extremities. Two factors influence the development of a cold injury the ambient temperature, and wind velocity. Reduced body temperature will very likely result in reduced mental alertness, reduction in rational decision making, and/or loss of consciousness with the threat of death.

-

Use appropriate cold weather clothing when temperatures are at or below 40° F as exposed skin surfaces must be protected. These protective items can include facemask, hand wear, and foot wear. Workers handling evaporative solvents during cold stress conditions will take special precautions to avoid soaking gloves and clothing because of the added danger of prolonged skin contact and evaporative cooling. Personnel will wear protective clothing appropriate for the level of cold and planned physical activity. The objective is to protect all parts of the body, with emphasis on the hands and feet. Eye protection against glare and ultraviolet light should be worn in snowy and icy conditions.

The work rate should not be so great as to cause heavy sweating that could result in wet clothing. If heavy work must be done, opportunities for rest breaks will be provided where workers have the opportunity to change into dry clothing. Conversely, plan work activities to minimize time spent sitting or standing still. Rest breaks should be taken in a warm, dry area. Windbreaks can also be used to shield the work area from the cooling effects of wind.

If extreme cold-related weather conditions occur, EAG field personnel and subcontractors will take the following precautions:

- Wear adequate insulated clothing when the air temperature drops below 40°F
- Reduce work periods in extreme conditions to allow adequate rest periods in a warm area
- Change clothes when work clothes become wet
- Avoid caffeine (which has diuretic and circulatory effects)

4.2.3 Lifting Hazards

Field personnel may be exposed to injury caused by lifting heavy objects and various pieces large or unwieldy pieces of equipment. All field team members will be trained in the proper methods for lifting heavy and/or large equipment and are cautioned against lifting objects that are too heavy or too big for one person. Proper lifting techniques include the following:

- Keep feet approximately shoulder width apart
- Bend at the knees
- Tighten abdominal muscles
- Lift with the legs
- Keep the load close to the body
- Keep the back upright
- Use the buddy system for larger or heavy pieces of equipment

All drums will be staged using an approved drum dolly or other appropriate equipment. Proper care will be taken in the use of this equipment. Healthy employees with no medical restrictions may lift and carry a maximum of 50 pounds using proper lifting and carrying techniques. This recommended weight limit may be reduced depending on physical and workplace factors.

4.2.4 Slips, Trips and Falls

The most common hazards that will be encountered during field activities will be slips, trips and falls. Field team members are trained to use common sense to avoid these hazards such as using work boots/safety shoes with nonskid soles. When working on slippery surfaces, tasks will be planned to decrease the risk of slipping via avoiding the slippery areas, if possible, or utilizing engineering controls. Engineering controls may involve the placement of supplemental material such as boards, gravel, or ice melt should be utilized to mitigate slippery conditions. Other engineering controls may involve the use of footwear traction control devices. Employees and subcontractors will avoid slippery surfaces, use engineering controls as appropriate, not hurry, and maintain good housekeeping.

4.2.5 Buried Hazards

Whenever the ground is penetrated, the potential for contacting buried hazards exists. During the planning/mobilization phase, prior to drilling or other excavation activities, EAG personnel and/or their contractors will establish the location of underground utility lines (gas, electrical, telephone, fiber optic cable, etc.) and/or substructures or other potential buried hazardous items. This may be conducted by review of historic utility and substructure maps, private utility locates, ground penetrating radar, or other technologies. If there is any evidence of utilities or subsurface objects/structures, drilling or excavation activities may be offset. If activities cannot be offset, measures will be taken to remove, disconnect, and/or protect the utilities and/or subsurface structures and/or objects. Every reasonable effort will be made to clear the area of intrusive work prior to fieldwork being started.

4.2.6 Electrical Hazards

It may be possible that overhead power lines will be in proximate locations during drilling or excavation activities. At least a 20 foot clearance must be maintained from overhead power lines. No equipment such as drill rigs or dump trucks can be moved while masts or buckets are in the upright position. Field personnel and subcontractors performing electrical work are required to be appropriately trained to work on the electrical systems in question prior to start of work. Authorization from project management personnel is required prior to any electrical work or work near overhead power lines. . When using extension cords, all field workers will ensure that they are in good working condition, are correctly rated for use, and do not contain abrasions such that bare wires could be exposed to the environment. Extension cords will not be used in wet areas without plugging the extension cord into a ground fault circuit interrupter (GFCI). GFCIs will detect a short circuit and cut power.

4.2.7 Heavy Equipment Operations

Heavy equipment must be operated in a safe manner and be properly maintained such that operators and ground personnel are protected.

Requirements for Operators

- Only qualified, trained, and authorized operators are allowed to operate equipment
- Seat belts will be used at all times in all equipment and trucks
- Operators will stop work whenever ground personnel or other equipment enter their work area; work will resume only when the area has been cleared
- No personnel may ride on equipment other than the Authorized Operator
- No personnel may be carried or lifted in the buckets or working “arms” of the equipment
- Spotters will be used when ground personnel are in the vicinity of heavy equipment work areas and/or when an operator is backing equipment near other structures or congested area

Requirements for Ground Personnel

- All ground personnel must wear orange protective vests in work areas with any operating heavy equipment
- Ground personnel will stay outside of the swing zone or work area of any operating equipment
- Ground personnel may only enter the swing or work area of any operating equipment when:
 - They have attracted the operators attention and made eye contact
 - The operator has idled the equipment down and grounded all extensions
 - The operator gives the ground personnel permission to approach
- Ground personnel shall never walk or position themselves between any fixed object and running equipment or between two running pieces of equipment

Equipment

- Maintain operations manuals at the site for each piece of equipment that is present and in use
- Ensure operators are familiar with the manual for the equipment and operate the equipment within the parameters of the manual
- Ensure all equipment is provided with roll-over protection systems
- Verify that seatbelts are present and functional in all equipment
- Prohibit the use of equipment that has cab glass which is broken or missing
- Ensure that backup alarms are functional on all trucks and equipment
- Require all extensions such as buckets, blades, forks, etc. to be grounded when not in use
- Require brakes to be set and wheels chocked (when applicable) when not in use

Daily inspections of equipment are required using a Daily Heavy Equipment Safety Checklist. Equipment deemed to be unsafe as a result of daily inspection will not be used until required repairs or maintenance occurs. During maintenance/repair, ensure that motors are turned off, all extensions are grounded or securely blocked, controls are in a neutral position, and the brakes are set.

4.2.8 Drilling and Excavation Safety

Prior to any intrusive work, as previously mentioned, the location of underground utilities, such as sewer, telephone, gas, water and electric lines must be determined and plainly staked. Necessary arrangements must be made with the utility company or owner for the protection, removal or relocation of the underground utilities. In such circumstances, excavation will be done in a manner that

does not endanger the field personnel engaged in the work or the underground utility. Utilities left in place will be protected by barricading, shoring, suspension or other measures, as necessary.

The use of unsafe or defective equipment is not permitted. Equipment must be inspected regularly. If found to be defective, equipment must be immediately removed from use and either repaired or replaced prior to resuming work with that equipment. Field personnel will be familiar with the location of first-aid kits and fire extinguishers. Telephone numbers for emergency assistance must be prominently posted and kept current.

Good housekeeping conditions will be observed in and around the work areas. Suitable storage places will be provided for all materials and supplies. Pipe, drill rods, etc. must be securely stacked on solid, level sills. Work surfaces, platforms, stairways, walkways, scaffolding, and access ways will be kept free of obstructions. All debris will be collected and stored in piles or containers for removal and disposal.

The area of the site to undergo intrusive activity must be walked over with the drillers and/or heavy equipment operators to identify all work locations, as well as making sure all marked utilities are seen by those doing the intrusive work.

Drilling Specific Concerns:

In areas where utilities have been identified or may be suspected, pre-drilling clearance such as hand-augering, hand excavation (with shovels or post-hole diggers), or air-knifing to a depth of at least 5' below ground surface (BGS) may be required. The Project Manager will provide guidance in those instances on what has been determined as an acceptable means of clearing drilling locations. It should be noted that if the soil lithology changes to gravel within those 5 feet, that may be an indication of a utility trench and extreme caution should be taken OR the drilling location should be offset 5 horizontal feet from the original location. Should 3 consecutive attempts be made without success to offset a particular drilling location, the field personnel should stop and contact the Project Manager for further instruction.

Special precaution must be taken when using a drill rig on a site within the vicinity of electrical power lines and other overhead utilities. Electricity can shock, burn and cause death. When overhead electrical power lines exist at or near a drilling site, all wires will be considered dangerous.

A check will be made for sagging power lines before a site is entered. Power lines will not be lifted to gain entrance. The appropriate utility company will be contacted and a request will be made that it lift or raise cut off power to the lines.

The area around the drill rig will be inspected before the drill rig mast (derrick) is raised at a site in the vicinity of power lines. The minimum distance from any point on the drill rig to the nearest power line will be determined when the mast is raised or is being raised. The mast will not be raised and the drill rig will not be operated if this distance is less than 20 feet, because hoist lines and overhead power lines can be moved toward each other by the wind.

Before the mast is raised, personnel will be cleared from the immediate area, with the exception of the operator and a helper, when necessary. A check will be made to ensure safe clearance from energized power lines or equipment (minimum 20-foot clearance). Unsecured equipment must be removed from the mast and cables, mud lines and catline ropes must be adequately secured to the mast before raising. After it is raised, the mast must be secured to the rig in an upright position with steel pins.

Excavation Specific Concerns:

For excavation work, entry into an excavated area or trench will only be allowed when:

- Shoring, sloping, and spoil pile placement is in conformance with 29 CFR 1926 Subpart P, and
- Personal protection and monitoring, as detailed in this HASP, has been implemented.

All excavation contractors are required to provide an OSHA trained and certified Competent Person. Daily inspections of excavations, the adjacent areas, and protective systems shall be made by the Competent Person for evidence of a situation that could result in a possible cave-in, indications of failure of protective systems, hazardous atmospheres, or other hazardous conditions. An inspection shall be conducted by the Competent Person prior to the start of work and as needed throughout each shift. Inspections shall also be made after every rainstorm or other hazard increasing occurrence. All inspections made by the Competent Person should be recorded in the field log book. No personnel shall perform work in a trench or excavation that contains accumulated water (any accumulated water will need to be either pumped out until the trench/excavation is dry, or the accumulated water is allowed to disperse naturally). Each employee in an excavation shall be protected from cave-ins by an adequate protective system except when excavations are made entirely in stable rock or the excavation is less than 5 feet in depth and examination by the Competent Person provides no indication of a potential cave-in. Protective systems consist of sloping or benching, use of trench boxes or other shielding mechanisms, or the use of a shoring system in accordance with the regulations.

When mobile equipment is operated adjacent to an excavation and the operators/drivers do not have a clear and direct view of the edge of the excavation, a warning system such as barricades, hand or mechanical signals, or spotters are required.

Adequate protection shall be provided to protect employees from loose rock or soil that could pose a hazard to personnel in the excavation. All temporary spoil piles shall be kept at least 2 feet away from the edge of the excavation. Spoil piles should be placed to channel rainwater or other run-off water away from the excavation.

All excavations deeper than 4 feet deep and which have the potential to have a hazardous atmosphere or oxygen deficient atmospheres (less than 19.5% oxygen) must be tested to ensure safe working conditions, prior to entry.

4.2.9 Use of Hand Tools and Portable Power Tools

Hand tools will be kept in good repair and used only for their designed purposes. Proper protective eyewear will be worn when using hand tools and portable power tools. Unguarded sharp-edged or

pointed tools will not be carried in field personnel's pockets. The use of tools with mushroomed heads, split or defective handles, worn parts, or other defects will not be permitted. Inspect all tools prior to start-up or use to identify any defects. Tools that have become unsafe will be reconditioned before reissue or they will be discarded and replaced. Throwing or dropping of tools from one level to another will not be permitted; rather, containers and hand lines will be used for transporting tools from one level to another if working at heights.

Non-sparking tools will be used in atmospheres where sources of ignition may cause fire or explosion. Electric-powered shop and hand tools will be of the double-insulated, shockproof type, or they will be effectively grounded. Power tools will be operated only by designated personnel who are familiar and trained with their use. When not in use, tools will not be left on scaffolds, ladders or overhead working surfaces.

4.2.10 Noise

Exposure to high levels of noise may occur when working near drill rigs or other heavy equipment. Also, depending upon where the work is being performed, local equipment (e.g., airports, factory machines, etc.) may produce high levels of noise. A good indication of the need for hearing protection is when verbal communication is difficult at a distance of 2-3 feet. Personnel will be provided with ear plugs and/or earmuffs when exposed to noise levels in excess of the 8-hour Permissible Exposure Limit (PEL) of 90 decibels.

4.2.11 Work Zone Traffic Control

Personnel will exercise caution when working near areas of vehicular traffic. Work zones will be identified by the use of delineators (traffic cones, flags, vehicles, DOT approved devices, temporary or permanent fencing, and/or safety barrier tape). Personnel will wear reflective vests when working in these areas. Depending on frequency, proximity, and nature of traffic, a flag person may also be utilized.

4.2.12 Work Over Water

If personnel will be working near, above or immediately adjacent to or within 6 feet of water that is 3 feet or more deep or where water presents a drowning hazard (e.g., fast-moving stream, water body with a soft bottom), employees are required to a U.S. Coast Guard (USCG) approved personal flotation device (PFD). All PFDs must have reflective tape on them to facilitate visibility. Employees must inspect PFDs daily before use for defects. Do not use defective PFDs.

4.2.13 Vehicle Use

Personnel must use caution when driving to, from, and across the site, paying special attention to other site traffic, as well as weather and road conditions. Heavy equipment should be transported during non-rush hour traffic.

4.3 Biological Hazards

Site activities on this Site may expose workers to other hazards such as poisonous plants, insects, animals, and indigenous pathogens. Protective clothing and respiratory protection equipment, and being capable of identifying poisonous plants, animals, and insects, can greatly reduce the chances of exposure. Thoroughly washing any exposed body parts, clothing, and equipment will also protect against infections. Avoiding contact with biological hazards is the best way to prevent potential adverse health effects. Recognition of potential hazards is essential. When avoidance is impractical or impossible, PPE, personal hygiene, good general health and awareness must be used to prevent adverse effects. If working in wooded/grassy areas, use appropriate insect repellants (containing DEET and/or Permethrin) and apply them per the manufacturers' directions. The following is a list of biological hazards that may be encountered while performing field activities at the project site and surrounding areas:

BIOLOGICAL HAZARD and LOCATION	CONTROL MEASURES
<p>Snakes typically are found in underbrush and tall grassy areas.</p>	<p>If you encounter a snake, stay calm and look around; there may be other snakes. Turn around and walk away on the same path you used to approach the area. If a person is bitten by a snake, wash and immobilize the injured area, keeping it lower than the heart if possible. Seek medical attention immediately. DO NOT apply ice, cut the wound or apply a tourniquet. Carry the victim or have him/her walk slowly if the victim must be moved. Try to identify the snake: note color, size, patterns and markings.</p>
<p>Poison ivy, poison oak and poison sumac typically are found in brush or wooded areas. They are more commonly found in moist areas or along the edges of wooded areas.</p>	<p>Become familiar with the identity of these plants. Wear protective clothing that covers exposed skin and clothes. Avoid contact with plants and the outside of protective clothing. If skin contacts a plant, wash the area with soap and water immediately. If the reaction is severe or worsens, seek medical attention.</p>
<p>Exposure to bloodborne pathogens may occur when rendering first aid or CPR, or when coming into contact with medical or other potentially infectious material or when coming into contact with landfill waste or waste streams containing such infectious material.</p>	<p>Training is required before a task involving potential exposure is performed. Exposure controls and personal protective equipment (PPE) area required. Hepatitis B vaccination must be offered before the person participates in a task where exposure is a possibility.</p>
<p>Bees, spiders and other stinging insects may be encountered almost anywhere and may present a serious hazard particularly to people who are allergic.</p>	<p>Watch for and avoid nests. Keep exposed skin to a minimum. Carry a kit if you have had allergic reactions in the past and inform the Project Manager and/or the buddy. If a stinger is present, remove it carefully with tweezers. Watch for allergic reaction; seek medical attention if a reaction develops.</p>
<p>Ticks typically are in wooded areas, bushes, tall grass and brush. Ticks are black, black and red or brown and can be up to one-quarter inch in size.</p>	<p>Avoid tick areas. Wear tightly woven, light-colored clothing with pants tucked into boots or socks. Spray outside of clothing with insect repellent containing permethrin. Check yourself for ticks often. If bitten, carefully remove tick with tweezers. Report the bit to the Project Manager. Look for symptoms of Lyme</p>

	disease that include a rash that looks like a bulls eye and chills, fever, headache, fatigue, stiff neck or bone pain. If symptoms appear, seek medical attention.
--	--

5.0 PERSONAL PROTECTIVE EQUIPMENT

PPE ensembles are used to protect employees and subcontractors from potential contamination hazards while conducting project field activities. Level D is expected to be used for most activities at the site. The following subsections describe the PPE requirements for the field activities.

5.1 Level D Protection

When the atmosphere contains no known hazards and work functions preclude splashes, immersions or the potential for unexpected inhalation of or contact with hazardous levels of any chemicals, Level D protection may be used. Level D does not provide respiratory protection and only provides minimal dermal protection. The Level D ensemble consists of the following:

- Work clothes that may consist of a short or long-sleeved cotton shirt and cotton pants, cotton overalls, or disposal overalls such as Tyvek™
- Steel-toe/steel-shank work boots
- Safety glasses with side shields
- Hearing protection, as necessary
- Hand protection, as appropriate
- Hard hat when working around overhead equipment such as a drilling rig
- Reflective vests when working around heavy equipment or near roadways
- Body harness and life vests when working on or within 6 feet of bulkheads, at heights, or in 3 feet or more of standing water (such as in Tin Mill Canal)

5.2 Modified Level D Protection

This is the level of protection that may be needed for material handling, sampling operations, and operation of remediation equipment when splash hazards are present. Modified Level D protection consists of the following:

- Disposable overalls such as polyethylene-coated Tyvek™
- Latex, vinyl, or nitrile inner gloves when handling liquids/fluids
- Nitrile outer gloves (taped to outer suit)
- Chemical-protective over-boots (taped to outer suit)
- Steel-toe/steel-shank, high-ankle work boots
- Hard hat with face shield
- Safety glasses with side shields or goggles
-) U
- Hearing protection, as necessary

5.3 Level C Protection

Level C protection will be used when site action levels are exceeded and respiratory protection is required. The Level C ensemble consists of Modified Level D with the following modifications:

- Half or full-face air-purifying respirator (APR) equipped with appropriate cartridges/filters
- Chemical resistant clothing such as poly-coated Tyvek™
- Inner and outer nitrile gloves
- Chemical-resistant safety boots or boot covers to go over safety boots

Upgrading or downgrading the level of protection used by EAG employees and subcontractors is a decision made by EAG based on the air monitoring protocols presented in Section 7.0 for respiratory protection, the potential for inhalation exposure to toxic chemicals, and the need for dermal protection during the activity.

5.4 First Aid, Emergency and Safety Equipment

The following first aid, emergency and safety equipment will be maintained onsite at the work area:

- A portable eye wash
- Appropriate ABC-type fire extinguishers (minimum of 10 pounds; remediation systems to house individual 20 pound extinguishers) carried in every vehicle used during field operations
- Industrial first-aid kit (one 16-unit that complies with American National Standards Institute (ANSI) Z308A for every 25 persons or less)
- Bloodborne pathogen precaution kit with CPR mouth shield
- Instant cold packs
- Soap or waterless hand cleaner and towels
- American Red Cross First Aid and CPR Instruction Manuals

6.0 PERSONNEL TRAINING AND STANDARD SAFETY PROCEDURES

Employees must have received, at the time of project assignment, a minimum of 40 hours of initial OSHA health and safety training for hazardous waste site operations. Personnel who have not met the requirements for the initial training will not be allowed in the Exclusion Zone (EZ) or Contamination Reduction Zone (CRZ) of any active work area. A copy of each subcontractor site worker's 40-hour training certificate must be sent to the Project Manager for review prior to the start of the site work.

The 8-hour refresher training course must be taken at a minimum of once per year. At the time of the job assignment, all site workers must have received 8 hours of refresher training within the past year. This course is required of all field personnel to maintain their qualifications for hazardous waste site work. A copy of each subcontractor site worker's most recent 8-hour refresher training certificate must be sent to the Project Manager for review prior to the start of the site work.

A site-specific safety orientation will be conducted by EAG for all EAG employees and subcontractors engaged in fieldwork.

6.1 Onsite Safety, Health and Emergency Response Training

The OSHA 1910.120 standard requires that site safety and health training be provided by a trained, experienced supervisor. "Trained" is defined to mean an individual that has satisfactorily completed the OSHA 40-hour Hazardous Waste Operations and Emergency Response (HAZWOPER) course and 8-hour site supervisor training. Training will be offered at the time of the initial task assignment and/or whenever new chemicals are introduced into the workplace. Training will include all applicable regulatory requirements, location of the program, inventory and MSDSs, chemicals used and their hazards (chemical, physical, and health), how to detect the presence or release of chemicals, safe work practices and methods employees can take to protect themselves from hazards, how to read MSDSs and site or project specific information on hazard warnings and labels in use at that location. All training will be documented and training certificates will be kept in the employee's permanent training file. All applicable training will also require annual refreshers.

EAG qualified personnel must also provide safety meetings.

6.2 Standard Safety Procedures

This section describes the standard safety procedures that EAG requires all onsite personnel to follow during site activities.

6.2.1 General Safety Work Practices

All onsite employees and subcontractors will observe the following general safety work practices:

- Health and safety tailgate briefings will occur to introduce new activities, any new safety issues, and emergency egress routes for work areas; any significant change (added personnel, change in scope, or change in field conditions) will trigger a second (or more) tailgate meeting to address whatever change occurred
- No food, drink, or tobacco products will be allowed in the Exclusion and Contamination Reduction Zones
- Loose clothing, hair, and/or jewelry will not be permitted around moving or rotating equipment
- The "buddy system" will be implemented as necessary whereby a pair of co-workers watches out for each other while in proximity of potential physical work hazards
- Good housekeeping of all work areas will be maintained on an ongoing basis

6.2.2 Hand Safety

This standard is intended to protect employees from activities that may expose them to injury. This standard provides information on recognizing those conditions that require personal protective equipment (PPE) or specific work practices to reduce the risk of hand injury.

Appropriate gloves must be worn when persons work with materials or equipment that presents the potential for hand injury due to sharp edges, corrosives, flammable and irritating materials, extreme temperatures, splinters, etc.

Guidelines for Working With and Around Equipment (Hand Tools, Portable Powered Equipment):

- Employees should be trained in the use of all tools.
- Keep hand and power tools in good repair and use them only for the task for which they were designed.

- Inspect tools before use and remove damaged or defective tools from service.
- Operate tools in accordance with manufacturer's instructions.
- Do not remove or bypass a guarding device for any reason.
- Keep surfaces and handles clean and free of excess oil to prevent slipping.
- Wear proper PPE, including gloves, as necessary.
- Do not carry sharp tools in pockets.
- Clean tools and return to the toolbox or storage area upon completion of a job.
- Before applying pressure, ensure that wrenches have a good bite.
- Brace yourself by placing your body in the proper position so you will not fall if the tool slips.
- Make sure hands and fingers have sufficient clearance in the event the tool slips.
- Always pull on a wrench, never push.
- When working with tools overhead, place tools in a holding receptacle when not in use.
- Do not throw tools from place to place or from person to person, or drop tools from heights.
- Inspect all tools prior to start-up or use to identify any defects.
- Powered hand tools should not be capable of being locked in the ON position.
- Require that all power-fastening devices be equipped with a safety interlock capable of activation only when in contact with the work surface.
- Do not allow loose clothing, long hair, loose jewelry, rings, and chains to be worn while working with power tools.
- Do not use cheater pipes.
- Make provisions to prevent machines from restarting through proper lockout/tagout.

Guidelines for using Cutting Tools:

- Always use the specific tool for the task. Tubing cutters, snips, self-retracting knives, concealed blade cutters, and related tools are task specific and minimize the risk of hand injury. For more information about cutting tools, see Supplemental Information A.
- Fixed open-blade knives (FOBK) are prohibited from use. Examples of fixed open-blade knives include pocket knives, multitools, hunting knives, and standard utility knives.
- When utilizing cutting tools, personnel will observe the following precautions to the fullest extent possible:
 - Use the correct tool and correct size tool for the job.
 - Cut in a direction away from yourself and not toward other workers in the area.
 - Maintain the noncutting hand and arm toward the body and out of the direction of the cutting tool if it were to slip out of the material being cut.
 - Ensure that the tool is sharp and clean; dirty and dull tools typically cause poor cuts and more hazard than a sharp, clean cutting tool.
 - Store these tools correctly with covers in place or blades retracted, as provided by the manufacturer.
 - On tasks where cutting may be very frequent or last all day (e.g., liner samples), consider Kevlar® gloves in the PPE evaluation for the project.
 - Do not remove guards on paper cutters.

6.2.3 Respiratory Protection

Based on air monitoring, an upgrade to Level C protection may be indicated. Half or full-face APRs will be utilized for protection against organic vapors and particulates. All employees required to wear respirators will be need to be medically cleared, in writing to do so by a qualified Occupational Physician.

All respirator users must be trained before they are assigned a respirator, annually thereafter, whenever a new hazard or job is introduces and whenever employees fail to demonstrate proper use or knowledge. Training will include, at a minimum:

- Why the respirator is necessary and what conditions can make the respirator ineffective.
- What limitation and capabilities of the respirators area.
- How to inspect, put on and remove and check the seals of the respirator.
- What respirator maintenance and storage procedures are.
- How to recognize medicals signs and symptoms that may limit or prevent effective use of the respirator.
- The engineering and administrative controls being used and the need for respirators.
- The hazards and consequences of improper respirator use.
- How to recognize and handle emergency situations.

Training will be documented and training certificated will be kept in the employee's permanent training file.

6.2.4 Personal Hygiene Practices

The field team must pay strict attention to sanitation and personal hygiene requirements to avoid personal contamination. The following instructions will be discussed and must be followed:

- During field activities, never put anything in the mouth, including fingers
- All employees must wash their hands, forearms, face, and neck before eating drinking, smoking or using the restroom
- Smoking is prohibited except in designated areas outside the work zone
- At the end of the day, all employees will shower upon returning home or to their hotel

6.2.5 Electrical Safety

All extension cords used onsite must be heavy-duty variety and must be properly grounded. All temporary circuitry must incorporate the use of GFCI devices. Refer to electrical safety in Section 4.2.6, Electrical Hazards.

6.2.6 Fire Safety

All flammable liquids will be used only for their intended purpose and stored and handled only in approved containers. Portable containers must be the approved red safety containers equipped with flame arresters and self-closing lids. All transfers of flammable liquids must be made with the containers grounded or bonded. Also, gasoline containers will be clearly labeled and storage areas (if

applicable) will be posted with “No Smoking” signs. Fire extinguishers will be stalled in all areas that contain flammable liquids.

6.2.7 Illumination

All work is planned for daylight hours. No special requirements are anticipated. However, should any work take place outdoors after daylight hours, suitable lighting will be required. In addition, suitable lighting is to be provided in each remediation system building or enclosure.

6.2.8 Sanitation

Potable water and toilet facilities will be provided in compliance with the OSHA 1926.51 standard. Any container used to distribute drinking water shall be clearly marked and not used for any other purpose. Single drinking cups will be supplied, both a sanitary container for the unused cups and a receptacle for disposed of the used cups will also be provided. Port-a-johns will be provided since there are no sanitary sewers on the job site.

7.0 EXPOSURE MONITORING PLAN

This section describes air and personnel monitoring protocols, sampling methods, and instrumentation to be used, as well as the methods and frequency of sampling instrument calibration and action levels for potential work site hazards. When engaged in air monitoring, EAG personnel and subcontractors must use the forms to record air monitoring data and air monitoring instrument calibration records. All monitoring records/forms are to be maintained in the project file by the EAG Project Manager.

7.1 Air Monitoring

The surveillance program is established to detect changes in the ambient air at the work site and to ensure the continuing safety of the work zones and adequacy of the level of worker protection. During field activities, the designated field team member will monitor the work site for combustible gas concentrations and organic vapors. Calibration of all monitoring equipment will be performed in accordance with the manufacturers’ procedures by trained EAG employees and subcontractors. The Project Manager, Project Field Team Leader or representative will be notified immediately of any contaminant levels that could trigger an upgrade in PPE or cause a suspension of site activities.

- One or more of the following direct-reading instruments may be used to aid in this determination. Photoionization Detectors (PID) and Flame Ionization Detectors (FID) will measure non-specific organic gases and vapors. Combustible Gas Indicators (CGI) will detect explosive atmospheres. Oxygen (O₂) meters will detect fluctuations in oxygen concentrations. These instruments should be calibrated or bump tested daily and whenever the readings may be erratic. All readings should be recorded in the field log books.

Air monitoring results obtained from the breathing zone during field activities will be recorded in field log books. All such records will also include the location, date/time, weather conditions, person monitored, background concentration, and identification of specific contaminant whenever possible. Air monitoring information will be utilized to evaluate personnel exposure and assess the appropriateness of PPE for Site conditions.

7.1.1 Combustible Gas and Oxygen Deficiency/Excess Monitoring

Explosive gas concentrations are not expected to exceed 10% of the lower explosive level (LEL). Should the need be indicated for monitoring, action guidance for the CGI/O2 meter responses is contained in **Table 7-1**.

Table 7-1

CGI/Oxygen Meter Action Levels	
Meter Response	Action
CGI response 0%-10% LEL	Continue normal operations
CGI initial response >10% and <20% LEL	Eliminate all sources of ignition from the work area; temporarily retreat from work area for 15-30 minutes and then monitor area again
CGI response after 15-30 minute retreat >10% and <20% LEL	Retreat from work area; notify Project Manager
CGI response >20%	Discontinue operations; retreat from work area
Oxygen level <19.5%	Retreat from work area; notify Project Manager
Oxygen level >23.5%	Retreat from work area; notify Project Manager

7.1.2 Organic Vapor Concentrations

Real-time monitoring for organic vapor concentrations in the breathing zone and down hole will be conducted during field operations (installation of groundwater monitoring and groundwater sampling by EAG and EAG subcontractor personnel) with a PID equipped with a 10.2- or 11.7-electron volt (eV) probe. The PID will be taken into the field and operated during site activities where contaminated soil and/or groundwater may be present. Air monitoring will be conducted during well installation and when a well is opened for groundwater measurements. Measurements will be made at the well head and personnel breathing zones where activities are being performed. The instrument will be calibrated using ultra-high purity air and isobutylene vapor of known concentration before and after use each day. Air calibration measurements will be documented in writing and kept in the project file. Action guidance for PID responses is contained in **Table 7-2**.

Table 7-2

Action Levels for General Site Work	
Meter Response in Breathing Zone (minimum of 3 minutes)	Action Required
<5ppm above background	Use Level D PPE
>5ppm above background	Level C PPE, including half or full-face APR with organic vapor cartridges/P100 filters
>50ppm above background	Stop work
Action Levels for Handling NAPL	
Meter Response in Breathing Zone (minimum of 3 minutes)	Action Required
<1ppm above background	Use Modified Level D PPE
>1ppm to <10ppm	Level C PPE, including half or full-face APR with organic vapor cartridges
>10ppm above background	Immediately withdraw; monitoring will continue until action levels will allow safe re-entry

If air concentrations of organic vapors are greater than 5 ppm above background in the breathing zone for a 3-minute period, personnel will stop work, retreat from site, and allow time (at least 15 minutes) for vapors to dissipate. If monitoring indicates that concentrations still exceed 5 ppm, workers will upgrade to Level C PPE. If monitoring indicates that concentrations exceed 50 ppm, work will be stopped until site conditions can be re-evaluated.

These action levels are based on the assumption that the major component of free product being recovered will be benzene or naphthalene.

Work involving NAPL recovery from monitoring wells will be conducted in Level C PPE. This level may be downgraded based on air monitoring data and actual field conditions. Downgrading of PPE must be approved by the PM and HSE staff. If ventilation is conducted, additional air monitoring will be performed to the resumption of work to determine the level of PPE required.

7.2 Physical Conditions Monitoring

Site workers will be monitored by the Project Manager for signs of weather-related symptoms from exposure to excessive heat or cold.

Whenever the air temperature exceeds 70°F for personnel wearing chemical protective clothing or 90°F for personnel wearing regular work clothes, the Project Manager will assess conditions that may cause heat stress in site workers.

8.0 MEDICAL SURVEILLANCE

This section discusses the medical surveillance program, how the results are reviewed by a physician and how participation is documented.

8.1 Medical Surveillance Program

All personnel who will be performing any task where potential exposure to hazardous material exists will undergo medical surveillance as outlined in OSHA 29 CFR 1910.120(f). All personnel performing tasks in the Exclusion Zone or Contamination Reduction Zone will be required to have passed the EAG medical surveillance examination (or equivalent), performed by a licensed Occupational Physician. The Project Manager will verify that all EAG and subcontractor personnel meet applicable OSHA medical surveillance requirements.

Applicable field employees will undergo an annual comprehensive medical examination, including a comprehensive health history, blood chemistry with complete blood count and differential, urinalysis, medical history, required chest x-rays, audiogram, pulmonary function testing, testing for heavy metals (as needed), and a physician's interpretation of each employee's medical surveillance examination, including the ability of the employee to wear a respirator. A comprehensive medical examination will be performed if an employee develops signs or symptoms indicating possible overexposure to hazardous substances and/or heat or cold stress.

8.2 Physician Review

All medical surveillance and examination results are reviewed by a licensed physician who is certified in Occupational Medicine by the American Board of Preventive Medicine. EAG employee participation in the medical surveillance program is a part of their permanent medical record maintained in the employee's home office. A copy of the current medical clearance signed by the occupational health physician for all EAG employees must be maintained at the home office.

9.0 SITE CONTROL MEASURES AND DECONTAMINATION

To provide for the protection of public health and safety and minimize the possibility of transferring hazardous substances from the site, contamination control procedures are required. These procedures consist of site control measures (which entail the delineation of work zones, communications, and site security) and decontamination procedures (which are necessary for both personnel and equipment). Contaminants that may be uncovered during sampling operations must not be transferred outside the work zone unless properly containerized, and must be removed from clothing, personnel, and equipment prior to relocation from that zone. This section discusses site control measures and decontamination procedures to be used during the collection of samples, the installation of soil borings and/or groundwater monitoring/remediation wells, excavations, and other intrusive work where contact with impacted soils and groundwater could occur by EAG and/or EAG subcontractor personnel.

9.1 Site Control Measures

Site control can be achieved by effectively delineating the work zone, providing appropriate communication, and establishing site security.

9.1.1 Work Zone Delineation

To minimize the transfer of hazardous substances from the site and to ensure proper protection of employees and subcontractors, work zones will be established by the Field Project Team Leader. Applicable site work and the associated requirement for work zones will be determined by the Project Manager. The work area will be divided into an Exclusion Zone (EZ), a Contamination Reduction Zone (CRZ), and a Support Zone (SZ). A typical work zone delineation setup is shown as **Figure 9-1**, below.

Exclusion Zone (EZ)

Contamination does or could exist in this zone. Only properly authorized and trained individuals (refer to Section 6.0) wearing appropriate PPE will be allowed to enter and work in this zone. All people entering the EZ must wear, at a minimum, Level D protection. An entry and exit point for personnel and equipment will be established at the periphery of the EZ (between the EZ and the CRZ) to regulate the flow of personnel and equipment.

Contamination Reduction Zone (CRZ)


Between the EZ and the SZ will be the CRZ, which will provide a transition between the potentially contaminated EZ and the clean SZ. The CRZ (located upwind of the EZ, if possible) will be a corridor leading from the EZ and will serve as a buffer to further reduce the probability of the SZ becoming contaminated. Exit from the EZ will only be allowed through this CRZ. The CRZ will provide additional assurance that the physical transfer of contaminating substances on people, equipment, and/or in the air will be limited through a combination of decontamination and zone restrictions. Within this zone, employees and subcontractors may perform personal decontamination (e.g., face and hand washing), and certain PPE and small equipment decontamination. Buckets or wash basins for boot

washing and equipment decontamination will be stationed on a sheet of plastic (a minimum of 8 feet by 8 feet), the boundaries of which will constitute the CRZ.

Support Zone (SZ)

The Support Zone will be considered a non-contaminated area. The location of support facilities in the SZ will be upwind of the EZ (where possible) and readily accessible to the nearest road. The field office/support facilities, equipment vehicles, a first aid station and a visitors/personnel entry and exit log for the work site will be located in this zone. Potentially contaminated personal clothing, equipment and samples are not permitted in this zone unless properly containerized.

**Figure 9-1
Typical Exclusion, Contamination Reduction, and Support Zone setups**

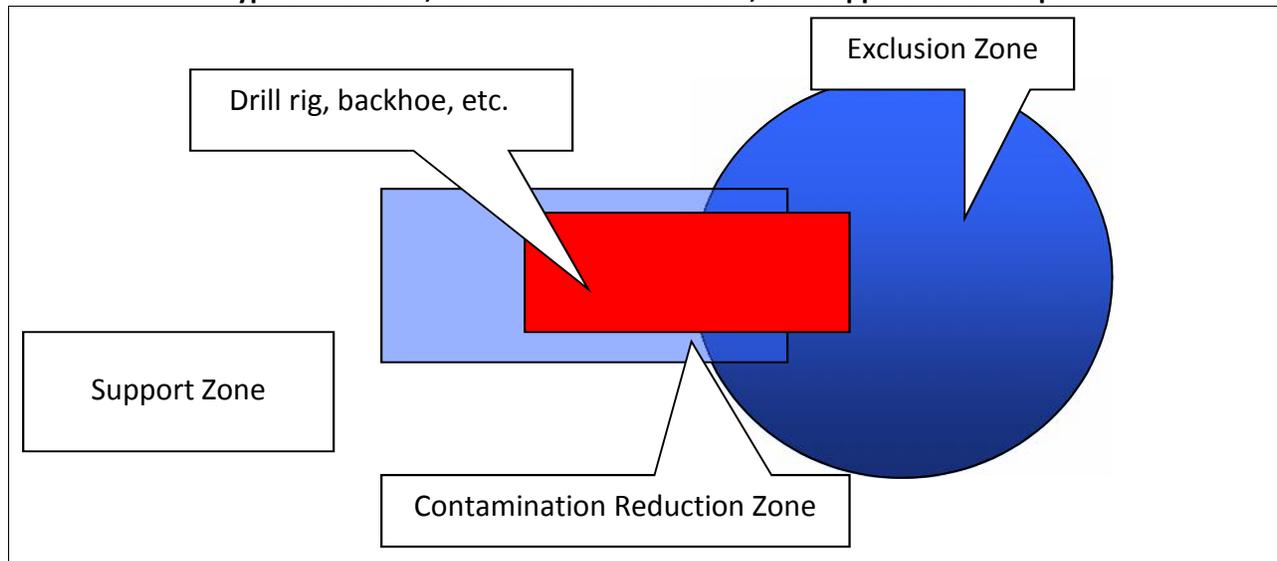

9.1.2 Communications

A loud and clear form of communication should be made available for Site personnel entering the work zones. Site communication may be in the form of hand signals, voice, or other communication devices. All forms of communication should be understood by all workers on the Site prior to starting work. Offsite communications may be conducted with mobile phones or walkie-talkies only if the atmosphere has been deemed non-explosive, and the person using the mobile device is in the SZ while placing the call, or inside the cab of a stationary vehicle.

9.1.3 Site Security

The Sparrows Point facility is not open to the public, and there is a strictly monitored main entrance with a security guard on duty at all times who only allows authorized personnel onto the Site. This limited access to the facility should eliminate the need for many requirements for specific site security except those needed to maintain work zone integrity, such as visible barriers around open excavations or EZs and CRZs. No site visitors will be allowed to travel unescorted by EAG or subcontractor personnel around the facility.

Once site visitors arrive at their intended work zone, they must check in with the Field Team Lead. If visitors are authorized to enter the CRZ and/or the EZ, they must have completed OSHA 1910.120 medical surveillance and training requirements (refer to Section 8.0 and Section 6.0). Visitors must wear

appropriate PPE before they will be allowed to enter the CRZ and/or the EZ. They must also be taken through this HASP during a brief tail-gate meeting and sign the Acknowledgement page in the back prior to engaging in any activities inside the CRZ or the EZ. All site visitors must follow the same site control measures and decontamination procedures as EAG personnel and subcontractors. The Project Manager must also be informed of each visitor's name, purpose for their visit, time of entry (and exit), location of tasks they wish to perform, whether they completed their intended task(s), and any other relevant information pertaining to their visit.

9.2 Decontamination Procedures

Decontamination of employees, subcontractors, and equipment leaving the EZ will be performed to minimize human exposure to hazardous substances and to minimize the spread of contamination to surrounding areas. The purpose of the CRZ is to provide a location to perform limited personnel decontamination and certain PPE and small equipment decontamination.

9.2.1 Personnel Decontamination

Persons leaving the EZ must pass through the CRZ and follow decontamination procedures before entering the SZ. Hand tools and other sampling equipment used in the EZ and reusable PPE (boots, safety glasses, etc.) will be appropriately cleaned prior to removal from the site each day. The step-by-step sequence for personnel decontamination is as follows:

- Remove boot covers (if used) at the boot washing station and place them in the disposal container provided
- Wash outer gloves and chemical resistant boots (if used) at the boot washing station
- Remove wrist tape (if used) and outer gloves and place them in the disposal container provided
- Remove ankle tape (if used) and disposable coveralls (if used) and place them in the disposal container provided
- Remove respirators (if used) and place each in designated locations in the CRZ
- Remove inner gloves and discard in the disposal container provided
- Wash hands and face and proceed to the SZ

Respirators must be fully decontaminated after each use by the personnel who previously wore them. All project employees and subcontractors are required to take a thorough soap and water shower in their home or motel room at the end of each workday. If monitoring or a general exposure assessment indicates that an employee has become contaminated, the employee or subcontractor will notify the EAG Project Manager and the Field Team Lead as soon as the contaminated state has been discovered.

9.2.2 Equipment Decontamination

All equipment leaving the EZ must be decontaminated either within the CRZ or at the central decontamination area. Small equipment, such as hand tools, will be thoroughly decontaminated within the CRZ before being placed in the SZ. The field tools may be scrubbed visually clean using a detergent solution (Alconox/Liquinox) with water and a stiff, long-bristled scrub brush. Following the solution scrubbing, the tools may be rinsed with distilled water or isopropyl alcohol. Any vehicle working in an EZ will be decontaminated before leaving the site. The vehicle will be cleaned by sweeping excess soil and debris off the wheels. A high-pressure sprayer will then be used to wash the wheels, if necessary.

Each piece of equipment will be inspected after cleaning for any soil remaining on the tires or elsewhere. All vehicles will be cleaned to the satisfaction of the Field Team Lead or a designated assistant prior to entering the SZ or leaving the site. Employees or subcontractors performing decontamination shall wear the appropriate level of PPE (refer to Section 5.0).

9.2.3 Waste Management

The Project Manager and the Field Team Leads will be responsible for overseeing the containerization and disposal of any field derived wastes. Contaminated or suspected contaminated field derived wastes shall be disposed of in accordance with all local, state, and/or federal regulations. Field derived wastes include decontamination rinse waters and other related decontamination generated wastes.

Soils and groundwater expected to be encountered during any sampling or intrusive work not to be contaminated, based on existing data, may be discharged to the ground surface in the immediate vicinity of the monitoring well. However, any known or suspected to be contaminated soil (in small quantities) or groundwater will be containerized for future removal, likely in 55-gallon drums or other approved storage vessels. Depending on the suspected contaminants, the recovered groundwater may be sent through one of the onsite groundwater treatment units. However, the treatment unit must be designed to address the contaminants of concern in the groundwater being treated. Otherwise, the liquid must be staged onsite for eventual offsite disposal at an approved facility.

Impacted soil, if in drums, will be staged in an area designated by the Project Manager or Field Team Lead for eventual disposal. For large excavations, where excavated soil is stockpiled, it may be necessary to place soils on plastic and cover with plastic to prevent any potential leachable runoff. The Project Manager and/or Field Team Lead will provide the proper guidance necessary for handling bulk soil piles.

Any NAPL recovered via remediation systems or manual recovery efforts will be properly containerized and either disposed of offsite as a recyclable material, if possible, or as a hazardous waste. The receiving facility must be an approved facility.

10.0 EMERGENCY RESPONSE AND CONTINGENCY PROCEDURES

The objective of emergency response and contingency procedures is to ensure that effective actions are implemented in a timely manner to minimize or control the effects of adverse events (e.g., potential chemical exposures, personal injuries, fires/explosions, and spills/releases). The following subsections describe the basic emergency responses required should an emergency take place during field investigation or remedial effort activities.

10.1 Emergency Phone Numbers

Emergency telephone numbers are listed in **Table 10-1**.

**Table 10-1
Emergency Telephone Numbers and Agencies**

Agency	Telephone Number
Security (Sparrows Point facility)	(410) 388-7761
Ambulance	911
Fire	911
Occupational Health Clinic	(410) 633-3600
Hospital	(410) 550-0100 (general) (410) 550-0350 (emergency)
National Response Center	(800) 424-8802
Poison Control Center - Maryland	(800) 222-1222
EAG Main Contact	
VP Remediation, Russ Becker	(314) 686-5611
Project Manager, James Calenda	(314) 620-3056

10.2 Injury/Illness Treatment

In the event of illness or injury, the following steps will be taken:

- Evaluate the extent of injuries or seriousness of illness.
- When employees require urgent medical attention, call for emergency assistance. First aid should be administered while awaiting an ambulance or paramedics. All emergency medical treatment, other than first aid, will be administered by the local paramedics. **Table 10-1** lists site emergency telephone numbers. In all cases, critical injuries must be immediately referred for professional medical attention.
- For a non-critical injury/illness, first aid will be administered by onsite personnel. Anyone sustaining a non-critical injury/illness who continues to work will be monitored by the Field Team Lead for any signs of worsening condition, if it is deemed that the person can return to work by the Team Lead and Project Manager. Injured personnel who later suffer any worsening change in status are to immediately notify the Team Lead or the Project Manager.

10.3 Occupational Health Clinic and Hospital Information

Occupational Health Clinic

The Concentra Medical Center, located at 1833 Portal Street, Baltimore, MD, is the closest occupational health clinic, just over 6 miles away. A map to the clinic is included as **Figure 10-1**. The clinic should be used for non-emergency injuries and illnesses.

Directions:

From Sparrow's Point Road, turn left onto Wharf Road;
Turn left onto MD-158 W/Bethlehem Blvd. (0.4 mile);
Turn right onto MD-157 N/Peninsula Expy. (2.7 miles);
Turn slight left onto Merritt Ave. (0.1 mile);
Merritt Ave. becomes Sollers Point Rd. (0.3 mile);
Turn left to stay on Sollers Point Rd (0.6 mile);
Turn left onto Williams Ave. (0.2 mile);
Turn right onto Dundalk Ave. (<0.1 miles);
Turn left onto Chandlery St. (0.1 mile);
Turn left onto Portal St.

Figure 10-1: Health Clinic (Non-Emergency) Map



Hospital

The Johns Hopkins Bayview Hospital is the closest emergency facility, just over 9 miles away. The hospital is located at 4940 Eastern Avenue in Baltimore, MD. **Figure 10-2** is a map to this hospital. Maps are also included in **Attachment E**.

Directions:

From the Sparrows Point Industrial Complex, go north on Route 151 for approximately one mile.


Take ramp (right) onto I-695 towards I-695/Essex.

At exit 40, take ramp (right) onto Route 151/North Point Boulevard North/MD 150;

Take ramp (right) onto Route 150 (Eastern Avenue).

Continue on Eastern Avenue to hospital on right.

Figure 10-2: Hospital Map

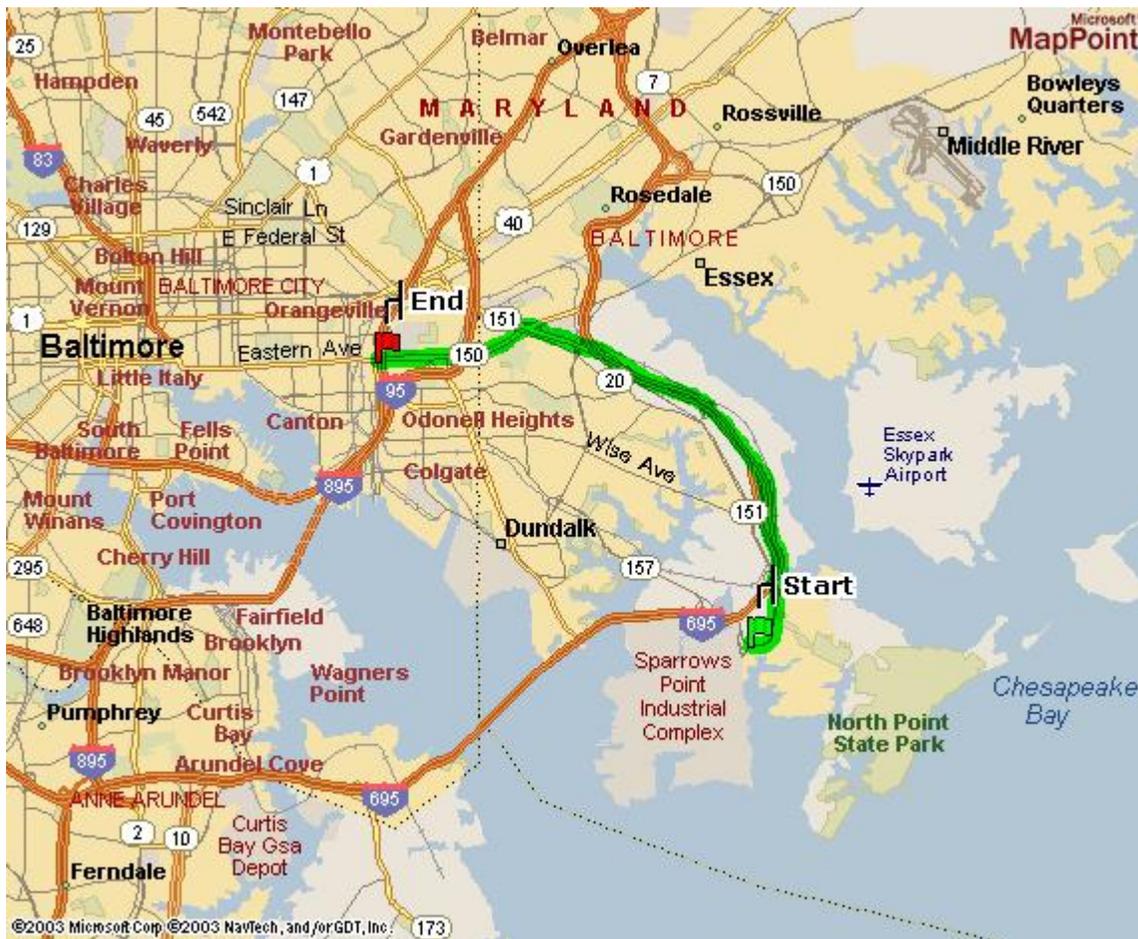

Prior to the start of field activities, the Project Field Team Leader will call to verify the telephone numbers and directions for the clinic and hospital, and then distribute location maps and the emergency telephone list to workers and vehicles.

10.4 Accident and Emergency Medical Response

All field team members will be aware of the location of a first aid kit kept onsite. All vehicles used to transport injured persons to an offsite medical facility will be provided with directions and a map to the medical facility.

If treatment beyond first aid is required, emergency response personnel will be contacted for assistance and transport. Before beginning site activities, the Project Field Team Leader will ensure that each field team member knows where the nearest emergency medical facilities are and how to get there. The closest hospital will be used in cases of life-threatening emergencies at the direction of the Project Field Team Leader. The telephone numbers of the local emergency services will be available in the SZ, and the Project Field Team Leader will brief the field team on the procedures for calling for help in an emergency.

Site personnel will inform the Project Manager of any medications, allergies, or other medical information that may be applicable for their medical treatment. The Project Manager will supply this information to emergency response personnel, and will accompany the victim to the hospital, if possible.

10.4.1 Chemical Exposure

In case of accidental overexposure to a hazardous material (groundwater, soil, and/or off-gas materials), guidelines shown in **Table 10-2** will be used.

Table 10-2
Chemical Exposure Guidelines

Type of Overexposure	First Aid Guidelines
Skin Contact	Skin: Wash/rinse the affected area thoroughly with copious amounts of soap and water.
	Eyes: Eyes should be rinsed for at least 15 minutes following chemical contamination.
	Contact emergency response personnel if required, or transport victim to the hospital.
Inhalation	Move the victim to fresh air.
	Contact emergency response personnel if required, or transport victim to the hospital.
Ingestion	Contact Poison Control Center.
	Contact emergency response personnel, or transport victim to the hospital.

10.4.2 Decontamination During a Medical Emergency

For minor medical problems or injuries, regular decontamination procedures will be followed. If emergency, life-saving first aid and/or medical treatment are required, regular decontamination procedures may need to be abbreviated or omitted:

- Do not attempt to wash or rinse an unresponsive victim unless the victim has been contaminated with an extremely toxic or corrosive chemical that may cause injury or loss of life to emergency response personnel.
- Outer garments can be removed if it does not cause a delay, interfere with treatment, or aggravate the problem.

- PPE can be cut away and respiratory protective equipment must always be removed.
- If contaminated clothing cannot be safely removed, then the victim should be wrapped in a blanket or plastic sheeting to prevent contamination to the inside of the ambulance and/or emergency response personnel.

The Project Manager or Field Team Lead will advise the medical staff as to the type of contamination possibly involved.

10.4.3 Small or Incipient Fire

A small fire is defined as a fire that can be extinguished with an available 20 pound type ABC fire extinguisher. An incipient fire is a fire that is small because it has just started. In the event of a small or incipient fire, the following minimum actions will be taken:

- Evacuate nearby personnel from the area, if possible, to an upwind location or to an area not affected by smoke or hazardous decomposition products if an upwind location is not feasible.
- Attempt to extinguish fire using portable fire extinguisher or by smothering.
- Contact emergency response personnel, as needed, for any injuries or exposures to hazardous decomposition products, or if fire cannot be put out.
- After the fire has been extinguished, or emergency response personnel have been contacted, notify the following project personnel:

The Project Manager

10.4.4 Large Fire or Explosion

An explosion, large fire or a small fire which cannot be extinguished is beyond the first line capabilities of EAG personnel. Professional emergency response personnel would be needed to provide emergency assistance for these types of incidents. In the event of a large fire, explosion or a small fire that cannot be extinguished, the following minimum actions will be taken:

- Evacuate all personnel from the site, if possible, to an upwind location, or to an area not affected by smoke or hazardous decomposition products if an upwind location is not feasible
- Perform a quick role call to account for all site personnel
- Contact the fire department
- Contact emergency response personnel, as needed, for any injuries or exposures to hazardous decomposition products
- After emergency response personnel have been contacted, notify the following project personnel:

The Project Manager

10.4.5 Adverse Weather Conditions

In the event of adverse weather conditions, the Project Manager will determine if work can continue without sacrificing the health and safety of site personnel. Threatening weather conditions will be monitored by the Project Manager and possibly the Team Lead via radio, television, internet, and/ or calls to the National Weather Service. Some of the conditions to be considered include:

- Potential for heat or cold stress
- Limited visibility

- Electrical storms
- Treacherous weather-related working conditions (i.e., heavy rainfall, icy conditions causing slippery footing hazards, etc.).

10.4.6 First Aid for Heat Stress/Cold Stress

First aid treatment for **heat cramps** includes shade, rest and fluid replacement. If available, the individual should drink electrolyte replacement fluids (e.g., Gatorade, Squincher or 10-K). The individual should recover within half an hour.

First aid treatment for **heat exhaustion** includes cooling the victim, elevating the feet and fluid replacement. If the individual has not recovered within half an hour, then transport the victim to the hospital for medical attention.

Heat stroke is a medical emergency, requiring the immediate cooling of the victim and transport to the hospital for medical treatment immediately.

First aid treatment for **frost nip** and **frostbite** includes covering the affected area with warmth and retreating to a warm area. If the individual has not recovered within half an hour, then transport the victim to the hospital for medical attention.

Frozen tissue is a medical emergency and the victim must receive medical attention immediately. Contact emergency response personnel immediately or transport the victim to the hospital.

First aid treatment of **mild hypothermia** includes using heat to raise the individual's body temperature. Heat may be applied to the victim in the form of heat packs, hot water bottles and blankets. If the individual has not recovered within half an hour, then transport the victim to the hospital for medical attention.

Severe hypothermia is a medical emergency and the victim must be transported to the hospital immediately. First aid treatment for severe hypothermia includes handling the victim very gently; rough handling may set off of an irregular heartbeat. **DO NOT** attempt to re-warm the severely hypothermic victim; re-warming may cause the development of an irregular heartbeat.

10.4.7 Snake Bites

If bitten, lower the extremity below the heart to reduce the poison's dissemination through the body. Remain calm, try to keep the heart rate reduced and seek medical attention immediately. Do not cut the wound or attempt to suck out the venom. Note any physical features (e.g., shape of head and color or pattern on body) of the snake.

10.4.8 Animal Bites

All bites should be treated as contaminated soft tissue injuries. Bites should be washed immediately with large amounts of soap and water. If soap is not available, flush the wound with water. The severity and onset of any infection is dependent upon the number of organisms (viruses or bacteria) introduced into the wound. Washing saliva out of the wound immediately will reduce the number of bacteria or viruses that can enter the tissue. Medical attention must be sought if rabies is suspected or the individual has not had a recent tetanus booster.

10.4.9 Insect Bites and Stings

Emergency care for insect bites and stings depends on the individual's reaction. To treat a sting that results in a minor reaction, remove the stinger by gently scraping it off the skin. Do not try to grasp the sac or stinger, because this forces the remaining venom into the skin. Once the stinger has been removed, clean the wound and surrounding area. Apply cold packs to slow the absorption of the venom and reduce pain and swelling. The treatment for a severe reaction to insect stings includes the following:

- Confirm with the victim whether they are highly allergic to the insect that stung them
 - If victim has gone into anaphylactic shock, retrieve their epi pen or other auto-injector and administer per the directions as hastily as possible
- Assuming the victim remains conscious, ask them to refrain from moving around, and to lie down
- Immobilize the injured area immediately
- If an extremity is involved, remove any rings or watch
- Keep the affected part low, below the level of the heart
- Apply cold compresses to the affected area
- If possible, try to identify the type of insect that inflicted the sting
- Transport the victim to a medical facility immediately, continuing supportive measures en route.

All employees and subcontractors must report severe reactions to insect stings prior to the beginning of work to both the Project Manager and Field Team Lead.

10.4.10 Poisonous Plants

Decontamination: Wash the skin immediately after contact with the plant. Proper washing may not be practical in the middle of the woods, but a product such as Technu or a small wash-up kit with prepackaged, alcohol-based cleansing tissues can be effective. Employees and subcontractors should not forget to wash contaminated clothing and clean up contaminated equipment prior to re-use.

Treatment: Options are as follows:

- Home treatment: Calamine lotion and an oatmeal bath (one cup to a tub full of water) can help relieve itching. To prevent secondary skin infection, scratching is not helpful and the fingernails should be cut to avoid damage to the skin. Over-the-counter hydrocortisone cream can decrease inflammation and itching; however, the label should be read and the cream used according to directions.
- When to see the doctor: Severe cases may require further treatment. A physician should be seen if the rash appears infected, is on the face or other sensitive body areas, or is too extensive to be easily treated at home.


10.4.11 Ticks

To remove an attached tick:

- Use fine-tipped tweezers or a "tick tool" to grasp the tick at the surface of the skin
- If tweezers are not available, use a tissue to protect the fingers (exposure to the tick's body fluid may lead to transmission of disease)
- With a steady motion, pull the tick straight out

Disinfect the bite site and the tweezers. Wash your hands thoroughly with soap and water. Save the tick if you can by placing it in a Ziploc bag in the freezer; this may help with diagnosis in the future.

If flu-like symptoms such as fatigue, headache, neck-stiffness or jaw discomfort begin following a tick bite, seek medical attention.



APPENDICES



Environmental Engineers

ATTACHMENT A
COMPLIANCE AGREEMENT

EAG HEALTH AND SAFETY PLAN

ACKNOWLEDGEMENT FORM

I, _____, have read (or had read to me), EAG's health and safety plan.
(Print Name)

I understand my responsibilities as they are defined in this plan and will abide by these rules and procedures, as well as any regulations or otherwise governing safety. When in doubt concerning safe job performance, I will speak to my immediate supervisor and/or Project Manager.

I understand EAG reserves the right to change or amend the HASP at any time.

I understand any violation to the plan policies or procedures will be cause for disciplinary action up to and including termination.

Employee Signature

Date

EAG Supervisor/Project Manager Signature

Date

ATTACHMENT B

Material Safety Data Sheets (MSDSs)
